

From: Byers, Harris <Harris.Byers@stantec.com>
Sent: Friday, April 28, 2023 8:51 AM
To: Beggs, Tauren R - DNR; Adam Tegen
Subject: Summary of River Point District
Attachments: Figure 2 - Previous SAG Projects.pdf; River Point District Summary.xlsx

Tauren:

For our call later today, attached is a spreadsheet summarizing work within each project area at River Point. Also attached is a figure illustrating the project areas for reference.

Look forward to catching up soon.

Sincerely,

Harris Byers, Ph.D.

Sr. Brownfields Project Manager
Contaminant Hydrogeologist / Urban Geochemist

Direct: 414 581-6476
Harris.Byers@stantec.com

Stantec
12080 Corporate Parkway Suite 200
Mequon WI 53092-2649



The content of this email is the confidential property of Stantec and should not be copied, modified, retransmitted, or used for any purpose except with Stantec's written authorization. If you are not the intended recipient, please delete all copies and notify us immediately.

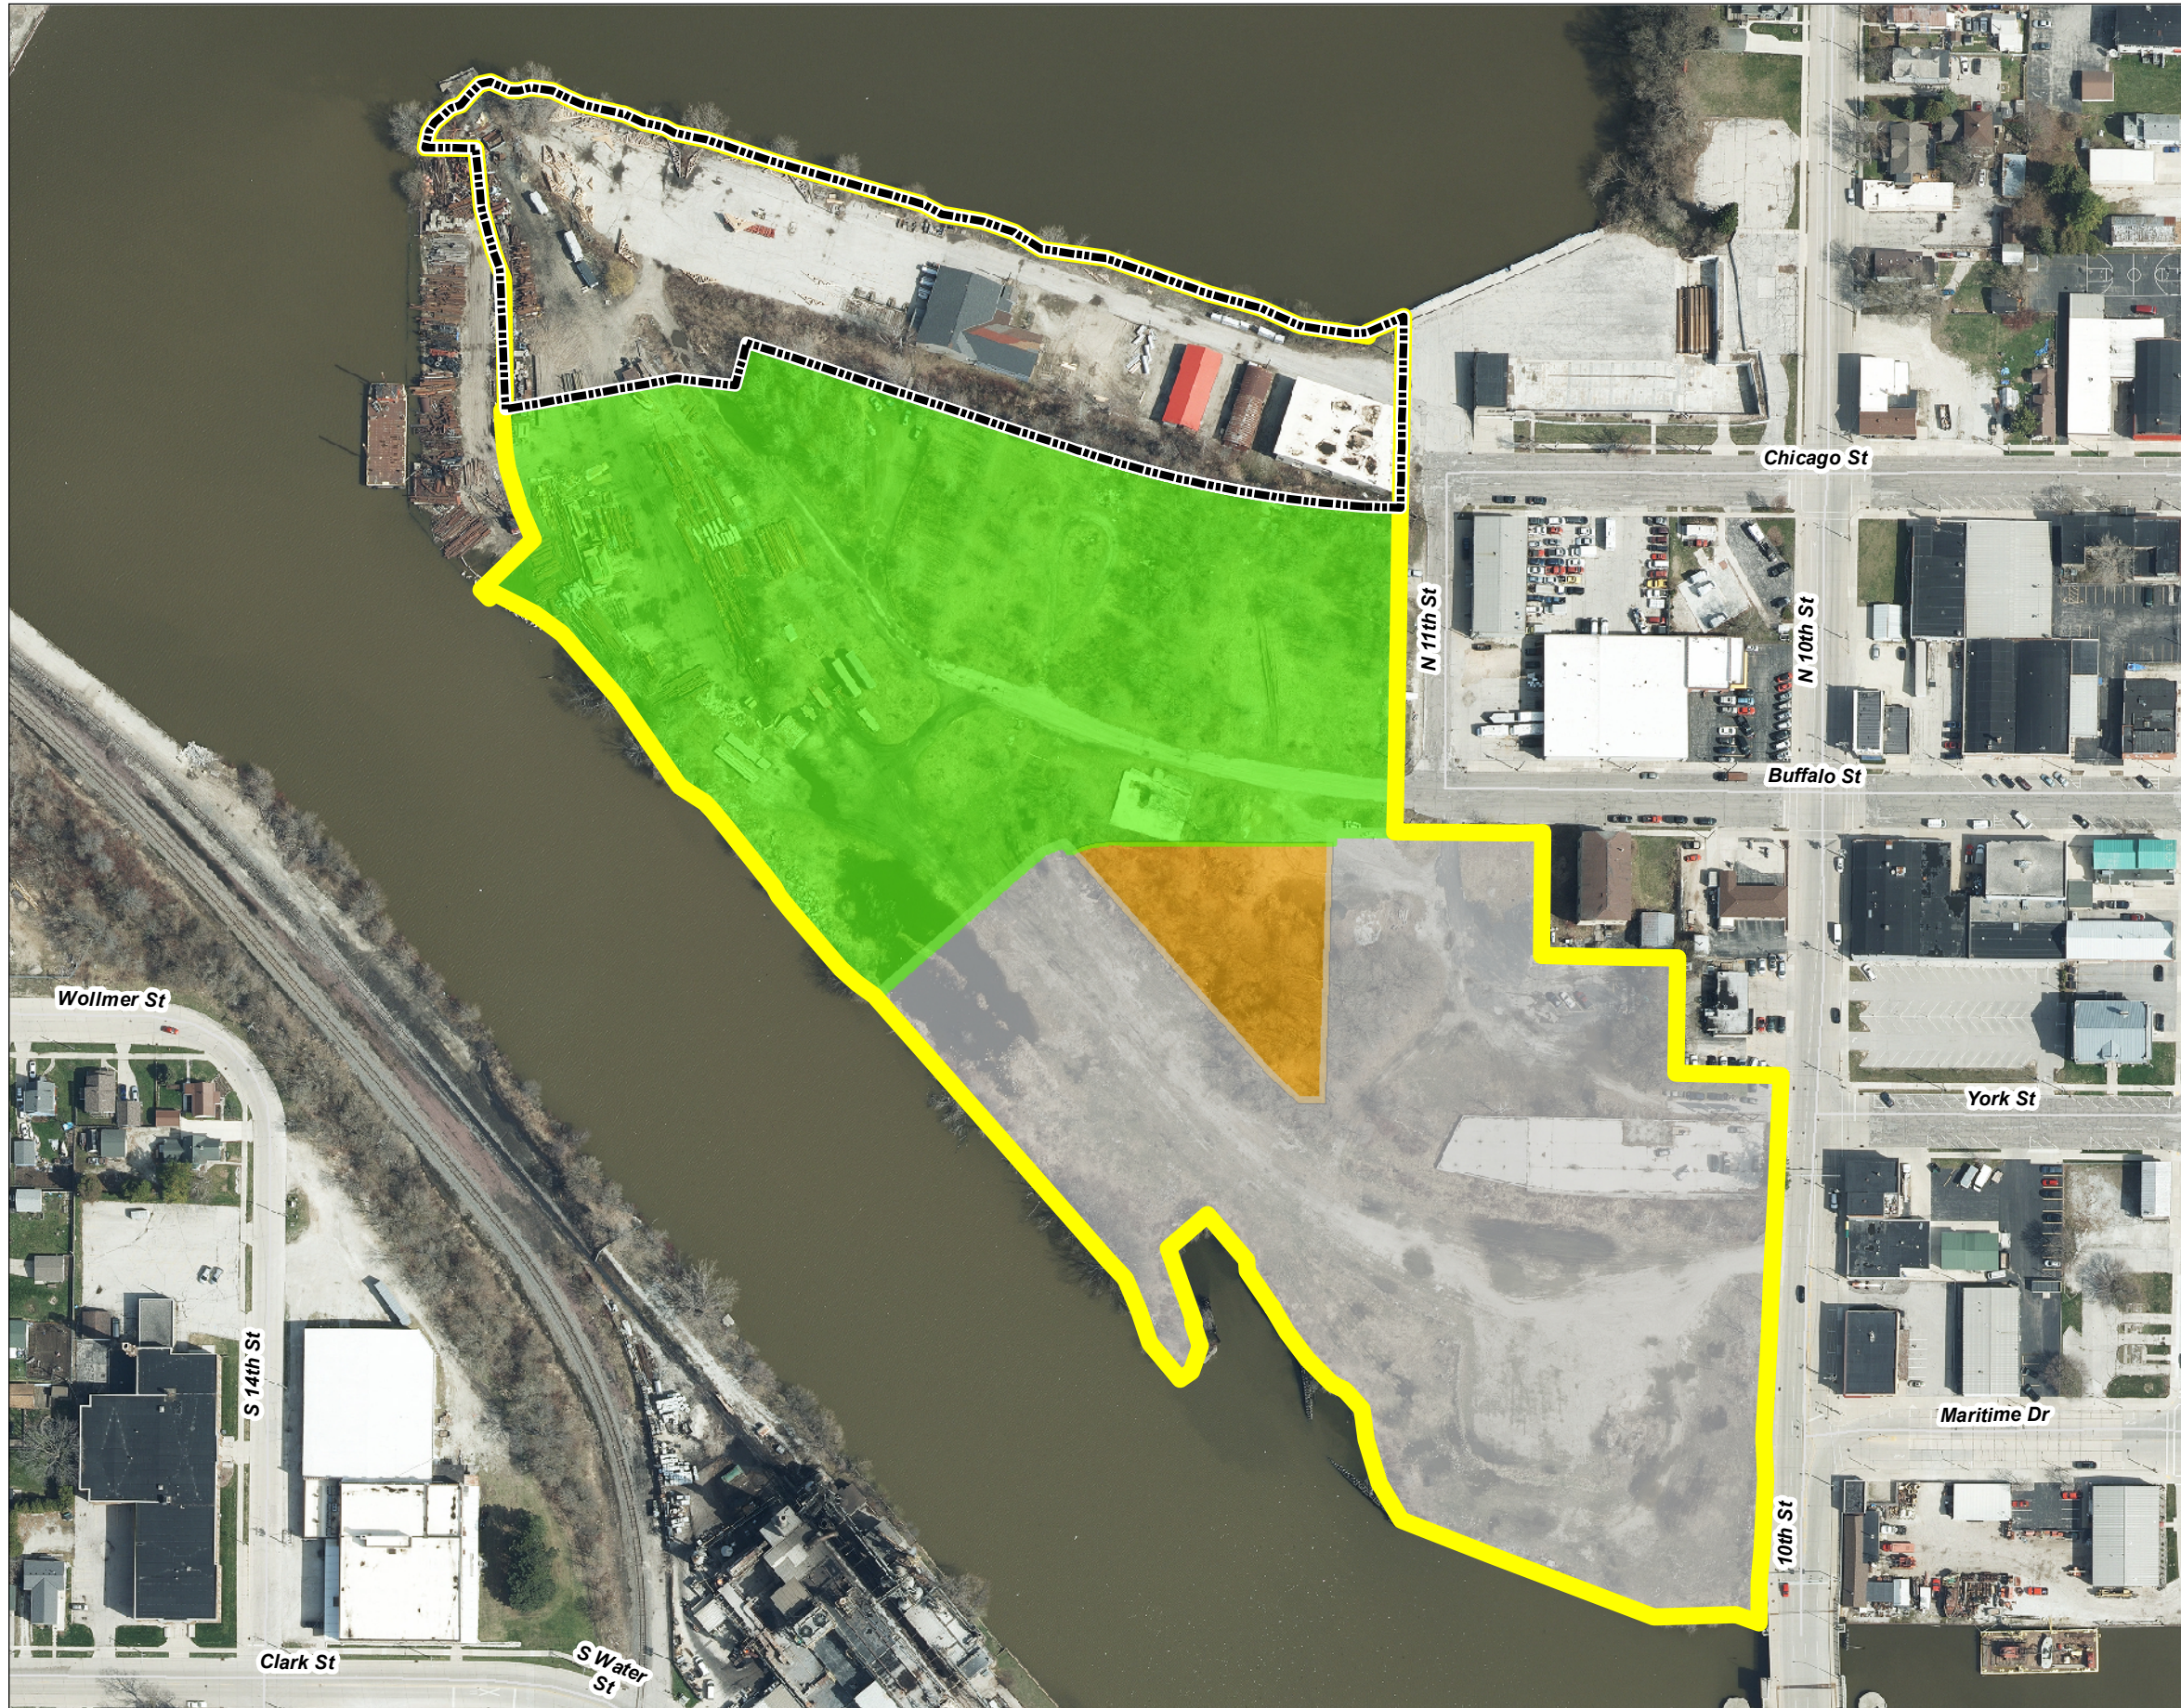


Figure No.
2
 Title
**Phase III Redevelopment Area
 and Previous SAG Project Areas**
 Client/Project
 Phase III Redevelopment Area
 River Point District
 City of Manitowoc
 0 130 260 Feet
 193708490
 Prepared by HLB on 3/30/2023

Legend


River Point District

Phase III Redevelopment Area

Phase II Redevelopment Area (SAG 2022)

Phase I Redevelopment Area (SAG 2020-2021)

Former Turntable and Engine House - NO SAG



Notes
 1. Coordinate System: NAD 1983 HARN WISCRS Manitowoc County Feet
 2. Orthophotograph: Manitowoc County, 2020



| Construction Area | Project Area | Phase of Work | Report | Status |
|---|---|---|--------|---|
| Phase I Construction Area | River North Apartments | Excavation of Petroleum Soil | | Submittal to you 4/28/2023 |
| | | Construction of SSDS | | Submittal to you 4/28/2023 |
| | | Sub-Slab Vapor Samples | | Submittal to you 4/28/2023 |
| | | Construction of Engineered Barriers | | Writing |
| | | Institutional Controls | | Wait until finish sub-slab vapor sampling (Fall 2023)? |
| | Junk Yard | Excavation of Soil for Stormwater (2021) + Excavation of Additional Soil (2023) = 2400 cy; fill to grade with topsoil and grass | | RACR Writing Now; Expect to You ~ May 2 |
| | | Post-Removal GW Sampling | | Expected Summer 2023, once grass is established |
| | | SI/RAOR/RAP (etc.) | | Once developer identified |
| | "Area B1" | Phase II ESA/SI (2022-2023 Sampling) | | Draft written; expect to you by May 5 |
| | Rights of Way | 2021 Roadwork finished | | Recommendations on next steps? Combined Construction Documentation Report?? |
| 2023 Roadwork and Shoreline (RAP/MMP Approved; Work Starting early May) | | | | |
| Phase II Construction Area | River front; former bulk petroleum area | Site Investigation | | Expected to you by May 5; need work to delineate GW impacts to far NE area |
| | Townhomes / Restaurant | RAP/MMP/718 Exemption | | Once developer identified |
| | Rights of Way | Roadwork and Shoreline (2024?) | | Once plans are developed |
| Phase III Construction Area | Northern river front; Braun Building | Site Investigation Workplan | | Implementation pending funding (SAG or Community-Managed WAM) |
| | Townhomes | RAP/MMP/718 Exemption | | Once developer identified |
| | Rights of Way | Roadwork and Shoreline (2024?) | | Once plans are developed |
