


*Ripon FF/NN Superfund Site
ERR # 915*

January 8, 1996
(304733096/2014)



Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711

Dear Mr. Ales:

Enclosed please find two copies of the Monthly Status Report for the Remedial Design work at FF/NN Landfill in Ripon, Wisconsin. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.

Judy L. Fassbender
Judy L. Fassbender
Project Manager

JLF:gf
Enc.

cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Jane Lemke/Environmental Response and Repair Section (SW/3), WDNR (1 copy)
Jim Kaiser, City of Ripon, Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01
MONTHLY STATUS REPORT

December, 1995

SITE NAME/ACTIVITY:

FF/NN Landfill
Ripon, Wisconsin
Remedial Design

PREPARED BY:

Mr. Ray Roder
Rienhart, Boerner, Van Deuren, Norris
& Rieselbach, S.C.
7617 Mineral Point Road
Milwaukee, Wisconsin 53701-2020

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Ms. Jane Lemke
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (1 copy)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (2 copies)

DATE:

January 1996

PERIOD:

December 1 - 31, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ Preparation of the Engineer's Report, RD/RA Work Plan, Monitoring Program Plan, QAPP and Health and Safety Plans continued in December. The RD/RA Work Plan and plan sheets were submitted to WDNR in December.

DATA TRANSMITTED WITH REPORT:

- ◆ None

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, December 8, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract for the RI/FS have been met. The RD/RA Work Plan was submitted to WDNR on December 6, 1995. The remainder of the RD/RA related documents will be submitted to WDNR in January 1996.

UPCOMING ACTIVITIES PLANNED:

- ◆ Remedial design activities are nearly complete. Preparation of the Engineer's Report, Monitoring Program Plan, Quality Assurance Project Plan, and Health and Safety Plans will be completed in early January.

PERSONNEL:

- ◆ No personnel changes have been made.
- ◆ Judy Fassbender, Senior Hydrogeologist, manages the project; Gerald DeMers, Senior Engineer, and Steven Franks, Director of Engineering, are currently directing the landfill cap and gas venting design work. Jennifer Ronk, Hydrogeologist, assists with plan preparations.

MEETINGS:

- ◆ No meetings were held during this reporting period.

*Ripon FF/NN Superfund
site, # 915*

December 8, 1995
(304733096/2014)


Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711

Dear Mr. Ales:

Enclosed please find three copies of the Monthly Status Report for the Remedial Design work at FF/NN Landfill in Ripon, Wisconsin. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.



Judy L. Fassbender
Project Manager

JLF:gf
Enc.

cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Section Chief/Environmental Response and Repair Section (SW/3), WDNR (1 copy)
Jim Kaiser, City of Ripon, Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01
MONTHLY STATUS REPORT

November, 1995

SITE NAME/ACTIVITY:

FF/NN Landfill
Ripon, Wisconsin
Remedial Design

PREPARED BY:

Mr. Ray Roder
Rienhart, Boerner, Van Deuren, Norris
& Rieselbach, S.C.
7617 Mineral Point Road
Milwaukee, Wisconsin 53701-2020

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Mr. Mark Giesfeldt
Section Chief
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (1 copy)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (2 copies)

DATE:

December 1995

PERIOD:

November 1 - 30, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ Preparation of the Engineer's Report, RD/RA Work Plan, Monitoring Program Plan, QAPP and Health and Safety Plans continued in November and will be completed in December.

DATA TRANSMITTED WITH REPORT:

- ◆ None

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, November 7, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract for the RI/FS have been met. Target dates for the remedial design will be established in the RD/RA Work Plan which was submitted to WDNR on December 6, 1995.

UPCOMING ACTIVITIES PLANNED:

- ◆ Remedial design activities are in progress and will continue into December. Also preparation of the OU-1 RD/RA Work Plan, Engineer's Report, Monitoring Program Plan, Quality Assurance Project Plan, and Health and Safety Plans will be completed.

PERSONNEL:

- ◆ No personnel changes have been made.
- ◆ Judy Fassbender, Senior Hydrogeologist, manages the project; Gerald DeMers, Senior Engineer, and Steven Franks, Director of Engineering, are currently directing the landfill cap and gas venting design work. Jennifer Ronk, Hydrogeologist, assists with plan preparations.

MEETINGS:

- ◆ No meetings were held during this reporting period.

HYDRO-SEARCH, INC.
A Tetra Tech Company

ERR/SF
FID# 431048200

November 7, 1995
(304733096/2014)


Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711

Dear Mr. Ales:


Enclosed please find three copies of the Monthly Status Report for the Remedial Design work at **FF/NN Landfill in Ripon, Wisconsin**. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.


Judy L. Fassbender
Project Manager

JLF:gf
Enc.



cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Section Chief/Environmental Response and Repair Section (SW/3), WDNR (3 copies)
Jim Kaiser, City of Ripon, Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01
MONTHLY STATUS REPORT

October, 1995

SITE NAME/ACTIVITY:

FF/NN Landfill
Ripon, Wisconsin
Remedial Design

PREPARED BY:

Mr. Ray Roder
Rienhart, Boerner, Van Deuren, Norris
& Rieselbach, S.C.
7617 Mineral Point Road
Milwaukee, Wisconsin 53701-2020

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Mr. Mark Giesfeldt
Section Chief
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (3 copies)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (3 copies)

DATE:

November 1995

PERIOD:

October 1 - 31, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ Preparation of the Engineer's Report continued in October.
- ◆ Preparation of the RD/RA Work Plan, the Monitoring Program Plan QAPP and Health and Safety Plans is nearing completion.

DATA TRANSMITTED WITH REPORT:

- ◆ None

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, October 10, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract for the RI/FS have been met. Target dates for the remedial design will be established in the RD/RA Work Plan which will be submitted to WDNR in mid November.

UPCOMING ACTIVITIES PLANNED:

- ◆ Remedial design activities are in progress and will continue through November. Also preparation of the OU-1 RD/RA Work Plan, Monitoring Program Plan, Quality Assurance Project Plan, and Health and Safety Plans will be completed.

PERSONNEL:

- ◆ No personnel changes have been made.
- ◆ Judy Fassbender, Senior Hydrogeologist, manages the project; Gerald DeMers, Senior Engineer, and Steven Franks, Director of Engineering, are currently directing the landfill cap and gas venting design work. Jennifer Ronk, Hydrogeologist, assists with plan preparations.


MEETINGS:

- ◆ No meetings were held during this reporting period.

HYDRO-SEARCH, INC.
A Tetra Tech Company

*Ripon FF/NN Superfund
Site, #915*

October 10, 1995
(304733096/2014)



Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711

Dear Mr. Ales:

Enclosed please find three copies of the Monthly Status Report for the Remedial Design work at FF/NN Landfill in Ripon, Wisconsin. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.

Judy L. Fassbender
Project Manager

JLF:gf
Enc.

cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Section Chief/Environmental Response and Repair Section (SW/3), WDNR (3 copies)
Jim Kaiser, City of Ripon, Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01
MONTHLY STATUS REPORT

September, 1995

SITE NAME/ACTIVITY:

FF/NN Landfill
Ripon, Wisconsin
Remedial Design

PREPARED BY:

Mr. Ray Roder
Rienhart, Boerner, Van Deuren, Norris
& Rieselbach, S.C.
7617 Mineral Point Road
Milwaukee, Wisconsin 53701-2020

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Mr. Mark Giesfeldt
Section Chief
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (3 copies)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (3 copies)

DATE:

October 1995

PERIOD:

September 1 - 30, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ Preparation of the Engineer's Report continued in September. Design calculations are currently undergoing internal review by Hydro-Search.
- ◆ Preparation of the RD/RA Work Plan, the Monitoring Program Plan, QAPP and Health and Safety Plans is nearly complete.

DATA TRANSMITTED WITH REPORT:

- ◆ None

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, September 7, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract for the RI/FS have been met. Target dates for the remedial design will be established in the RD/RA Work Plan which will be submitted to WDNR in early November.

UPCOMING ACTIVITIES PLANNED:

- ◆ Remedial design activities are in progress and will continue through October. Also preparation of the OU-1 RD/RA Work Plan, Monitoring Program Plan, Quality Assurance Project Plan, and Health and Safety Plans will be completed.

PERSONNEL:

- ◆ No personnel changes have been made.
- ◆ Judy Fassbender, Senior Hydrogeologist, manages the project; Gerald DeMers, Senior Engineer, and Steven Franks, Director of Engineering, are currently directing the landfill cap and gas venting design work. Jennifer Ronk, Hydrogeologist, assists with plan preparations.

MEETINGS:


- ◆ A meeting between Steve Ales of WDNR; Gerald DeMers, Steve Franks, and Judy Fassbender of Hydro-Search; and Ray Roder of Reinhart, Boerner, Van Deuren, Norris & Rieselbach was held on September 6, 1995 to discuss aspects of the design for the cap and gas system.

HYDRO-SEARCH, INC.

A Tetra Tech Company

Ripon FF/NN Superfund Site #915-

September 7, 1995
(304733096/2014)



Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711

Dear Mr. Ales:

Enclosed please find three copies of the Monthly Status Report for the Remedial Design work at FF/NN Landfill in Ripon, Wisconsin. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.


Judy L. Fassbender
Project Manager

JLF:gf
Enc.

cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Section Chief/Environmental Response and Repair Section (SW/3), WDNR (3 copies)
Jim Kaiser, City of Ripon, Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01
MONTHLY STATUS REPORT

August, 1995

SITE NAME/ACTIVITY:

FF/NN Landfill
Ripon, Wisconsin
Remedial Design

PREPARED BY:

Mr. Ray Roder
Rienhart, Boerner, Van Deuren, Norris
& Rieselbach, S.C.
7617 Mineral Point Road
Milwaukee, Wisconsin 53701-2020

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Mr. Mark Giesfeldt
Section Chief
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (3 copies)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (3 copies)

DATE:

September 1995

PERIOD:

August 1 - 31, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ Preparation of plan sheets, including the following continued during August:
 - Plan view with existing contours
 - Contours with topsoil removed, gas trench locations
 - Cross sections
 - Details
 - Typical pipe and Anchor trench
 - drainage pipe outlet
 - typical cross section at edge of geosynthetics
 - cross section of gas trench
 - passive gas vent
 - small animal exclusion device
 - gas collection piping expansion joint

- ◆ The Engineer's report was begun. Design calculation and text was prepared on the following:
 - Gas generation and piping sizing
 - Slope stability
 - HELP Modeling for cap drainage
 - Cover subsidence

DATA TRANSMITTED WITH REPORT:

- ◆ None

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, August 7, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract for the RI/FS have been met. Target dates for the remedial design will be established following issuance of the Proposed Plan.

UPCOMING ACTIVITIES PLANNED:

- ◆ Remedial design activities are in progress and will continue through September. Also preparation of the OU-1 RD/RA Work Plan, Monitoring Program Plan, Quality Assurance Project Plan, and Health and Safety Plans will continue.

PERSONNEL:

- ◆ No personnel changes have been made.
- ◆ Judy Fassbender, Senior Hydrogeologist, manages the project; Gerald DeMers, Senior Engineer, and Steven Franks, Director of Engineering, are currently directing the landfill cap and gas venting design work. Jennifer Ronk, Hydrogeologist, assists with plan preparations.

MEETINGS:


- ◆ No meetings were held in August. A meeting between Steve Ales of WDNR; Gerald DeMers, Steve Franks, and Judy Fassbender of Hydro-Search; and Ray Roder of Reinhart, Boerner, Van Deuren, Norris & Rieselbach has been scheduled for September 6, 1995 to discuss aspects of the design for the cap and gas system.

F0112

HYDRO-SEARCH, INC.
A Tetra Tech Company

*Ripon FF/NN Superfund site
#915*

August 7, 1995
(304733096/2014)



Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711

Dear Mr. Ales:

Enclosed please find three copies of the Monthly Status Report for the Remedial Design work at FF/NN Landfill in Ripon, Wisconsin. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.

Judy L. Fassbender
Judy L. Fassbender
Project Manager

JLF:gf
Enc.

cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Section Chief/Environmental Response and Repair Section (SW/3), WDNR (3 copies)
Jim Kaiser, City of Ripon, Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01
MONTHLY STATUS REPORT

July, 1995

SITE NAME/ACTIVITY:

FF/NN Landfill
Ripon, Wisconsin
Remedial Design

PREPARED BY:

Mr. Ray Roder
Rienhart, Boerner, Van Deuren, Norris
& Rieselbach, S.C.
7617 Mineral Point Road
Milwaukee, Wisconsin 53701-2020

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Mr. Mark Giesfeldt
Section Chief
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (3 copies)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (3 copies)

DATE:

August 1995

PERIOD:

July 1 - 31, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ Preparation of plan sheets, including the following began during July:
 1. Title sheet, location map, list of drawings
 2. Plan view with existing contours
 3. Contours with topsoil removed, gas trench locations
 4. Contours with clay in-place
 5. Cut and Fill Contours for Clay
 6. Contours with vegetative cover soil in-place
 7. Contours with topsoil in-place-final grades
 8. Cross sections (3) -
 9. Cross sections (3) - 12 cross sections required
 10. Cross sections (3) - for 100' x 100' intervals
 11. Cross sections (3) -
 12. Details - Typical pipe and Anchor trench detail
 - drainage pipe outlet detail
 - typical cross section at edge of geosynthetics
 - cross section of gas trench detail
 - passive gas vent detail
 - small animal exclusion device detail
 - gas collection piping expansion joint

- ◆ Preparation of several of the remedial design related plans was also initiated in July.

DATA TRANSMITTED WITH REPORT:

- ◆ None

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, July 12, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract for the RI/FS have been met. Target dates for the remedial design will be established following issuance of the Proposed Plan.

UPCOMING ACTIVITIES PLANNED:

- ◆ Remedial design activities are in progress and will continue through August. Also preparation of the OU-1 RD/RA Work Plan, Monitoring Program Plan, Quality Assurance Project Plan, and Health and Safety Plans will continue.

PERSONNEL:

- ◆ No personnel changes have been made.
- ◆ Judy Fassbender, Senior Hydrogeologist, manages the project; Gerald DeMers, Senior Engineer, and Steven Franks, Director of Engineering, are currently directing the landfill cap and gas venting design work. Jennifer Ronk, Hydrogeologist, assists with plan preparations.


MEETINGS:

- ◆ No meetings were held in July. However, a meeting between Steve Ales and Jeff Otto (if available) of WDNR and Gerald DeMers and Steve Franks of Hydro-Search will be scheduled in August to discuss aspects of the design for the cap and gas system.

HYDRO-SEARCH, INC.

A Tetra Tech Company

*Ripon FF/NN Superfund Site
#915*



July 12, 1995
(304733096/1010)


Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711

Dear Mr. Ales:

Enclosed please find three copies of the Monthly Status Report for the Remedial Investigation/Feasibility Study work at FF/NN Landfill in Ripon, Wisconsin. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.


Judy L. Fassbender
Project Manager

JLF:gf
Enc.

cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Section Chief/Environmental Response and Repair Section (SW/3), WDNR (3 copies)
Jim Kaiser, City of Ripon Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01
MONTHLY STATUS REPORT

June, 1995

SITE NAME/ACTIVITY:

FF/NN Landfill
Ripon, Wisconsin
Remedial Investigation/Feasibility Study

PREPARED BY:

Mr. Ray Roder
Whyte, Hirschboeck & Dudek
One East Main Street
Madison, Wisconsin 53701

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Mr. Mark Giesfeldt
Section Chief
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (3 copies)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (3 copies)

DATE:

July, 1995

PERIOD:

June 1 - 30, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ As a result of the April 7, 1995 meeting with WDNR, an additional cap and gas alternative was evaluated in an Addendum to the FS. The Addendum was submitted to the WDNR on June 2, 1995.
- ◆ Future ground-water contaminant concentrations for composite cap and existing cap conditions were projected using an analytical model. The projected concentrations and model results were presented in a Technical Memorandum which was submitted to the WDNR on June 8, 1995.
- ◆ Several aspects of the work related to the remedial design have been initiated. These include initial clay borrow source investigations, site surveying, confirmation of cap thickness and initial internal planning for the design itself. Two potential clay borrow sources have been identified for use. Both of the sources have undergone significant physical property testing related to the use of the clay for other landfill sites. Adequate amounts and quality of clay exists at one of the two locations identified; adequate quantities of clay may be available at the second area as well. The availability of clay at the second location will be confirmed in the next several weeks.
- ◆ A surveyor was contracted to complete a survey of the landfill. The final survey presents topography using one foot contour intervals so areas of settling which may have developed since the last survey in 1991 can be easily noted. Capping material quantities will be calculated using the new survey information to ensure appropriate cap thickness and drainage for the planned cap. The survey was complete June 29, 1995.
- ◆ On Monday, June 19, 1995, Hydro-Search completed an extensive series of hand auger borings on the landfill cap to better define areas suspected of having less than 2 feet of clay. Based on information collected during the Remedial Investigation, areas near LC-2, along Highway NN and along the north and west edges of the landfill were identified as having less than 2 feet of clay. The precise extent of areas with less than two feet of clay is critical to estimating the amount of clay required for the new cap. Hand auger borings revealed that a much smaller area of the cap than originally estimated requires additional clay.

DATA TRANSMITTED WITH REPORT:

- ◆ Revised Clay Cap Thickness Map.

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, June 13, 1995.
- ◆ Feasibility Study Report Addendum, June 2, 1995.
- ◆ Ground-water Contaminant Concentration Projection Technical Memorandum, June 8, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract are as follows:

- ◆ Task 1 - Draft Site Evaluation Report, (September 14, 1992, completed).
- ◆ WDNR approval of Task 1 - Site Evaluation Report (October 1, 1992, completed).
- ◆ Task 1 - Final Draft, Site Evaluation Report, 30 days following WDNR request for draft modifications, if any (not applicable).
- ◆ Task 2 - Draft Work Plans, 60 days following WDNR approval of the Site Evaluation Report, (December 15, 1992 completed).
- ◆ WDNR review of Task 2 - Draft Work Plans (60 days; February 12, 1993, completed).
- ◆ Task 2 - Revised Work Plans (March 19, 1993, completed).
- ◆ WDNR approval of revised work plans (March 31, 1993, completed).
- ◆ Target compound shortlist recommendation (August 25, 1993, completed).
- ◆ Technical Memorandum #1 (October 20, 1993, completed).
- ◆ Recommendations for additional well locations (January 12, 1994, completed).
- ◆ Alternative Array Document (June 15, 1994, completed).
- ◆ RI Report (August 19, 1994, completed).
- ◆ Feasibility Study Report (January 6, 1995, completed).
- ◆ Feasibility Study Report Addendum (June 2, 1995, completed).
- ◆ Ground-Water Contaminant Concentration Projection Technical Memorandum (June 8, 1995, completed).

UPCOMING ACTIVITIES PLANNED:


- ◆ Remedial design activities are in progress and will continue through July. Also preparation of the OU-1 RD/RA Work Plan, Monitoring Program Plan, Quality Assurance Project Plan, and Health and Safety Plan will continue.

PERSONNEL CHANGES:

- ◆ None.


MEETINGS:

- ◆ A conference call was held with the WDNR on June 29, 1995 to discuss remedial design issues. Steve Ales and Jeff Otto of WDNR discussed aspects of the design for the cap and gas system with Gerald DeMers and Steve Franks of Hydro-Search.

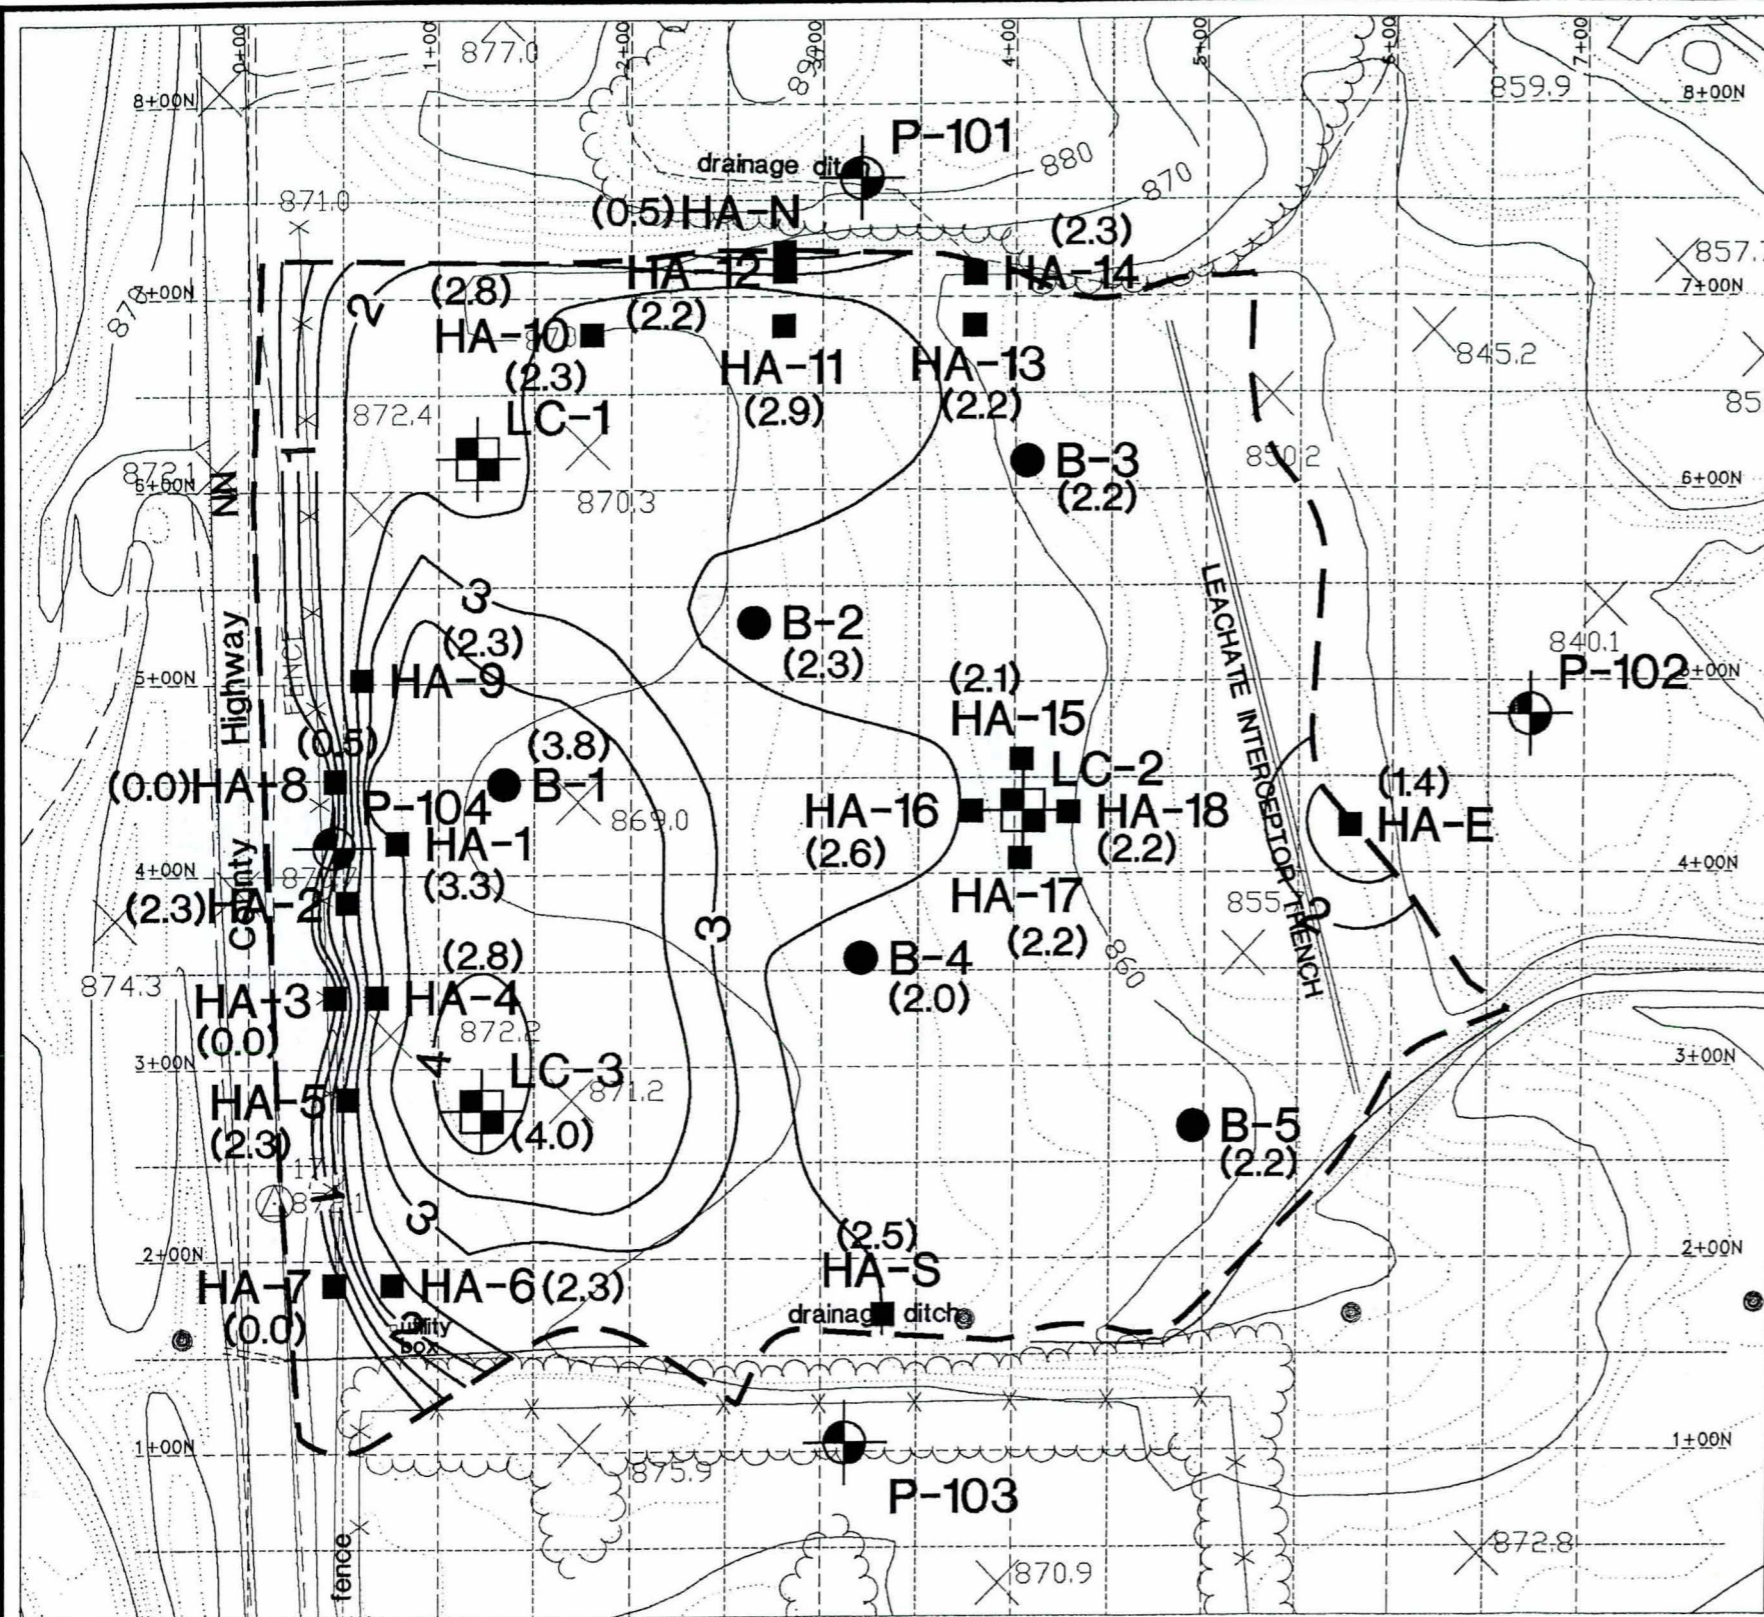

EXPLANATION

- B-2 BOREHOLE LOCATION AND DESIGNATION
- HA-N HAND AUGER LOCATION AND DESIGNATION
- ⊠ LC-1 LEACHATE HEAD WELL LOCATION AND DESIGNATION
- ⊙ P-104 PIEZOMETER LOCATION AND DESIGNATION
- - - - - APPROXIMATE EXTENT OF REFUSE
- (2.2) THICKNESS OF CLAY LAYER (feet)
- 3 — THICKNESS CONTOUR (feet)




FF/NN LANDFILL RIPON, WISCONSIN	DATE: 07/11/95
THICKNESS OF CLAY LAYER	DESIGNED: MCL
	CHECKED: GLD
	APPROVED: SPF
	DRAWN: MCL
	PROJ: 304733098
HYDRO-SEARCH INC A Tetra Tech Company	Figure 2

HYDRO-SEARCH, INC.
A Tetra Tech Company

*Ripon FF/NN Superfund site
915*

June 13, 1995
(304733096/1010)



Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711

Dear Mr. Ales:

Enclosed please find three copies of the Monthly Status Report for the Remedial Investigation/Feasibility Study work at FF/NN Landfill in Ripon, Wisconsin. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.

Judy L. Fassbender
Judy L. Fassbender
Project Manager

JLF:gf
Enc.

cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Section Chief/Environmental Response and Repair Section (SW/3), WDNR (3 copies)
Jim Kaiser, City of Ripon Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01
MONTHLY STATUS REPORT

May, 1995

SITE NAME/ACTIVITY:

FF/NN Landfill
Ripon, Wisconsin
Remedial Investigation/Feasibility Study

PREPARED BY:

Mr. Ray Roder
Whyte, Hirschboeck & Dudek
One East Main Street
Madison, Wisconsin 53701

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Mr. Mark Giesfeldt
Section Chief
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (3 copies)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (3 copies)

DATE:

June, 1995

PERIOD:

May 1 - 31, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ As a result of the April 7, 1995 meeting with WDNR, an additional cap and gas alternative was evaluated in an Addendum to the FS. The Addendum was submitted to the WDNR on June 2, 1995.
- ◆ Future ground-water contaminant concentrations for composite cap and existing cap conditions were projected using an analytical model. The projected concentrations and model results have been presented in a Technical Memorandum which was submitted to the WDNR on June 8, 1995.
- ◆ A request for WDNR approval to begin remedial design work for the source control operable unit was submitted on May 24, 1995. WDNR approved the immediate start of remedial design activities on their May 26, 1995 correspondence.

DATA TRANSMITTED WITH REPORT:

- ◆ None.

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, May 3, 1995.
- ◆ Request for approval to begin the Source Control Remedial Design, May 24, 1995.
- ◆ Feasibility Study Report Addendum, June 2, 1995.
- ◆ Ground-water Contaminant Concentration Projection Technical Memorandum, June 8, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract are as follows:

- ◆ Task 1 - Draft Site Evaluation Report, (September 14, 1992, completed).
- ◆ WDNR approval of Task 1 - Site Evaluation Report (October 1, 1992, completed).

Monthly Status Report

Page 3

- ◆ Task 1 - Final Draft, Site Evaluation Report, 30 days following WDNR request for draft modifications, if any (not applicable).
- ◆ Task 2 - Draft Work Plans, 60 days following WDNR approval of the Site Evaluation Report, (December 15, 1992 completed).
- ◆ WDNR review of Task 2 - Draft Work Plans (60 days; February 12, 1993, completed).
- ◆ Task 2 - Revised Work Plans (March 19, 1993, completed).
- ◆ WDNR approval of revised work plans (March 31, 1993, completed).
- ◆ Target compound shortlist recommendation (August 25, 1993, completed).
- ◆ Technical Memorandum #1 (October 20, 1993, completed).
- ◆ Recommendations for additional well locations (January 12, 1994, completed).
- ◆ Alternative Array Document (June 15, 1994, completed).
- ◆ RI Report (August 19, 1994, completed).
- ◆ Feasibility Study Report (January 6, 1995, completed).
- ◆ Feasibility Study Report Addendum (June 2, 1995, completed).
- ◆ Ground-Water Contaminant Concentration Projection Technical Memorandum (June 8, 1995, completed).

UPCOMING ACTIVITIES PLANNED:

- ◆ Remedial design activities are in progress. A site survey is currently being scheduled for late June and potential borrow sources are under investigation. Preparation of the OU-1 RD/RA Work Plan, Monitoring Program Plan, Quality Assurance Project Plan, and Health and Safety Plan will begin in June.

PERSONNEL CHANGES:


- ◆ None.

MEETINGS:

- ◆ A meeting with the WDNR is planned for June 29, 1995 to discuss remedial design issues. No meetings were held during this reporting period.

Ripon FF/NN, #915

May 3, 1995
(304733096/1010)



Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711

Dear Mr. Ales:

Enclosed please find three copies of the Monthly Status Report for the Remedial Investigation/Feasibility Study work at Ripon FF/NN Landfill in Ripon, Wisconsin. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.

Judy L. Fassbender
Project Manager

JLF:gf
Enc.

cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Section Chief/Environmental Response and Repair Section (SW/3), WDNR (3 copies)
Jim Kaiser, City of Ripon Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01
MONTHLY STATUS REPORT

April, 1995

SITE NAME/ACTIVITY:

Ripon FF/NN Landfill
Ripon, Wisconsin
Remedial Investigation/Feasibility Study

PREPARED BY:

Mr. Ray Roder
Whyte, Hirschboeck & Dudek
One East Main Street
Madison, Wisconsin 53701

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Mr. Mark Giesfeldt
Section Chief
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (3 copies)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (3 copies)

DATE:

May, 1995

PERIOD:

April 1 - 30, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ A meeting was held at the WDNR Fitchburg office to discuss the findings of the RI report, FS and possible additional remedial alternatives on April 7, 1995.
- ◆ As a result of the April 7, 1995 meeting, an additional cap and gas alternative will be evaluated in an Addendum to the FS. The Addendum will be submitted to the WDNR in mid May.
- ◆ Future ground-water contaminant concentrations for composite cap and existing cap conditions will be projected using an analytical model. The projected concentrations and model results will be presented in a Technical Memorandum which will be submitted to the WDNR in mid May.

DATA TRANSMITTED WITH REPORT:

- ◆ None.

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, April 7, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract are as follows:

- ◆ Task 1 - Draft Site Evaluation Report, (September 14, 1992, completed).
- ◆ WDNR approval of Task 1 - Site Evaluation Report (October 1, 1992, completed).
- ◆ Task 1 - Final Draft, Site Evaluation Report, 30 days following WDNR request for draft modifications, if any (not applicable).
- ◆ Task 2 - Draft Work Plans, 60 days following WDNR approval of the Site Evaluation Report, (December 15, 1992 completed).
- ◆ WDNR review of Task 2 - Draft Work Plans (60 days; February 12, 1993, completed).

- ◆ Task 2 - Revised Work Plans (March 19, 1993, completed).
- ◆ WDNR approval of revised work plans (March 31, 1993, completed).
- ◆ Target compound shortlist recommendation (August 25, 1993, completed).
- ◆ Technical Memorandum #1 (October 20, 1993, completed).
- ◆ Recommendations for additional well locations (January 12, 1994, completed).
- ◆ Alternative Array Document (June 15, 1994, completed).
- ◆ RI Report (August 19, 1994, completed).
- ◆ Feasibility Study Report (January 6, 1995, completed).
- ◆ Feasibility Study Report Addendum, mid May 1995.
- ◆ Ground-Water Contaminant Concentration Projection Technical Memorandum, mid May 1995.

UPCOMING ACTIVITIES PLANNED:

- ◆ The Addendum to the FS and the Contaminant Projection Technical Memorandum are currently being prepared and will be completed in May.

PERSONNEL CHANGES:

- ◆ None.

MEETINGS:

- ◆ A meeting was held on April 7, 1995 to discuss future actions at the site.


HYDRO-SEARCH, INC.

A Tetra Tech Company

*Ripon FF/NN Superfund Site
915*

April 7, 1995
(304733096/1010)

Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711




Dear Mr. Ales:

Enclosed please find three copies of the Monthly Status Report for the Remedial Investigation/Feasibility Study work at Ripon FF/NN Landfill in Ripon, Wisconsin. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.


Judy L. Fassbender
Project Manager

JLF:gf
Enc.

cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Section Chief/Environmental Response and Repair Section (SW/3), WDNR (3 copies)
Jim Kaiser, City of Ripon Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01

MONTHLY STATUS REPORT

March, 1995

SITE NAME/ACTIVITY:

Ripon FF/NN Landfill
Ripon, Wisconsin
Remedial Investigation/Feasibility Study

PREPARED BY:

Mr. Ray Roder
Whyte, Hirschboeck & Dudek
One East Main Street
Madison, Wisconsin 53701

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Mr. Mark Giesfeldt
Section Chief
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (3 copies)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (3 copies)

DATE:

April, 1995

PERIOD:

March 1 - 31, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ A meeting to discuss the findings of the RI report, FS and possible additional remedial alternatives was originally scheduled for March 23, and was later rescheduled for April 7, 1995. No activity other than preparation for the meeting has occurred on this project during this reporting period.

DATA TRANSMITTED WITH REPORT:

- ◆ None.

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, March 2, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract are as follows:

- ◆ Task 1 - Draft Site Evaluation Report, (September 14, 1992, completed).
- ◆ WDNR approval of Task 1 - Site Evaluation Report (October 1, 1992, completed).
- ◆ Task 1 - Final Draft, Site Evaluation Report, 30 days following WDNR request for draft modifications, if any (not applicable).
- ◆ Task 2 - Draft Work Plans, 60 days following WDNR approval of the Site Evaluation Report, (December 15, 1992 completed).
- ◆ WDNR review of Task 2 - Draft Work Plans (60 days; February 12, 1993, completed).
- ◆ Task 2 - Revised Work Plans (March 19, 1993, completed).
- ◆ WDNR approval of revised work plans (March 31, 1993, completed).
- ◆ Target compound shortlist recommendation (August 25, 1993, completed).
- ◆ Technical Memorandum #1 (October 20, 1993, completed).

- ◆ Recommendations for additional well locations (January 12, 1994, completed).
- ◆ Alternative Array Document (June 15, 1994, completed).
- ◆ RI Report (August 19, 1994, completed).
- ◆ Feasibility Study Report (January 6, 1995, completed).

UPCOMING ACTIVITIES PLANNED:

- ◆ A meeting is planned for April 7, 1995 to discuss future actions at the site.

PERSONNEL CHANGES:


- ◆ None.

MEETINGS:

- ◆ None.

Ripon FF/NN Landfill #915

March 2, 1995
(304733096/1010)




Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711

Dear Mr. Ales:

Enclosed please find three copies of the Monthly Status Report for the Remedial Investigation/Feasibility Study work at Ripon FF/NN Landfill in Ripon, Wisconsin. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.


Judy L. Fassbender
Project Manager

JLF:gf
Enc.

cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Section Chief/Environmental Response and Repair Section (SW/3), WDNR (3 copies)
Jim Kaiser, City of Ripon Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01
MONTHLY STATUS REPORT

February, 1995

SITE NAME/ACTIVITY:

Ripon FF/NN Landfill
Ripon, Wisconsin
Remedial Investigation/Feasibility Study

PREPARED BY:

Mr. Ray Roder
Whyte, Hirschboeck & Dudek
One East Main Street
Madison, Wisconsin 53701

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Mr. Mark Giesfeldt
Section Chief
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (3 copies)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (3 copies)

DATE:

March, 1995

PERIOD:

February 1 - 28, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ There was no activity on the project during this reporting period. The FS is currently undergoing WDNR review. Activities will resume following WDNR review of the FS.

DATA TRANSMITTED WITH REPORT:

- ◆ None.

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, February 3, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract are as follows:

- ◆ Task 1 - Draft Site Evaluation Report, (September 14, 1992, completed).
- ◆ WDNR approval of Task 1 - Site Evaluation Report (October 1, 1992, completed).
- ◆ Task 1 - Final Draft, Site Evaluation Report, 30 days following WDNR request for draft modifications, if any (not applicable).
- ◆ Task 2 - Draft Work Plans, 60 days following WDNR approval of the Site Evaluation Report, (December 15, 1992 completed).
- ◆ WDNR review of Task 2 - Draft Work Plans (60 days; February 12, 1993, completed).
- ◆ Task 2 - Revised Work Plans (March 19, 1993, completed).
- ◆ WDNR approval of revised work plans (March 31, 1993, completed).
- ◆ Target compound shortlist recommendation (August 25, 1993, completed).
- ◆ Technical Memorandum #1 (October 20, 1993, completed).
- ◆ Recommendations for additional well locations (January 12, 1994, completed).

Monthly Status Report

Page 3

- ◆ Alternative Array Document (June 15, 1994, completed).
- ◆ RI Report (August 19, 1994, completed).
- ◆ Feasibility Study Report (January 6, 1995, completed).

UPCOMING ACTIVITIES PLANNED:

- ◆ No activities are planned prior to completion of WDNR review of the Feasibility Study.

PERSONNEL CHANGES:

- ◆ None.

MEETINGS:


- ◆ None.

HYDRO-SEARCH, INC.

A Tetra Tech Company

Ripon FF/NN Landfill, #915

February 3, 1995
(304733096/1010)




Mr. Steve Ales
Wisconsin Department of Natural Resources
Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, WI 53711

Dear Mr. Ales:

Enclosed please find three copies of the Monthly Status Report for the Remedial Investigation/Feasibility Study work at Ripon FF/NN Landfill in Ripon, Wisconsin. Should you have any questions or comments, please do not hesitate to call.

Sincerely,

HYDRO-SEARCH, INC.


Judy L. Fassbender
Project Manager

JLF:gf
Enc.

cc: Ray Roder, Rienhart, Boerner, Van Deuren, Norris, Rieselbach, S.C. (1 copy)
Section Chief/Environmental Response and Repair Section (SW/3), WDNR (3 copies)
Jim Kaiser, City of Ripon Department of Public Works (1 copy)
Nelson Olavarria - Cooper Industries (1 copy)

CONTRACT SF-92-01

MONTHLY STATUS REPORT

January, 1995

SITE NAME/ACTIVITY:

Ripon FF/NN Landfill
Ripon, Wisconsin
Remedial Investigation/Feasibility Study

PREPARED BY:

Mr. Ray Roder
Whyte, Hirschboeck & Dudek
One East Main Street
Madison, Wisconsin 53701

Ms. Judy Fassbender
Hydro-Search, Inc.
175 N. Corporate Drive, Suite 100
Brookfield, Wisconsin 53045

PREPARED FOR:

Mr. Mark Giesfeldt
Section Chief
Environmental Repair and
Response Section (SW/3)
Wisconsin Department of
Natural Resources
P.O. Box 7921
Madison, Wisconsin 53707 (3 copies)

Mr. Steve Ales
District Solid and
Hazardous Waste Program Supervisor
Wisconsin Department of Natural
Resources, Southern District Headquarters
3911 Fish Hatchery Road
Fitchburg, Wisconsin 53711 (3 copies)

DATE:

February, 1995

PERIOD:

January 1 - 31, 1995

PROGRESS MADE THIS REPORTING PERIOD:

- ◆ The Feasibility Study was issued to the WDNR on January 6, 1995.

DATA TRANSMITTED WITH REPORT:

- ◆ None.

ANTICIPATED PROBLEMS AND RECOMMENDED SOLUTIONS:

- ◆ No problems are anticipated at this time.

DOCUMENTS SUBMITTED:

- ◆ Monthly Progress Report, January 6, 1995.

TARGET COMPLETION DATE OF ACTIVITIES/DOCUMENTS (ACTUAL DATE):

Target dates for the work schedule adopted as part of the contract are as follows:

- ◆ Task 1 - Draft Site Evaluation Report, (September 14, 1992, completed).
- ◆ WDNR approval of Task 1 - Site Evaluation Report (October 1, 1992, completed).
- ◆ Task 1 - Final Draft, Site Evaluation Report, 30 days following WDNR request for draft modifications, if any (not applicable).
- ◆ Task 2 - Draft Work Plans, 60 days following WDNR approval of the Site Evaluation Report, (December 15, 1992 completed).
- ◆ WDNR review of Task 2 - Draft Work Plans (60 days; February 12, 1993, completed).
- ◆ Task 2 - Revised Work Plans (March 19, 1993, completed).
- ◆ WDNR approval of revised work plans (March 31, 1993, completed).
- ◆ Target compound shortlist recommendation (August 25, 1993, completed).
- ◆ Technical Memorandum #1 (October 20, 1993, completed).
- ◆ Recommendations for additional well locations (January 12, 1994, completed).

- ◆ Alternative Array Document (June 15, 1994, completed).
- ◆ RI Report (August 19, 1994, completed).
- ◆ Feasibility Study Report (January 6, 1995, completed).

UPCOMING ACTIVITIES PLANNED:

- ◆ No activities are planned prior to completion of WDNR review of the Feasibility Study.

PERSONNEL CHANGES:

- ◆ None.

MEETINGS:

- ◆ None.
