

---

**ANNUAL  
OPERATION & MAINTENANCE REPORT**  
October 1999 Through September 2000

---

**N.W. MAUTHE  
GROUNDWATER TREATMENT SYSTEM**  
Appleton, Wisconsin

Prepared For The  
**WISCONSIN DEPARTMENT OF NATURAL RESOURCES**

RECEIVED  
MAR 15 2001  
WDNR  
NER - APPLETON




---

**Midwest Contract Operations, Inc.**

January 19, 2001  
Revised March 2, 2001  
MCO. No. M050-90728.16  
JMS:smd

File



State of Wisconsin \ DEPARTMENT OF NATURAL RESOURCES

Scott McCallum, Governor  
Darrell Bazzell, Secretary

Appleton Field Station  
Agricultural Services Center  
3369 W. Brewster Street  
Appleton, Wisconsin 54914-1602  
Telephone 920-832-1803  
FAX 920-832-1800

March 19, 2001

Mr. Dion Novak, RPM  
U.S. EPA, HSRM-6J  
77 W. Jackson Blvd.  
Chicago, IL 60604-3590

Subject: Annual Operation and Maintenance Report, October 1999 through September 2000, N.W. Mauthe Superfund Site, 725 S. Outagamie Street, Appleton, Wisconsin, WDNR BRRTS ID# 02-45-000127

Dear Dion:

Please find enclosed a copy of the annual operation and maintenance report for the N.W. Mauthe Superfund Site. This report contains summaries of the operation and maintenance activities at the plant as well as the results from continuing groundwater and effluent monitoring for the period of October 1999 through September 2000. WDNR's contractor for operation and maintenance activities at the site prepared this report. Please call me at (920) 832-1803 if you have any questions.

Sincerely,

Jennifer Huffman, P.G.  
Hydrogeologist  
Remediation and Redevelopment Program

Enclosure

Cc: Gary Edelstein/Marie Stewart – RR/3 (w/Enclosure)





## Midwest Contract Operations, Inc.

P.O. BOX 418 MENASHA, WI 54952-0418 PH 414-751-4299 FAX 414-751-4284

January 19, 2001

**Revised March 2, 2001**

Ms. Jennifer Huffman  
Wisconsin Department Of Natural Resources  
3369 West Brewster Street  
Appleton, WI 54912-1602

Re: N.W. Mauthe Groundwater Treatment System  
Appleton, Wisconsin  
Annual Operation & Maintenance Report  
MCO. No. M050-90728.16

Dear Ms. Huffman:

Enclosed, please find Midwest Contract Operations, Inc.'s "Annual Operation & Maintenance Report" for the N.W. Mauthe Groundwater Treatment System, 725 South Outagamie Street, Appleton, Wisconsin.

This report includes a site history, a summary of treatment system performance and monitoring, a summary of compliance sampling and reporting, operation and maintenance activities over the last year, and conclusions and recommendations for the site.

If you have any questions or require additional information, feel free to contact me.

Very truly yours,

MIDWEST CONTRACT OPERATIONS, INC.


John M. Stoeger  
Project Manager

JMS:smd


Enclosure: "Annual Operation & Maintenance Report"


**PROFESSIONAL QUALIFICATIONS STATEMENT**

I, Thomas J. Kispert, hereby certify I am a Registered Professional Engineer in the State of Wisconsin, registered in accordance with the requirements of ch. A-E-4, Wisconsin Administrative Code; that this document has been prepared in accordance with the Rules of Professional Conduct in ch. A-E 8, Wisconsin Administrative Code; and that, to the best of my knowledge, all information contained in this document is correct and the document was prepared in compliance with all applicable requirements of chs. NR 700 to 726, Wisconsin Administrative Code.”


  
Thomas J. Kispert, P.E., C.C.S. / P.E. No. E-26225  
Senior Project Engineer

1-24-01  
Date




  
[Stamp] 1-24-01

“I, Stuart A. Boerst, hereby certify that I am a Hydrogeologist, as the term is defined in s.NR 712.03(1), Wisconsin Administrative Code, and that, to the best of my knowledge, all of the information contained in this document is correct and the document was prepared in compliance with all applicable requirements of chs. NR 700 to 726, Wisconsin Administrative Code.”

  
Stuart A. Boerst, P.S., P.H.  
Hydrogeologist

1/24/01  
Date



  
[Stamp] 1/24/01

---

**ANNUAL  
OPERATION & MAINTENANCE REPORT  
October 1999 Through September 2000**

---

**N.W. MAUTHE  
GROUNDWATER TREATMENT SYSTEM  
Appleton, Wisconsin**

Prepared For The  
**WISCONSIN DEPARTMENT OF NATURAL RESOURCES**

Prepared By  
Midwest Contract Operations, Inc.

January 19, 2001

**March 2, 2001**

MCO. No. M050-90728.16

**Table Of Contents**

---

- I. SITE BACKGROUND
  
- II. BATCH TREATMENT PROCESS
  - A. Groundwater Treatment System
  - B. Permit Monitoring & Reporting
    - 1. Monthly Reporting
    - 2. Quarterly & Semi-Annual Reporting
  - C. Compliance Sampling
  - D. Routine Operation & Maintenance Activities
    - 1. Daily Site Inspections
    - 2. Weekly Operation & Maintenance Activities
    - 3. Monthly Operation & Maintenance Activities
    - 4. Annual Operation & Maintenance Activities
    - 5. Periodic Operation & Maintenance Activities
  - E. Significant Operation & Maintenance Activities
  - F. Emergency Operation Shut Downs
  
- III. GROUNDWATER SAMPLING
  - A. Groundwater Sampling Procedures
  - B. Groundwater Sampling Results
  
- IV. GROUNDWATER COLLECTION SYSTEM
  - A. Collection Trenches
  
- V. CONCLUSIONS & RECOMMENDATIONS

## Table Of Contents

---

### List Of Figures

- Figure #1 - Site Location Map
- Figure #2 - Collection Trench & Monitoring Well Locations
- Figure #3 - Groundwater Monitoring Wells Locations & Groundwater Contours
- Figure #4 - Piezometer Locations & Piezometric Contours
- Figure #5 - Isoconcentration Map – Total Chromium ug/l in Groundwater

### List Of Tables

- Table #1 - City Of Appleton Effluent Compliance Limits / Effluent Point 001
- Table #2 - Batch Discharges / October 1, 1999 Through September 30, 2000
- Table #3 - Laboratory Analytical Results / Effluent Point 001
- Table #4 - Laboratory Analytical Results / Selected Metals
- Table #5 - Laboratory Analytical Results / VOC's
- Table #6 - Groundwater Elevation

### List Of Appendices

- Appendix A - Concentration Versus Time Graphs  
Inorganic Compounds / All Wells
- Appendix B - Concentration Versus Time Graph  
Detected VOC Compounds At MW-107
- Appendix C - Groundwater Elevations Versus Time / All Wells
- Appendix D - Operation & Maintenance Cost Summary
- Appendix E - Operation & Maintenance Report / Form 4400-194
- Appendix F - Weekly Hexavalent Chromium Concentrations

---

---

**ANNUAL  
OPERATION & MAINTENANCE REPORT**  
October 1999 Through September 2000

---

---

**N.W. MAUTHE  
GROUNDWATER TREATMENT SYSTEM**  
Appleton, Wisconsin

Prepared For The  
**WISCONSIN DEPARTMENT OF NATURAL RESOURCES**

Prepared By  
Midwest Contract Operations, Inc.

January 19, 2001  
**Revised March 3, 2001**  
MCO. No. M050-90728.16

---

**I. SITE BACKGROUND**

The N.W. Mauthe site is a former electroplating facility, located at 725 South Outagamie Street, Appleton, Wisconsin (Refer to Figure #1, Site Location Map). The property was used for a chrome plating company, from 1960 until 1976. Electroplating of zinc, cadmium and, possibly, copper and silver was conducted from 1978 to 1987 in an adjacent building on the same property. After 1987, all plating operations ceased on the property.

Concerns over sub-surface discharges to the surrounding environment led the Wisconsin Department of Natural Resources (DNR) and United States Environmental Protection Agency (USEPA) to conduct a remedial investigation and clean up of the N.W. Mauthe site and surrounding properties.

The investigation determined the N.W. Mauthe site was contaminated with zinc, cadmium, chromium and cyanide. Additionally, several volatile organic compounds (VOC's) were also present.

Based upon the findings of the remedial investigation, the following actions were taken to remediate the N.W. Mauthe site and adjacent properties of the sub-surface contamination.

- A. Demolition and removal of the buildings on the N.W. Mauthe property.
- B. Excavation and off-site treatment of soils with a total chromium concentration of greater than 500 mg/kg.
- C. Backfilling of the excavation with clean soils, capping the site with 2-feet of clay and topsoil, and the establishment of vegetative cover.
- D. Installation of groundwater collection trenches and construction and operation of a groundwater treatment facility to contain and/or control groundwater contamination with ultimate compliance with groundwater Applicable or Relevant and Appropriate Requirements (ARAR's).
- E. Improvement or installation of foundation drain systems and cleaning, painting or sealing of basement walls and floors, as needed, for homes or businesses in the area of the site, to prevent seepage of contaminated water into the buildings.

The groundwater collection trench system, the location of sump pump and drain connections, and the groundwater monitoring wells and piezometers associated with the site are shown in Figure #2.

Midwest Contract Operations, Inc. (MCO) began operating the groundwater treatment system in February 1997. CH<sub>2</sub>M Hill, the site engineer and project manager for the U.S. EPA, retained responsibility for the overall site operations and the groundwater monitoring wells associated with the treatment system.

The objectives of the collection and treatment system are to reduce the contaminant concentrations in the groundwater to achieve federal drinking water standards and/or state groundwater quality standards, whichever are more stringent.

In October 1998, after the first year of operation and maintenance of the remediation system, the Wisconsin DNR assumed the responsibility from the U.S. EPA for all operation and maintenance of the site. MCO was retained by the Wisconsin DNR for the operation and maintenance of the entire groundwater treatment system, including the groundwater monitoring wells. As of September 2000, MCO has completed eight rounds of groundwater sampling and is operating the batch treatment process, which is designed to remove chromium from the groundwater. A description of the batch process will be discussed later in this report.

//



## II. BATCH TREATMENT PROCESS

### A. Groundwater Treatment System

As part of the remediation phase at the N.W. Mauthe site, a groundwater collection system was installed on and adjacent to the N.W. Mauthe property. Approximately 1,000 lineal feet of coarse sand filled trenching was installed to draw groundwater from the contaminated areas to two collection sumps. From the collection sumps, groundwater is pumped to a 9,000 gallon holding tank, located within the treatment building.

Each batch of groundwater to be treated is pumped from the storage tank to the reaction tank. The batch process treatment system utilizes ferrous sulfate and caustic additions to treat the contaminated groundwater. Through chemical addition, mixing, aeration and settling, the chromium is removed from the groundwater. The fully automated process treats approximately 2,600 gallons per batch (based on physical tank measurements) and is capable of treating four batches per day.

Treated groundwater decants from the reaction tank to the City of Appleton sanitary sewer system. The chromium containing sludge settles to the bottom of the reaction tank. Excess sludge is pumped to a sludge storage tank, also located within the treatment building.

During each discharge, the effluent is tested for hexavalent chromium using a Hach Test kit. The pH is recorded off two meters, located in the reaction tank. The pH values from the two meters are recorded during discharge as the high and low pH values on a daily log sheet. The average of the two pH values is calculated. The effluent wastewater is tested quarterly for total chromium at a DNR approved environmental laboratory.

### B. Permit Monitoring & Reporting

The discharge from the groundwater treatment system is tested for hexavalent chromium during each batch discharge using a Hach Hexavalent Chromium test kit. The effluent discharge is also tested quarterly at a DNR certified laboratory and annually for the parameters listed in Table #1. The effluent limits established by the City of Appleton Wastewater Treatment Plant are outlined in the City of Appleton Industrial User Permit, No. 00-21, and are included in Table #1. The permit was reissued by the City of Appleton on June 9, 2000. The only significant change to the permit requirements was the elimination of the annual flow meter calibration requirements and addition of the confirmation of the proper

operation of the flow meter signal converter. The reporting requirements for compliance with the City of Appleton Industrial User Permit and the Wisconsin DNR are summarized below.

**1. Monthly Reporting**

Monthly reports are submitted to the City of Appleton Wastewater Treatment plant. The reports include total flows for the month, individual batch flows, high, low and average pH of each batch and Hexavalent Chromium concentrations (as measured with a Hach test kit) of each batch. A summary of the batch discharges for this period are contained in Table #2. For the time period covered by this report, there were no exceedances of the effluence discharge limits.

Additionally, the Wisconsin DNR is provided with a monthly report summarizing operations at the site. The monthly reports include MCO's operating invoice for the month, a copy of the City of Appleton monthly report, a list of invoices paid during the month, and a copy of the facility log. Also included in this report is a narrative of any alarm call-outs or non-routine occurrences at the site.

**2. Quarterly & Semi-Annual Reporting**

Quarterly reports are submitted to the Wisconsin DNR and the City of Appleton covering the time periods of October through December, January through March, April through June, and July through September.

Semi-annual reporting consists of submittal of Wisconsin DNR Form 4400-194 with the March Quarterly Report and completion of a Semi-Annual Operation & Maintenance Report for the year ending September 30, 2000. The September report includes a summary of routine operation and maintenance activities at the site, the analytical results and reporting for the groundwater monitoring and treatment system effluent, the collection and treatment performance and effectiveness, an operation and maintenance cost summary, and recommendations.

The quarterly reports include site background, a description of the treatment process and analytical results, groundwater sampling procedures and results, a discussion of public contacts, applicable operation and maintenance activities, and MCO's conclusions and recommendations. A summary of the reported quarterly and annual discharge concentrations

are shown in Table #3. The discharges for this period have consistently met the discharge limitations.

**C. Compliance Sampling**

Compliance sampling of the treatment system effluent is conducted twice per year by the City of Appleton. The samples were collected on February 15, 2000 and September 28, 2000. The effluent is analyzed for all the parameters listed in Table #1, except for Hexavalent Chromium.

MCO collects one compliance sample from the outfall during the first quarter of each year. The sample was collected on March 13, 2000. The MCO collected sample is analyzed for all of the parameters in Table #1.

A summary of the compliance sampling results from Outfall 001 are contained in Table #3. The laboratory analytical data was previously submitted in the quarterly DNR reports. During the period from October 1, 1999 through September 30, 2000, there were no exceedances of the City of Appleton Industrial User Discharge Permit.

**D. Routine Operation & Maintenance Activities**

Completed operations log sheets are kept on file at the groundwater treatment facility for all of the operation and maintenance activities listed below.

**1. Daily Site Inspections**

A daily inspection of the facility is required to check the nitrogen cylinder, which provides a blanket of nitrogen gas in the ferrous sulfate drum. The pressure at the nitrogen tank and the total flow from the flow totalizer are recorded daily and/or after each batch discharge. Additionally, a walk through of the building is conducted to check for any obvious equipment problems. The site activities are documented on daily log sheets and a daily checklist.

**2. Weekly Operation & Maintenance Activities**

The following activities are conducted on a weekly basis, normally on Wednesday of each week.

- a. Test influent chromium concentration in storage tank, utilizing a Hach test kit. The Chromium concentration is entered into the

programmable logic controller (PLC), which uses the figure to calculate the required ferrous sulfate additions per batch.

- b. Record water levels in the two collection sumps.
- c. Record pump operating pressure levels.
- d. Record liquid levels in the storage tank and sludge storage tank. Record the sludge depth in the reaction tank and adjust if not within the minimum or maximum levels needed for desired coprecipitation.
- e. Record weights of ferrous sulfate and caustic drums.
- f. Calibrate or clean pH meters in the reaction tank. Meters are calibrated approximately once per month, depending upon the drift between the two probes. The system Operation & Maintenance Manual had required weekly calibration of the pH probes. Over the first year of system operation, MCO found that the pH meters remained in calibration and did not require re-calibration on a weekly basis. MCO consulted with the equipment manufacturer's Operation & Maintenance Manual, and determined a weekly probe cleaning and monthly calibration was recommended. Since October 1998, MCO has followed the manufacturer's recommended probe maintenance schedule.

The weekly checks are documented on log sheets, which are kept on file at the treatment facility.

### 3. **Monthly Operation & Maintenance Activities**

The following activities are performed each month, generally near the first of the month.

#### a. Top Mounted Mixers

The oil level in the mixers is checked and the seals are observed for obvious leaks. The motor bearings are greased monthly. Top mounted mixers are located in the storage tank, reaction tank and sludge storage tank.

b. Chemical Feed Pumps

The ferrous sulfate and caustic feed pumps are checked for proper operation. The feed lines and valves are checked for signs of leakage. Upon installation of each new chemical drum, hot water is pumped through the chemical feed system to clean out the supply piping. This is performed approximately four times per year on each feed system. Due to the nature of groundwater flows, the lines are cleaned more during the spring and fall wet weather periods and not on a quarterly schedule, as specified in the Operation & Maintenance Manual. The spill containment sump below the drums is topped off with water to the level of the stand pipe.

c. Double Diaphragm Pumps

The most used double diaphragm pump is used for pumping water from the storage tank to the reaction tank. Additional pumps are used to pump sludge from the reaction tank to the sludge storage tank and from the sludge storage tank to the truck loading station. Each pump is operated as part of the monthly maintenance and checked for unusual noise and proper lubrication. The lubrication oil is filled and the water trap is drained, as needed.

d. Air Compressor

The compressor oil level is checked. The air filter is checked and changed, as needed. The compressor is run under full load and the on panel gauges are checked for proper operation. The oil filter is changed, as needed.

e. Unit Heaters

The unit heaters are checked during cold weather for proper operation, excessive noise and vibration. The heaters are shut-off in spring and turned on in the fall.

f. Air Conditioner

The facility heater / air conditioner is checked for proper operation and the air filter is cleaned, as-needed.

g. Water Heater

The water heater is checked for any visible leaks. The relief valve is tested for proper operation. Between 1 and 2-quarts of water are drained from the tank monthly.

h. Ceiling Fans

The ceiling fans are checked for excessive vibration or dirt build-up.

i. Safety Shower

The safety shower is tested monthly for proper operation.

4. **Annual Operation & Maintenance Activities**

The following activities are performed on an annual basis.

- a. The unit heaters are cleaned and test fired. This will normally occur in September of the year. The Operation & Maintenance Plan for the facility calls for lubrication of the heater motors. The actual maintenance of the heaters deviates from the Operation & Maintenance Plan because the moving parts on the heaters have sealed bearings and do not require lubrication.
- b. The submersible pumps in the two collection sumps and building sump are removed and the lubricating oil changed. The Operation & Maintenance Plan for the facility calls for replacement of the mechanical seal, oil filter, plug gasket and o-rings be replaced annually. A visual observation of the condition of the oil is done to verify the integrity of the pump seals. If no water is noted in the removed pump oil, the seals and o-rings are not changed. The oil in the two pumps was changed on September 27, 2000. MCO found water in the oil of the Sump #1 pump. The pump was removed and replaced with the spare pump. In 2001, the refurbished pump will replace the pump in Sump #2, which will be sent in for refurbishment. The pumps will be removed and refurbished every 2-years.

- c. The air compressor oil and filter are changed.
- d. The ceiling fan blades are cleaned during the September operation and maintenance activities.
- e. The Operation & Maintenance Manual requires the top mounted mixer gear oil be changed annually. MCO deviated from the plan by performing a monthly visual inspection of the oil for any obvious breakdown. The Wisconsin DNR case manager has required the oil be changed annually. This will be performed when the sump pump maintenance is performed each fall.

## 5. Periodic Operation & Maintenance Activities

The following activities are performed on an as-needed basis throughout the year.

- a. Lawn mowing and snow removal is conducted as required.
- b. The ferrous sulfate chemical feed pump calibration is verified prior to installation of a new 55-gallon drum. The sodium hydroxide pumping system is not calibrated because the pump is controlled by the reaction tank pH and not by volume.
- c. The ferrous sulfate and caustic chemical feed lines are cleaned prior to installation of new 55-gallon drums. The cartridge valves are changed, as needed.
- d. The water traps are emptied and oil reservoirs checked for the air pumps prior to each use.
- e. Level sensing meters in the storage tank, reaction tank and sludge storage tank are compared with actual tank levels by visual observations.
- f. The effluent flow meter operation is checked during each discharge. According to the factory representative, there are no operator performed calibration functions for the flow meter, unless a hardware failure occurs.

**E. Significant Operation & Maintenance Activities**

The following significant operation and maintenance activities were performed between October 1, 1999 and September 30, 2000.

1. On May 16, 2000, the gear box lubricating oil on the three top-mounted mixers was changed.
2. On July 12, 2000, two air line drains were installed on the compressed air lines.
3. On July 24, 2000, the Panel View control panel light was replaced.
4. On August 9, 2000, several small leaks in the nitrogen system were repaired.
5. On September 6, 2000, filters in the ferrous sulfate pump were changed and the pump was cleaned.
6. On September 11, 2000, the stab bar for the building sump pump was replaced.
7. On September 27 and 28, 2000, the oil was changed in the two lift station sumps and the building sump. Water was discovered in the oil of the Lift Station #1 sump pump. The pump was removed and replaced with the spare pump. The removed pump was returned to the factory for reconditioning.

**F. Emergency Operation Shut Downs**

There was no emergency shut-downs during the reporting period.



### III. GROUNDWATER SAMPLING

#### A. Groundwater Sampling Procedures

A total of 11 groundwater monitoring wells are associated with the groundwater treatment system and are sampled quarterly to determine the groundwater quality conditions at the site. Additionally, four piezometers were installed to measure the effectiveness of the groundwater collection trench system.

Groundwater levels are measured in the monitoring wells and the piezometers, relative to the north side of the top of the well casing. The latest round of groundwater monitoring well and piezometer groundwater readings and contours are shown in Figures #3 and #4. The groundwater elevation versus time graph is contained in Appendix C.

The 11 groundwater monitoring wells are sampled in March, June, September and December of each year. A dedicated 12-volt submersible pump is installed in each well. Water level measurements are collected from each monitoring well prior to sampling. Each well is slowly pumped dry and allowed to recharge for approximately 3-hours. The wells are then pumped dry again, allowed to recharge and then sampled. Two duplicate samples are also collected as a quality control measure. Purge water from the wells is collected and dumped into the collection sumps.

The sampling process utilizes a flow through cell to read the pH, temperature, conductivity, redox potential and dissolved oxygen in each well. The flow through cell consists of a 1-liter laboratory beaker placed over a 5-gallon bucket. Flow through the cell is maintained at approximately 250 ml/min. utilizing a resistor to control pump flow. The same approximate flow rate is maintained for purging and sampling. Groundwater samples are collected upon stabilization of the conductivity in each monitoring well or after each well has been pumped dry twice. The pH, conductivity, redox potential and dissolved oxygen readings for each monitoring well are recorded upon stabilization of the conductivity. The groundwater samples are then collected in the order of VOC vials first and metal samples second. The metal samples are not filtered. The laboratory containers supplied for metals analysis included NaOH and HNO<sub>3</sub> as preservatives. The collected samples are submitted to Northern Lake Service, Inc., Crandon, Wisconsin. The collected samples are analyzed for cyanide, selected metals and Volatile Organic Compounds (VOC's), as specified by the Wisconsin DNR. As of the December 15, 1999 sampling event, copper, cyanide, mercury and zinc analysis was discontinued for all eleven (11) monitoring wells. Alkalinity and

ferrous iron testing was conducted using field Hach test kits. VOC analysis has been reduced to annually for all wells, except MW-107. VOC testing at MW-107 will remain quarterly.

## **B. Groundwater Sampling Results**

The collected groundwater samples are analyzed for cadmium, chromium, manganese and VOC's (when required). Additionally, field analysis is conducted at each well for pH, temperature, conductivity, dissolved oxygen, Redox potential, alkalinity and ferrous iron. The field analysis sampling results will track the ability of the VOC groundwater contamination to naturally bio-remediate at the site.

The laboratory analytical results indicate that levels of total chromium exceed the DNR NR 140.10 Groundwater Enforcement Standards in monitoring wells MW-103, MW-104 and MW-107. MW-107 is the closest down-gradient well to the remediation building. Additionally, VOC compounds in MW-107 have been detected in excess of either the NR 149.21(9) maximum contaminant levels (MCL's) or the NR 140.10 Groundwater Enforcement Standards (ES). Exceedances of the MCL and ES for manganese have been found in all of the groundwater wells since sampling began in February 1997. These exceedances also appear in the background wells (W-2 & MW-108) which would indicate that the high levels of manganese in the groundwater occurs naturally.

A review of the laboratory analytical and groundwater flow data does not indicate any significant seasonal changes in the analytical results or groundwater flow direction. Overall, concentrations of organic and inorganic compounds appear to be decreasing.

The laboratory analytical results are contained in Tables #4 and #5. As of December 15, 1999, copper, cyanide, mercury and zinc analysis was discontinued on the monitoring well samples. Graphs of the contaminant concentrations over time for the analyzed inorganic compounds are contained in Appendix A. For graphing purposes, analytical results below the laboratory LOD were listed at half the analytical laboratory's method detection limit. A graph of the detected VOC compounds at MW-107 over time is contained in Appendix B. An Isoconcentration map for total chromium is shown in Figure #5.

The effectiveness of the existing groundwater treatment system towards meeting the clean-up goals in the groundwater will require analysis of data over an extended period of time to evaluate trends in metals and VOC reductions. Based

upon the current analytical results, concentrations are generally stable, except in the source areas.

#### IV. GROUNDWATER COLLECTION SYSTEM

##### A. Collection Trenches

The groundwater collection system utilizes approximately 1,000 linear feet of coarse sand filled trenching, which was installed to draw groundwater from the contaminated areas to two collection sumps. Collection Sump #1, designated Manhole #1 on the site map and located at the southwest corner of the property, collects flows from below the Miller Electric parking lot and the south end of the Mauthe property.

Collection Sump #2, designated Manhole #2, on the site map and located along Outagamie Street south of the railroad tracks, collects flows from the triangular area bounded by the railroad tracks, Outagamie Street and Second Street.

Piezometric groundwater levels in the area of the trenching indicate that the trenches are creating a capture zone, which directs groundwater to the collection trench system. Based upon the groundwater elevation data, the capture zone acts as containment for the existing contaminant plume.

Groundwater flows from the Mauthe site tend to flow southwest toward the collection trenches. Groundwater flow from the properties south of the railroad tracks flow in a northerly direction during periods of lower groundwater elevations and northeasterly in periods of higher groundwater elevations. In both cases, the flows are captured by the collection trench system. A summary of the historical groundwater elevations is shown in Table #6.

Foundation drains at 1410 and 1414 West Second Street and 801 South Outagamie Street are connected to the collection trench system. Additionally, the sump pump at 1428 West Second Street is connected to the system. During the operation and maintenance period from October 1, 1999 through September 30, 2000, there were no reported problems with the foundation drains on any of the connected drain systems.

#### V. CONCLUSIONS & RECOMMENDATIONS

The latest round (September 27, 2000) of groundwater samples collected from the 11 monitoring wells, indicates residual chromium contamination above the DNR NR 140.10

ES exists in monitoring wells MW-103, MW-104 and MW-107. Additionally, VOC compounds in excess of the NR 140.10 ES or the NR 149.21(9) maximum contaminant levels (MCL's) were detected in MW-107. High levels of manganese, noted historically in all wells, appears to occur naturally and may not be related to the past site uses.

A review of the groundwater flow patterns over the last year indicates the groundwater collection trench system is creating a capture zone that prevents the contamination plume from expanding and directs the groundwater to the trenching and, ultimately, the remediation system.

There have been no exceedances of the City of Appleton Industrial Discharge Permit for the treated effluent. The influent and effluent from the facility are sampled and analyzed to monitor the treatment process and confirm compliance with the discharge permit. The plant is operated and maintained to consistently meet the standards set by the City of Appleton POTW. The hexavalent chromium analysis was mistakenly omitted from the March 13, 2000 laboratory analytical request and, therefore the hexavalent chromium test was not run. The total chromium for the March 13, 2000 effluent sample was .14 mg/l. This is well below the City of Appleton Wastewater Treatment Facility effluent limits for total chromium and hexavalent chromium. Hexavalent chromium will be run with the March 2001 analysis.

Data collected to date shows stable concentrations in the groundwater monitoring wells, with the exception of wells MW-103, MW-104 and MW-107. The effectiveness of the treatment system, in meeting the groundwater clean-up goals, will require additional data over time to evaluate the trends in organic and inorganic compound reductions.

Based upon the results of the September 27, 2000 groundwater sampling results and the batch treatment process analytical results, MCO recommends continued operation of the groundwater treatment system at the N.W. Mauthe groundwater remediation site.

MCO has included an operation and maintenance cost summary for the site in Appendix D. The Wisconsin DNR Operation & Maintenance Report Form 4400-194 is contained in Appendix E. A summary of the influent hexavalent chromium concentrations, as measured with a Hach Kit, are included in Appendix F.

**Table #1**

**CITY OF APPLETON EFFLUENT COMPLIANCE LIMITS**  
**Effluent Point 001**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
**MCO No. M050-90728.16**

	<b>Aluminum</b> (mg/l)	<b>Arsenic</b> (mg/l)	<b>Cadmium</b> (mg/l)	<b>Chromium Total</b> (mg/l)	<b>Copper</b> (mg/l)	<b>Cyanide</b> (mg/l)	<b>Lead</b> (mg/l)	<b>Mercury</b> (mg/l)	<b>Nickel</b> (mg/l)	<b>Zinc</b> (mg/l)	<b>Hexavalent Chromium</b> (mg/L)
Effluent Limits Permit #00-21	70	1.0	0.3	7.0	3.5	1.0	2.0	0.002	2.0	10.0	4.5

mg/l = milligram / liter  
ug/l = microgram / liter

**Table #2**

**BATCH DISCHARGES**  
**October 1, 1999 Through September 30, 2000**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
**MCO No. M050-90728.16**

<b>Month</b>	<b>Monthly (gallons)</b>	<b>Quarterly Flow (gallons)</b>
October 1999	18,905	
November 1999	22,070	63,081
December 1999	22,106	
January 2000	29,116	
February 2000	44,213	124,613
March 2000	51,284	
April 2000	75,716	
May 2000	110,193	311,266
June 2000	125,357	
July 2000	72,347	
August 2000	69,323	249,346
September 2000	107,676	
<b>TOTAL</b>	<b>748,306</b>	

Table #3

**LABORATORY ANALYTICAL RESULTS**  
**Effluent Point 001**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
MCO No. M050-90728.16

Sample Name	Sample Date	Aluminum (mg/l)	Arsenic (mg/l)	Cadmium (mg/l)	Chromium Total (mg/l)	Copper (mg/l)	Cyanide (mg/l)	Lead (mg/l)	Mercury (mg/l)	Nickel (mg/l)	Zinc (mg/l)	Hexavalent Chromium (mg/L)
Outfall 001*	02/20/97	<.02	<.003	<.00050	0.0400	<.01	<.00001	<.005	<.0002	<.005	0.0051	<.01
Outfall 001*	05/27/97	NA	NA	NA	0.2600	NA	NA	NA	NA	NA	NA	NA
Outfall 001*	09/11/97	NA	NA	NA	0.5570	NA	NA	NA	NA	NA	NA	NA
Outfall 001*	12/12/97	NA	NA	NA	0.2790	NA	NA	NA	NA	NA	NA	NA
Outfall 001*	03/24/98	0.0152	<.002	<.00004	0.0637	<.0095	<.0017	<.0006	<.000015	<.0095	0.0046	0.1000
Outfall 001**	04/29/98	<.011	<.002	<.005	0.2200	<.05	0.0020	<.1	<.0002	<.04	<.005	NA
Outfall 001*	06/10/98	NA	NA	NA	0.0784	NA	NA	NA	NA	NA	NA	NA
Outfall 001**	10/07/98	<.011	<.002	0.0050	0.1700	<.05	<.001	<.1	<.0002	<.04	0.0250	NA
Outfall 001***	10/27/98	NA	NA	NA	0.0940	NA	NA	NA	NA	NA	NA	NA
Outfall 001***	02/09/99	NA	NA	NA	0.1600	NA	NA	NA	NA	NA	NA	NA
Outfall 001***	03/18/99	<.009	<.003	<.00031	NA	.00068****	<.000032	<.0024	<.00005	.00351****	<.012	<.0036
Outfall 001**	03/18/99	<.011	<.002	<.005	<.05	<.05	0.0010	0.1000	<.00005	0.0400	0.0180	NA
Outfall 001***	06/08/99	NA	NA	NA	0.1900	NA	NA	NA	NA	NA	NA	NA
Outfall 001***	09/13/99	NA	NA	NA	0.1700	NA	NA	NA	NA	NA	NA	NA
Outfall 001**	09/21/99	<.011	<.002	<.005	<.05	<.05	0.0030	<.1	<.00015	<.04	0.0080	NA
Outfall 001***	12/15/99	NA	NA	NA	0.0870	NA	NA	NA	NA	NA	NA	NA
Outfall 001**	02/15/00	<.015	<.0020	<.005	0.0900	<.05	<.001	<.1	<.00013	<.04	0.0280	NA
Outfall 001***	03/13/00	<.009	<.003	<.00031	0.1400	<.0006	<.0044	<.0024	<.00005	0.0012	<.012	NA
Outfall 001 ***	06/22/00	NA	NA	NA	0.2400	NA	NA	NA	NA	NA	NA	NA
Outfall 001***	09/27/00	NA	NA	NA	0.5100	NA	NA	NA	NA	NA	NA	NA
Effluent Limits Permit #00-21		70.0000	1.0000	0.3000	7.0000	3.5000	1.0000	2.0000	0.0020	2.0000	10.0000	4.5000

mg/l = milligram / liter

ug/l = microgram / liter

NA = not analyzed

\* = Sampled by CH2M Hill

\*\* = Sampled by the City of Appleton

\*\*\* = Sampled by MCO

\*\*\*\* = Detected of compound in area of less certain quantitation.

Table #4

**LABORATORY ANALYTICAL RESULTS / Selected Metals**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
MCO No. M050-90728.16

Well Name	Sample Date	Cadmium (ug/l)	Chromium (ug/l)	Copper (ug/l)	Cyanide (ug/l)	Manganese (ug/l)	Mercury (ug/l)	Zinc (ug/l)
W-2	02/20/97	NA	15	26	NA	460.0	NA	49
	05/27/97	0.43	8.5	<10	NA	170.0	<.2	30
	09/18/97	0.27	4.5**	9.5**	3**	116.0	<.03	16.9
	12/12/97	.13*	6.2	<9.7	<.8	133.0	.06*	20.4
	03/25/98	0.08	<3.9	<9.5	<1.7	83.8	.007*	18.6
	06/10/98	.31*	16.4	18.6**	<1.7	466.0	.027*	40.8
	10/27/98	.51*	3.60	4.7*	<.0032	69.0	<.05	170
	02/09/99	.46*	<.62	4.0	<.0032	240.0	<0.05	23
	06/08/99	<.31	<.62	1.8*	<.0032	290.0	<0.05	<12
	09/13/99	<.31	2.00	3.2	<.0032	240.0	<.05	<12
	12/15/99	<.31	.72 *	NA	NA	2.8	NA	NA
	03/13/00	<.31	.79 *	NA	NA	7.8	NA	NA
	06/22/00	<.31	<.62	NA	NA	<.42	NA	NA
	09/27/00	2.70	1.1*	NA	NA	17.0	NA	NA
W-8	02/20/97	NA	17	22	NA	320.0	NA	34
	05/27/97	1.6	37	27	NA	670.0	<.2	54
	09/18/97	0.45	14.4	14.6**	1**	338.0	.11**	31.8
	12/12/97	0.5*	5.7	<9.7	<.8	147.0	.07*	17.1
	03/25/98	0.43	10.1	15**	<1.7	205.0	.007*	21
	06/10/98	0.54	9.9	12.6**	<1.7	264.0	.016*	21.6
	10/27/98	0.80	3.90	4.8*	<.0032	64.0	<.05	85
	02/09/99	<.31	<.62	<60	<.0032	850.0	<.05	12
	06/08/99	<.31	<.62	2.6	<.0032	50.0	<.05	<12
	09/13/99	<.31	1.90	2.7	<.0032	98.0	<.05	29
	12/15/99	<.31	2.80	NA	NA	180.0	NA	NA
	03/13/00	<.31	1.4 *	NA	NA	65.0	NA	NA
	06/22/00	<.31	3.10	NA	NA	74.0	NA	NA
	09/27/00	.27*	.75*	NA	NA	26.0	NA	NA
W-15	02/20/97	NA	32	52	NA	430.0	NA	88
	05/27/97	0.27	5.9	15	NA	97.0	<.2	39
	09/18/97	0.31	13.9	18.8**	<.78	325.0	<.03	35.5
	12/12/97	.12*	5.7	9.7**	<.8	80.9	.03*	18.5
	03/25/98	.04*	<3.9	<9.5	<1.7	85.7	.038*	13.7
	06/10/98	.11*	10	13.2**	<1.7	147.0	.016*	18.8
	10/27/98	.41*	6.80	7.40	<.0032	110.0	<.05	100
	02/09/99	<.31	<.62	<.60	<.0032	320.0	<.05	<12
	06/08/99	<.31	2.40	14.00	<.0032	130.0	<.05	66
	09/13/99	<.31	5.30	6.40	<.0032	130.0	<.05	16
	12/15/99	<.31	5.00	NA	NA	90.0	NA	NA
	03/13/00	<.31	7.00	NA	NA	130.0	NA	NA
	06/22/00	<.31	1.80	NA	NA	11.0	NA	NA
	09/27/00	<.23	4.20	NA	NA	24.0	NA	NA



Table #4

**LABORATORY ANALYTICAL RESULTS / Selected Metals**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
MCO No. M050-90728.16

Well Name	Sample Date	Cadmium (ug/l)	Chromium (ug/l)	Copper (ug/l)	Cyanide (ug/l)	Manganese (ug/l)	Mercury (ug/l)	Zinc (ug/l)
MW-101	02/20/97	NA	36	41	NA	820.0	NA	49
	05/27/97	<.2	10	11	NA	170.0	<.03	18
	09/18/97	.06**	11.9	10.7**	1**	145.0	<.05	18.2
	12/12/97	.06*	12.8	<9.7	<.8	176.0	.05*	20.7
	03/25/98	.04*	20.9	21.6**	<1.7	239.0	.007*	32.7
	06/10/98	.27*	48.2	46.8	<1.7	604.0	.044*	75.9
	10/27/98	<.16	3.20	4.2*	<.0032	24.0	<.05	54
	02/09/99	<.31	<.62	<.60	<.0032	1900.0	<.05	14
	06/08/99	<.31	1.80	8.2	<.0032	380.0	<.05	39
	09/13/99	<.31	2.90	5.1	<.0032	31.0	<.05	<12
	12/15/99	<.31	2.50	NA	NA	9.1	NA	NA
	03/13/00	<.31	2.30	NA	NA	100.0	NA	NA
	06/22/00	<.31	1.4 *	NA	NA	<4.2	NA	NA
	09/27/00	<.23	19.00	NA	NA	37.0	NA	NA
MW-102	02/20/97	NA	26	38	NA	570.0	NA	34
	05/27/97	0.21	48	77	NA	920.0	<.2	73
	09/18/97	.08**	<3.92	6.9**	2**	302.0	<.03	8.7
	12/12/97	.04*	<3.9	<9.7	<.8	387.0	.04*	10.9
	03/25/98	.11*	<3.9	9.5**	<1.7	302.0	.007*	7.4*
	06/10/98	.04*	<3.9	<9.8	<1.7	318.0	.018*	9.5
	10/27/98	.27*	.98*	3.2*	<.0032	340.0	<.05	24
	02/09/99	<.31	.73*	<.60	<.0032	670.0	<.05	20
	06/08/99	<.31	1.2*	5.8	<.0032	140.0	<.05	36
	09/13/99	<.31	4.00	15.0	<.0032	160.0	<.05	73
	12/15/99	<.31	1.2 *	NA	NA	550.0	NA	NA
	03/13/00	<.31	1.70	NA	NA	580.0	NA	NA
	06/22/00	<.31	<.62	NA	NA	310.0	NA	NA
	09/27/00	<.23	2.10	NA	NA	130.0	NA	NA
MW-103	02/20/97	NA	1,300	47	NA	800.0	NA	27
	05/27/97	<.2	160.0	31	NA	900.0	<.2	29
	09/18/97	.06**	35.2	13.5**	3**	287.0	<.03	13.7
	12/12/97	.04*	16.3	<9.7	<.8	84.3	.09*	21.4
	03/25/98	.04*	15.5	<9.5	<1.7	83.0	.007*	7.5*
	06/10/98	.15*	57.6	27.5	<1.7	417.0	.02*	33.7
	10/27/98	<.16	6.30	2.3*	<.0032	27.0	<.05	30.0
	06/08/99	<.31	87.00	3.5	<.0032	810.0	<.05	30
	09/13/99	<.31	720.0	5.9	<.0032	83.0	<.05	15
	12/15/99	<.31	260.0	NA	NA	160.0	NA	NA
	03/13/00	<.31	600.0	NA	NA	79.0	NA	NA
	06/22/00	<.31	130.0	NA	NA	180.0	NA	NA
	09/27/00	<.23	280.0	NA	NA	230.0	NA	NA

Table #4

**LABORATORY ANALYTICAL RESULTS / Selected Metals**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
MCO No. M050-90728.16

Well Name	Sample Date	Cadmium (ug/l)	Chromium (ug/l)	Copper (ug/l)	Cyanide (ug/l)	Manganese (ug/l)	Mercury (ug/l)	Zinc (ug/l)
MW-104	02/20/97	NA	5.9	15	NA	550.0	NA	6.9
	05/27/97	<.02	6.9	11	NA	470.0	<.2	5.2
	09/18/97	<.04	35.6	5**	3**	235.0	<.03	4.74
	12/12/97	.04*	61.8	9.8**	<.8	279.0	.05*	14
	03/25/98	.04*	66.8	<9.5	<1.7	73.6	.008*	7.4*
	06/10/98	.04*	219.0	<9.8	<1.7	107.0	.016*	12.8
	10/27/98	.29*	150.0	2.3*	<.0032	25.0	<.05	30
	02/09/99	<.31	94.0	1.4*	<.0032	1000.0	<.05	<12
	06/08/99	1*	62.0	12.0	<.0032	620.0	<.05	17
	09/13/99	<.31	80.0	3.2	<.0032	9.2	<.05	<12
	12/15/99	<.31	170.0	NA	NA	1.6	NA	NA
	03/13/00	<.31	300.0	NA	NA	13.0	NA	NA
	06/22/00	<.31	210.0	NA	NA	41.0	NA	NA
	09/27/00	<.23	510.0	NA	NA	3.9	NA	NA
MW-105	02/20/97	NA	21	22	NA	1100.0	NA	23
	05/27/97	<.2	5	<10	NA	120.0	<.2	12
	09/18/97	.14**	29.5	28.3	1**	532.0	<.03	46
	12/12/97	.36*	15.8	12.5**	<.8	297.0	.03*	27.1
	03/25/98	.04*	30.8	27.6	<1.7	518.0	.064*	44
	06/10/98	.048*	13.7	15.3**	<1.7	217.0	.016*	22.1
	10/27/98	.29*	8.80	8.20	<.0032	150.0	<.05	70
	02/09/99	<.31	1.3*	4.30	<.0032	2000.0	<.05	19
	06/08/99	<.31	1*	18.00	<.0032	1300.0	<.05	66
	09/13/99	<.31	.64*	24.00	<.0032	1700.0	<.05	30
	12/15/99	<.31	<.62	NA	NA	860.0	NA	NA
	03/13/00	<.31	4.80	NA	NA	660.0	NA	NA
	06/22/00	<.31	1.0*	NA	NA	600.0	NA	NA
	09/27/00	<.23	1.2*	NA	NA	700.0	NA	NA
MW-106	02/20/97	NA	21	24	NA	320.0	NA	26
	05/27/97	<.02	40	35	NA	590.0	<.2	68
	09/18/97	.05**	5.5	6.2**	1**	56.9	<.03	35.6
	12/12/97	.04*	9.2	9.7**	<.08	155.0	.03*	18.4
	03/25/98	NA	13.40	14.4**	<1.7	150.0	.007*	18.5
	06/10/98	.04*	<3.9	10.2**	<1.7	10.0	.016*	10.9
	10/27/98	.27*	3.20	4.3*	<.0032	38.0	<.05	88
	02/09/99	<.31	<.62	1.1*	<.0032	760.0	<.05	22
	06/08/99	<.31	.79*	2.3	<.0032	900.0	<.05	<12
	09/13/99	<.31	1.80	4.7	<.0032	1100.0	<.05	30
	12/15/99	<.31	1.3*	NA	NA	130.0	NA	NA
	03/31/00	<.31	2.30	NA	NA	270.0	NA	NA
	06/22/00	<.31	.73*	NA	NA	<4.2	NA	NA
	09/27/00	<.23	.88*	NA	NA	50.0	NA	NA

**Table #4**

**LABORATORY ANALYTICAL RESULTS / Selected Metals  
N.W. Mauthe Superfund Site - Appleton, Wisconsin  
MCO No. M050-90728.16**

Well Name	Sample Date	Cadmium (ug/l)	Chromium (ug/l)	Copper (ug/l)	Cyanide (ug/l)	Manganese (ug/l)	Mercury (ug/l)	Zinc (ug/l)
MW-107	02/20/97	NA	2,000	13	NA	190.0	NA	6.9
	05/27/97	<.2	3,600	<10	NA	91.0	<.2	10
	09/18/97	<.04	2,670	<8.1	1**	59.3	<.03	33.5
	12/12/97	.04*	2,310	<9.7	<.8	48.4	.1*	6.7
	03/25/98	.04*	11,200*	12.1**	<1.7	68.2	.041*	9.3*
	06/10/98	.11*	6,240	13.8**	<1.7	161.0	.027*	17.3*
	10/27/98	<.16	7,100	1.2*	<.0032	28.0	<.05	94
	02/09/99	<.31	3,200	1.9*	<.0032	49.0	<.05	<12
	06/08/99	<.31	5,800	3.0	<.0032	25.0	<.05	<12
	09/13/99	<.31	4,000	1.9*	<.0032	18.0	<.05	<12
	12/15/99	<.31	14,000	NA	NA	.83 *	NA	NA
	03/13/00	<.31	8,100	NA	NA	22.0	NA	NA
	06/22/00	<.31	14,000	NA	NA	<42	NA	NA
	09/27/00	<.23	11,000	NA	NA	4.9	NA	NA
MW-108	02/20/97	NA	25	23	NA	490.0	NA	31
	05/27/97	<.2	11	13	NA	210.0	<.2	15
	09/18/97	.14**	27.4	22.4**	1**	462.0	<.03	36.6
	12/12/97	.04*	5.6	<9.7	<.8	74.8	.03*	27.9
	03/25/98	.04*	9.4	10.4**	<1.7	142.0	.007*	13.8
	06/10/98	.14*	28.4	25.5	<1.7	478.0	.021*	40.5
	10/27/98	.26*	8.90	7.40	<.0032	88.0	<.05	44
	02/09/99	<.31	1.70	3.90	<.0032	560.0	<.05	30
	06/08/99	<.31	3.10	1.4*	<.0032	450.0	<.05	54
	09/13/99	<.31	4.50	5.30	<.0032	100.0	<.05	<12
	12/15/99	<.31	6.10	NA	NA	79.0	NA	NA
	03/13/00	<.31	3.6	NA	NA	41.0	NA	NA
	06/22/00	<.31	6.5	NA	NA	<4.2	NA	NA
	09/27/00	<.23	2.9	NA	NA	29.0	NA	NA
Maximum Contaminant Level (MCL)		5	100	100	200	50.0	2	5,000
Enforcement Standard Chapter NR 140.10		5	100	1,300	200	50.0	2	5,000
Preventive Action Limit Chapter NR 140.10		0.5	10	130	40	25.0	0.2	2,500

**EXPLANATION:**

Samples collected prior to 10/27/98 were collected by CH2M Hill.

\* = Detection of compound in area of less certain quantification.

\*\* = Compound was found in sample and blank.

ND = Not detected above the analytical laboratories method detection limit

NA = Not Analyzed

MW-104 = Was tested for Aluminum, Nickel, Arsenic & Lead. No quantifiable detections were noted for any of the analytes.

ug/L = Microgram/Liter

mg/L = Milligram / Liter

indicates an exceedance of the NR 140 Groundwater Quality Enforcement Standard

Table #5

LABORATORY ANALYTICAL RESULTS  
Volatile Organic Compounds (VOC's)  
N.W. Mauthe Superfund Site - Appleton, Wisconsin  
MCO No. M050-90728.16

Well Name	Sample Date	Benzene (ug/l)	Chloroform (ug/l)	1,1-Dichloroethane (ug/l)	1,1-Dichloroethene (ug/l)	cis-1,2-Dichloroethene (ug/l)	Trans-1,2-Dichloroethene (ug/l)	Ortho-Xylene (ug/l)	Toluene (ug/l)	1,1,1-Trichloroethane (ug/l)	1,1,2-Trichloroethane (ug/l)	Trichloroethene (ug/l)	Meta, para Xylene (ug/l)	Total Xylenes (ug/l)
W-2	02/20/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	05/27/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	09/18/97	<.5	<.6	<85	<.7	<.7	<.7	<124	<68	<40	<.5	<.5	<124	<.5
	12/12/97	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	03/25/98	<.5	<.6	<85	<.7	<.7	<.7	<.4	<88	<40	<.5	<.5	.4**	<.5
	06/10/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	10/27/98	<.24	<.23	<.27	<.28	<.27	<.26	<.17	<.21	<.26	<.23	<.29	<.36	<.36
	02/09/99	.15*	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
	06/08/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
	09/13/99	<.13	<.15	<.14	<.15	<.16	<.17	***	.13*	<.14	<.15	<.14	***	<.37
03/13/00	<.32	<.28	<.36	<.35	<.15	<.39	***	<.37	<.33	<.11	<.34	***	<.71	
W-8	02/20/97	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	05/27/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	09/18/97	<.5	<.6	<85	<40	<.7	<.7	<124	<68	<40	<.5	<.5	<124	<.5
	12/12/97	<.5	<.6	<85	<40	<.7	<.7	<.4	<68	<40	<.5	<.5	.4**	<.5
	03/25/98	<.5	<.6	<85	<40	<.7	<.7	<.3	<68	<40	<.5	<.5	.3**	<.5
	06/10/98	<.5	<.6	<85	<40	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	10/27/98	<.24	<.23	<.27	<.28	<.27	<.26	<.17	<.21	<.26	<.23	<.29	<.36	<.36
	02/09/99	.19*	<.15	<.15	<.15	<.16	<.17	***	.15*	<.14	<.15	<.15	***	<.37
	06/08/99	<.13	<.15	<.14	<.15	<.16	<.17	***	0.13	<.14	<.15	<.14	***	<.37
	09/13/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
03/13/00	<.32	<.28	<.36	<.35	<.15	<.39	***	<.37	<.33	<.11	<.34	***	<.71	
W-15	02/20/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	05/27/97	<.5	0.22	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	09/18/97	<.5	<.6	<85	<.7	<.7	<.7	<124	<68	<40	<.5	<.5	<124	<.5
	12/12/97	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	03/25/98	<.5	<.6	<85	<.7	<.7	<.7	<.4	<88	<40	<.5	<.5	.4**	<.5
	06/10/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	10/27/98	<.24	<.23	<.27	<.28	<.27	<.26	<.17	<.21	<.26	<.23	<.29	<.36	<.36
	02/09/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
	06/08/99	.16*	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
	09/13/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
03/13/00	<.32	<.28	<.36	<.35	<.15	<.39	***	<.37	<.33	<.11	<.34	***	<.71	

Table #5

LABORATORY ANALYTICAL RESULTS  
 Volatile Organic Compounds (VOC's)  
 N.W. Mauthe Superfund Site - Appleton, Wisconsin  
 MCO No. M050-90728.16

Well Name	Sample Date	Benzene (ug/l)	Chloroform (ug/l)	1,1-Dichloroethane (ug/l)	1,1-Dichloroethane (ug/l)	cis-1,2-Dichloroethane (ug/l)	Trans-1,2-Dichloroethane (ug/l)	Ortho-Xylene (ug/l)	Toluene (ug/l)	1,1,1-Trichloroethane (ug/l)	1,1,2-Trichloroethane (ug/l)	Trichloroethene (ug/l)	Meta, para Xylene (ug/l)	Total Xylenes (ug/l)
MW-101	02/20/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	05/27/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	09/18/97	<.5	<.6	.491*	.353*	<.7	<.7	<124	<68	3.03	<.5	3.31	<124	<.5
	12/12/97	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	03/25/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	06/10/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	10/27/98	<.24	<.23	<.27	<.28	<.27	<.26	<.17	<.21	<.26	<.23	<.29	<.36	<.36
	02/09/99	<.13	<.15	<.14	<.15	<.16	<.17	***	0.91	<.14	<.15	<.14	***	<.37
	06/08/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
	03/13/00	<.32	<.28	<.36	<.35	<.15	<.39	***	<.37	<.33	<.11	<.34	***	<.71
MW-102	02/20/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	05/27/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	09/18/97	<.5	<.6	<85	<85	<.7	<.7	<124	<68	<40	<.5	<.5	<124	<.5
	12/12/97	<.5	<.6	<85	<85	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	03/25/98	<.5	<.6	<85	<85	<.7	<.7	<.4	<68	<40	<.5	<.5	.4*	<.5
	06/10/98	<.5	<.6	<85	<85	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	10/27/98	<.24	<.23	<.27	<.28	<.27	<.26	<.17	<.21	<.26	<.23	<.29	<.36	<.36
	02/09/99	<.13	<.15	<.14	<.15	<.16	<.17	***	0.65	<.14	<.15	<.14	***	<.37
	06/08/99	<.13	<.15	<.14	<.15	<.16	<.17	***	.21*	<.14	<.15	<.14	***	<.37
	09/13/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
03/13/00	<.32	<.28	<.36	<.35	<.15	<.39	***	<.37	<.33	<.11	<.34	***	<.71	
MW-103	02/20/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	05/27/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	09/18/97	<.5	<.6	<85	<.7	<.7	<.7	<124	<68	<40	<.5	<.5	<124	<.5
	12/12/97	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	03/25/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	06/10/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	10/27/98	<.24	<.23	<.27	<.28	<.27	<.26	<.17	<.21	<.26	<.23	<.29	<.36	<.36
	02/09/99	<.13	<.15	<.14	<.15	<.16	<.17	***	.15*	<.14	<.15	<.14	***	<.37
	06/08/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
	09/13/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
03/13/00	<.32	<.28	<.36	<.35	<.15	<.39	***	<.37	<.33	<.11	<.34	***	<.71	

Table #5

LABORATORY ANALYTICAL RESULTS  
 Volatile Organic Compounds (VOC's)  
 N.W. Mauthe Superfund Site - Appleton, Wisconsin  
 MCO No. M050-90728.16

Well Name	Sample Date	Benzene (ug/l)	Chloroform (ug/l)	1,1-Dichloroethane (ug/l)	1,1-Dichloroethene (ug/l)	cis-1,2-Dichloroethene (ug/l)	Trans-1,2-Dichloroethene (ug/l)	Ortho-Xylene (ug/l)	Toluene (ug/l)	1,1,1-Trichloroethane (ug/l)	1,1,2-Trichloroethane (ug/l)	Trichloroethene (ug/l)	Meta, para Xylene (ug/l)	Total Xylenes (ug/l)
MW-104	02/20/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	05/27/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	09/18/97	<.5	<.6	<85	<.7	<.7	<.7	<124	<68	.324*	<.5	<.5	<124	<.5
	12/12/97	<.5	<.6	0.4	<.7	<.7	<.7	<120	<68	1*	<.5	0.9	<120	<.5
	03/25/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	.8*	<.5	<.5	<120	<.5
	06/10/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	2*	<.5	<.5	<120	<.5
	10/27/98	<.24	<.23	.35*	<.28	<.27	<.26	<.17	<.21	1.8	<.23	<.29	<.36	<.5
	02/09/99	<.13	<.15	.38*	<.15	<.16	<.17	***	.17*	1.5	<.15	<.14	***	<.37
	06/08/99	<.13	<.15	.34*	<.15	<.16	<.17	***	.14*	1.4	<.15	<.14	***	<.37
	09/13/99	<.13	<.15	.38*	<.15	<.16	<.17	***	.27*	1.6	<.15	<.14	***	<.37
	03/13/00	<.32	<.28	.38*	<.35	<.15	<.39	***	<.37	1.6	<.11	<.34	***	<.71
MW-105	02/20/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	05/27/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	09/18/97	<.5	<.6	<85	<.7	<.7	<.7	<124	<68	<40	<.5	<.5	<124	<.5
	12/12/97	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	03/25/98	<.5	<.6	<85	<.7	<.7	<.7	<.4	<68	<40	<.5	<.5	.4*	<.5
	06/10/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	10/27/98	<.24	<.23	<.27	<.28	<.27	<.26	<.17	<.21	<.26	<.23	<.29	<.36	<.5
	02/09/99	.16*	<.15	<.14	<.15	<.16	<.17	***	.3*	<.14	<.15	<.14	***	<.37
	06/08/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13*	<.14	<.15	<.14	***	<.37
	09/13/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
	03/13/00	<.32	<.28	<.36	<.35	<.15	<.39	***	<.37	<.33	<.11	<.34	***	<.71
MW-106	02/20/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	05/27/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5
	09/18/97	<.5	<.6	<85	<.7	<.7	<.7	<124	<68	2.73*	<.5	<.5	<124	<.5
	12/12/97	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	03/25/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	06/10/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	<.5
	10/27/98	<.24	<.23	<.27	<.28	<.27	<.26	<.17	<.21	<.26	<.23	<.29	<.36	<.5
	02/09/99	.18*	<.15	<.14	<.15	<.16	<.17	***	<.17	<.14	<.15	<.14	***	<.37
	06/08/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
	09/13/99	<.13	<.15	<.14	<.15	<.16	<.17	***	<.13	<.14	<.15	<.14	***	<.37
	03/13/00	<.32	<.28	<.36	<.35	<.15	0.39	***	<.37	<.33	<.11	<.34	***	<.71

Table #5

**LABORATORY ANALYTICAL RESULTS**  
**Volatle Organic Compounds (VOC's)**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
MCO No. M050-90728.16

Well Name	Sample Date	Benzene (ug/l)	Chloroform (ug/l)	1,1-Dichloroethane (ug/l)	1,1-Dichloroethene (ug/l)	cis-1,2-Dichloroethene (ug/l)	Trans-1,2-Dichloroethene (ug/l)	Ortho-Xylene (ug/l)	Toluene (ug/l)	1,1,1-Trichloroethane (ug/l)	1,1,2-Trichloroethane (ug/l)	Trichloroethene (ug/l)	Meta, para Xylene (ug/l)	Total Xylenes (ug/l)
MW-107	02/20/97	<.5	0.3	11	8.4	0.7	<.7	<.5	<.5	81	0.6	50	<.5	-
	05/27/97	0.09	1.10	36	40	3.1	<3.1	<.5	0.34	390	3.5	420	<.5	-
	09/18/97	<10	<12	47.6*	22.1	2.61*	<2.61	<2480	<68	265*	2.83	295	<2480	-
	12/12/97	<10	<12	56*	23	3*	<3	<2500	<68	280	3	290	<2500	-
	03/25/98	<25	<30	61*	69	5*	<5	<17	<68	720	5	620	17*	-
	06/10/98	<12	<15	59*	58	<3	<3	<3100	63*	340*	4*	390	<3100	-
	10/27/98	<.24	1.4	62	46*	3.6	.51*	<.17	<.21	550	4.9	640	<.36	-
	02/09/99	<3.2	<3.8	48	24	<4.0	<4.2	***	<3.2	220	<.38	250	***	<9.2
	06/08/99	<2.6	<3.0	42	20	<3.2	<3.4	***	<2.6	200	<3.0	310	***	<7.4
	09/13/99	<.26	<3.0	34	19	<.32	<3.4	***	<2.6	180	<.30	320	***	<7.4
	12/15/99	<3.2	<3.8	37	56	4.6 *	<4.2	***	<3.2	570	4.5 *	880	***	<9.2
	03/13/00	<26	<23	50 *	32 *	<12	<31	***	<30	340	<.90	630	***	<57
	06/22/00	<26	<23	<29	50 *	<12	<31	***	<30	540	<.9	850	***	<57
	09/27/00	<26	<23	35*	54*	<12	<31	***	<30	560	<.9	870	***	<57
MW-108	02/20/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	-
	05/27/97	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	<.5	-
	09/18/97	<.5	<.6	<85	<.7	<.7	<.7	<124	<68	<40	<.5	<.5	<124	-
	12/12/97	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	-
	03/25/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<40	<.5	<.5	<120	-
	06/10/98	<.5	<.6	<85	<.7	<.7	<.7	<120	<68	<44	<.5	<.5	<120	-
	10/27/98	<.24	<.23	<.22	<.28	<.27	<.26	<.17	<.21	<.26	<.23	<.29	<.36	-
	02/09/99	<.13	<.15	<.14	<.15	<.16	<.17	***	0.83	<.14	<.15	<.14	***	<.37
	06/08/99	<.13	<.15	<.14	<.15	<.16	<.17	***	.15*	<.14	<.15	<.14	***	<.37
	09/13/99	<.13	<.15	<.14	<.15	<.16	<.17	***	0.84	<.14	<.15	<.14	***	<.32
	03/13/00	<.32	<.28	<.36	<.35	<.15	<.39	***	<.37	<.33	<.11	<.36	***	<.71
MCL NR 149.21 (9)		5.0	-	-	7.0	70	100	-	1,000	200	5.0	5.0	---	-
Enforcement Standards (ES) 140.10		5	6	850	7	70	100	620**	343	200	5	5	620**	620
Preventive Action Plan (PAL) 140.10		0.5	0.6	85	0.7	7	20	124**	686	40	0.5	0.5	124**	124

## EXPLANATION:

Results prior to 10/27/98 for cis-1,2,-Dichloroethene and Trans-1,2 Dichloroethene were listed as Total Dichloroethene and were placed in this table under the heading cis-1,2,-Dichloroethene.

Results prior to 10/27/98 for Ortho Xylene and Meta, para Xylene were listed as Total Xylenes and were placed in this table under the heading Meta, para Xylene.

\* = Detection of compound in area of less certain quantification

\*\* = Standard includes Ortho-, Meta, para-Xylenes

\*\*\* = As of 02/09/99 Xylene results are listed as "Total Xylenes".

ND = Not Detected

NA = Not Analyzed

MCL = Maximum Contaminant Levels

ug/l = Microgram/Liter

  = Indicates an exceedance of the MCL 149.21(9) or ES 140.10

**Table #6**

**GROUNDWATER ELEVATIONS  
N.W. Mauthe Superfund Site - Appleton, Wisconsin  
MCO No. M050-90728.16**

Well Name	Date Measured	Depth To Water (feet)	Reference Elevation (To Top PVC) (feet)	Groundwater Elevation (feet)
W-2	02/01/97	-		798.66
	05/01/97	-		801.01
	09/01/97	-		800.28
	12/01/97	-	804.66	797.69
	03/01/98	-		802.08
	06/01/98	-		799.38
	10/27/98	5.85		798.81
	02/08/99	4.50		800.16
	06/08/99	3.31		801.35
	09/13/99	5.78		798.88
	12/15/99	6.63		798.03
	03/13/00	1.60		803.06
	06/22/00	2.63		802.03
09/27/00	3.28		801.38	
W-8	02/01/97	-		797.22
	05/01/97	-		797.66
	09/01/97	-		798.01
	12/01/97	-	803.36	796.52
	03/01/98	-		798.16
	06/01/98	-		797.31
	10/27/98	6.41		796.95
	02/08/99	5.49		797.87
	06/08/99	4.38		798.98
	09/13/99	6.71		796.65
	12/15/99	6.91		796.45
	03/13/00	6.25		797.11
	06/22/00	6.42		797.34
09/27/00	5.66		797.70	
W-15	02/01/97	-		793.97
	05/01/97	-		796.92
	09/01/97	-		797.23
	12/01/97	-	803.76	795.52
	03/01/98	-		796.78
	06/01/98	-		796.32
	10/27/98	7.95		795.81
	02/08/99	9.19		794.57
	06/08/99	6.89		796.87
	09/13/99	7.85		795.91
	12/15/99	8.97		794.79
	03/13/00	7.80		795.96
	06/22/00	6.42		797.34
09/27/00	6.30		797.46	



Table #6

**GROUNDWATER ELEVATIONS**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
MCO No. M050-90728.16

Well Name	Date Measured	Depth To Water (feet)	Reference Elevation (To Top PVC) (feet)	Groundwater Elevation (feet)
MW-101	02/01/97	-		797.16
	05/01/97	-		799.99
	09/01/97	-		798.67
	12/01/97	-	807.59	798.21
	03/01/98	-		803.43
	06/01/98	-		800.48
	10/27/98	10.26		797.33
	02/08/99	11.91		795.68
	06/08/99	9.79		797.80
	09/13/99	10.35		797.24
	12/15/99	9.01		798.58
	03/13/00	12.67		794.92
	06/22/00	6.28		801.31
	09/27/00	10.41		797.18
	MW-102	02/01/97	-	
05/01/97		-		780.89
09/01/97		-		780.79
12/01/97		-	804.45	780.95
03/01/98		-		780.47
06/01/98		-		780.72
10/27/98		24.11		780.34
02/08/99		23.84		780.61
06/08/99		23.59		780.86
09/13/99		23.70		780.75
12/15/99		24.27		780.18
03/13/00		24.00		780.45
06/22/00		23.69		780.76
09/27/00		23.65		780.80
MW-103		02/01/97	-	
	05/01/97	-		791.83
	09/01/97	-		789.60
	12/01/97	-	803.74	787.78
	03/01/98	-		791.03
	06/01/98	-		789.13
	10/27/98	11.96		791.78
	02/08/99	10.24		793.50
	06/08/99	8.69		795.05
	09/13/99	9.79		793.95
	12/15/99	12.68		791.06
	03/13/00	9.63		794.07
	06/22/00	8.22		795.52
	09/27/00	7.76		795.98

Table #6

**GROUNDWATER ELEVATIONS**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
MCO No. M050-90728.16

Well Name	Date Measured	Depth To Water (feet)	Reference Elevation (To Top PVC) (feet)	Groundwater Elevation (feet)
MW-104	02/01/97	-		792.94
	05/01/97	-		789.91
	09/01/97	-		798.59
	12/01/97	-	807.28	795.70
	03/01/98	-		799.46
	06/01/98	-		796.60
	10/27/98	10.51		796.77
	02/08/99	9.04		798.24
	06/08/99	7.49		799.79
	09/13/99	10.28		797.00
	12/15/99	10.78		796.50
	03/13/00	9.51		797.77
	06/22/00	8.41		798.88
	09/27/00	8.61		798.67
MW-105	02/01/97	-		793.74
	05/01/97	-		800.60
	09/01/97	-		800.37
	12/01/97	-	803.96	799.03
	03/01/98	-		800.08
	06/01/98	-		800.50
	10/27/98	5.41		798.55
	02/08/99	6.46		797.50
	06/08/99	3.04		800.92
	09/13/99	4.60		799.36
	12/15/99	5.28		798.68
	03/13/00	4.97		798.99
	06/22/00	3.06		800.90
	09/27/00	3.38		800.58
MW-106	02/01/97	-		794.75
	05/01/97	-		797.23
	09/01/97	-		796.91
	12/01/97	-	804.08	795.48
	03/01/98	-		797.37
	06/01/98	-		796.76
	10/27/98	8.12		795.96
	02/08/99	9.75		794.33
	06/08/99	6.72		797.36
	09/13/99	7.88		796.20
	12/15/99	8.71		795.37
	03/13/00	8.72		795.36
	06/22/00	6.87		797.21
	09/27/00	7.41		796.67

Table #6


**GROUNDWATER ELEVATIONS**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
MCO No. M050-90728.16

Well Name	Date Measured	Depth To Water (feet)	Reference Elevation (To Top PVC) (feet)	Groundwater Elevation (feet)
MW-107	02/01/97	-		788.23
	05/01/97	-		796.60
	09/01/97	-		797.64
	12/01/97	-	809.01	796.49
	03/01/98	-		796.68
	06/01/98	-		796.31
	10/27/98	10.71		798.30
	02/08/99	11.11		797.90
	06/08/99	11.04		797.97
	09/13/99	11.55		797.46
	12/15/99	11.66		797.35
	03/13/00	11.13		797.88
	06/22/00	10.69		798.32
	09/27/00	12.36		796.65
MW-108	02/01/97	-		798.36
	05/01/97	-		793.32
	09/01/97	-		790.53
	12/01/97	-	806.61	788.65
	03/01/98	-		795.59
	06/01/98	-		789.30
	10/27/98	6.98		799.63
	02/08/99	6.72		799.89
	06/08/99	5.80		800.81
	09/13/99	6.68		799.93
	12/15/99	6.87		799.74
	03/13/00	6.84		799.77
	06/22/00	6.28		800.33
	09/27/00	6.31		800.30
PZ-01	10/27/98	17.43	804.17	786.74
	02/08/99	18.24		785.93
	06/08/99	18.22		785.95
	09/13/99	18.25		785.92
	12/15/99	18.25		785.92
	03/13/00	18.25		785.92
	06/22/00	18.21		785.96
09/27/00	18.21		785.96	
PZ-02	10/27/98	14.66	803.64	788.98
	02/08/99	14.70		788.94
	06/08/99	14.70		788.94
	09/13/99	14.74		788.90
	12/15/99	14.72		788.92
	03/13/00	14.76		788.88
	06/22/00	14.41		789.23
09/27/00	14.43		789.21	

**Table #6**

**GROUNDWATER ELEVATIONS  
N.W. Mauthe Superfund Site - Appleton, Wisconsin  
MCO No. M050-90728.16**

<b>Well Name</b>	<b>Date Measured</b>	<b>Depth To Water (feet)</b>	<b>Reference Elevation (To Top PVC) (feet)</b>	<b>Groundwater Elevation (feet)</b>
PZ-03	10/27/98	22.71	803.62	780.91
	02/08/99	23.74		779.88
	06/08/99	23.74		779.88
	09/13/99	23.55		780.07
	12/15/99	23.52		780.10
	03/13/00	23.30		780.24
	06/22/00	23.40		780.22
	09/27/00	20.21		783.41
	PZ-04	10/27/98	15.18	807.30
02/08/99		23.61		783.69
06/08/99		21.69		785.61
9/13/99		23.87		783.43
12/15/99		23.80		783.50
03/13/00		25.77		781.53
06/22/00		22.51		784.79
09/27/00		19.60		787.70

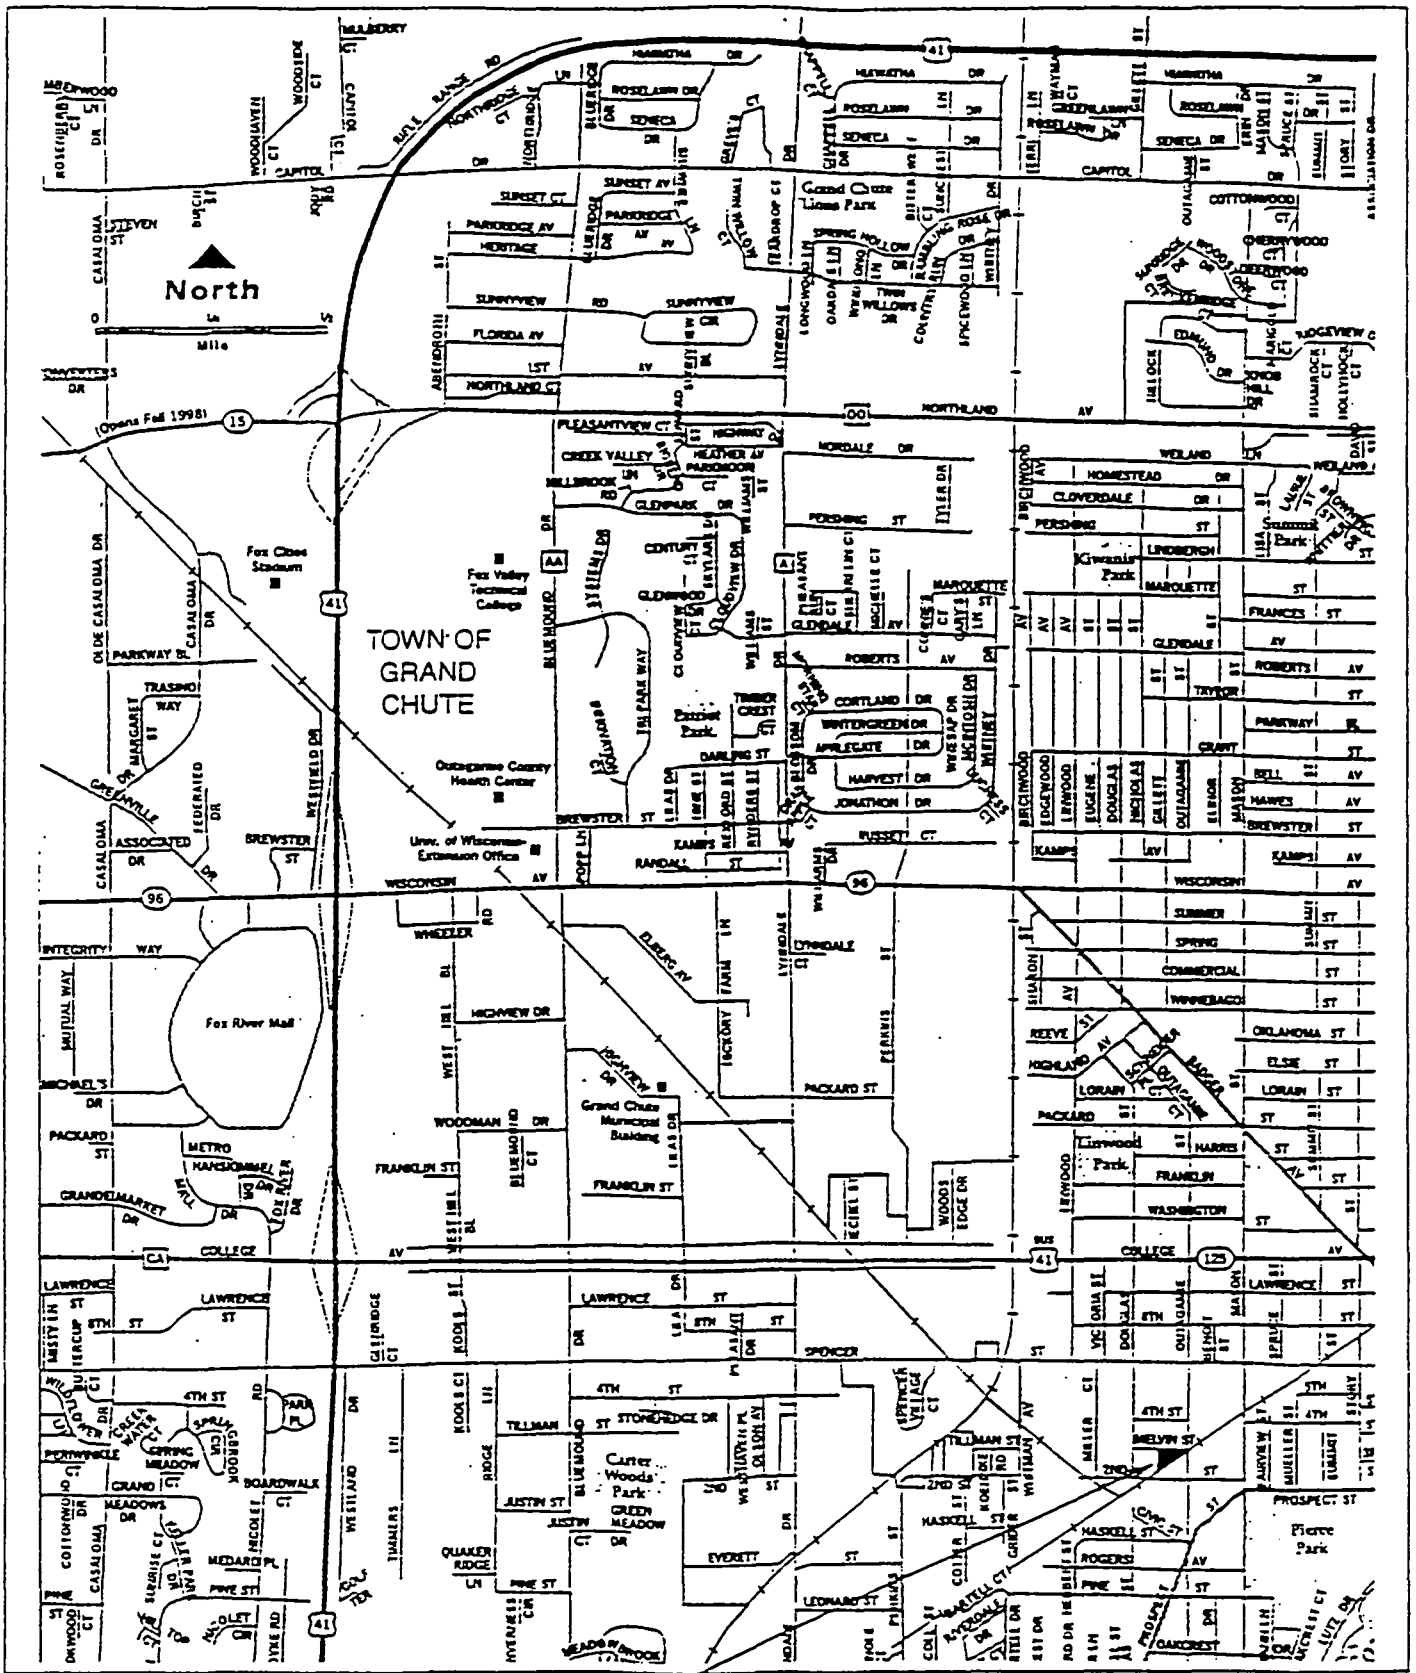

SITE LOCATION



FIGURE 1

**SITE LOCATION MAP**

N.W. MAUTHE SUPERFUND SITE  
APPLETON, WI

McM #M050-98808 July, 99

**McMAHON**  
ASSOCIATES, INC.

ENGINEERS • ARCHITECTS  
SCIENTISTS • SURVEYORS

MW-108

W-2

MELVIN STREET

NORTH



40 20 0 40

SCALE - FEET

ELECTRIC SUBSTATION

PZ-4

MW-101

WEST GROUNDWATER COLLECTION TRENCH

GROUNDWATER TREATMENT FACILITY

MW-107

MANHOLE No.1

BLDG

GAR

MW-104

GAR

HSE

HSE

TAVERN SUMP EFFLUENT PIPE

FOUNDATION DRAIN LATERAL

SOUTHEAST GROUNDWATER COLLECTION TRENCH

SECOND STREET

W-8

MW-105

MANHOLE No.2

MW-102

HSE

CENTRAL GROUNDWATER COLLECTION TRENCH

FOUNDATION DRAIN LATERAL

PZ-3

MW-103

FOUNDATION DRAIN LATERAL

PZ-1

W-15

TAVERN

MW-106

PZ-2

OUTAGAMIE STREET

FIGURE 2  
COLLECTION TRENCH AND  
MONITORING WELL LOCATIONS  
N.W. MAUTHE SUPERFUND SITE

APPLETON, WISCONSIN  
McM# M050-90728.14 SEPTEMBER 27, 2000

C:\DwgCNC\M050\90728-14\Fig-02.dwg 12/13/00 10:33 AM

MW-108  
800.33

W-2  
801.38

MELVIN STREET

ELECTRIC  
SUBSTATION

WEST  
GROUNDWATER  
COLLECTION  
TRENCH

PZ-4

MW-101  
797.18

GROUNDWATER  
TREATMENT  
FACILITY

MW-107  
796.65

MANHOLE No.1

BLDG

MW-104  
798.67

GAR

FOUNDATION  
DRAIN LATERAL

HSE

HSE

TAVERN  
SUMP EFFLUENT  
PIPE

FOUNDATION  
DRAIN LATERAL

PZ-2

MW-106  
796.67

TAVERN

SOUTHEAST  
GROUNDWATER  
COLLECTION  
TRENCH

SECOND STREET

W-8  
797.70

MW-105  
800.58

799

W-2  
801.38

801

799

797

795

793

791

789

787

785

783

781

MANHOLE No.2

MW-102  
780.80

781

783

785

787

789

791

793

795

W-15  
797.56

NORTH



40 20 0 40

SCALE - FEET

**LEGEND**

W-2 803.06 MONITORING WELL & GROUNDWATER ELEVATION

GROUNDWATER FLOW DIRECTION

797 GROUNDWATER CONTOUR

OUTAGAMIE STREET


**FIGURE 3**  
**GROUNDWATER MONITORING WELLS**  
**LOCATIONS & GROUNDWATER CONTOURS**  
**N.W. MAUTHE SUPERFUND SITE**  
APPLETON, WISCONSIN  
McM# M050-90728.14 SEPTEMBER 27, 2000

C:\Dwg\CNC\M050\90728-14\Fig-03.dwg 12/13/00 10:34 AM

MW-108

W-2

MELVIN STREET

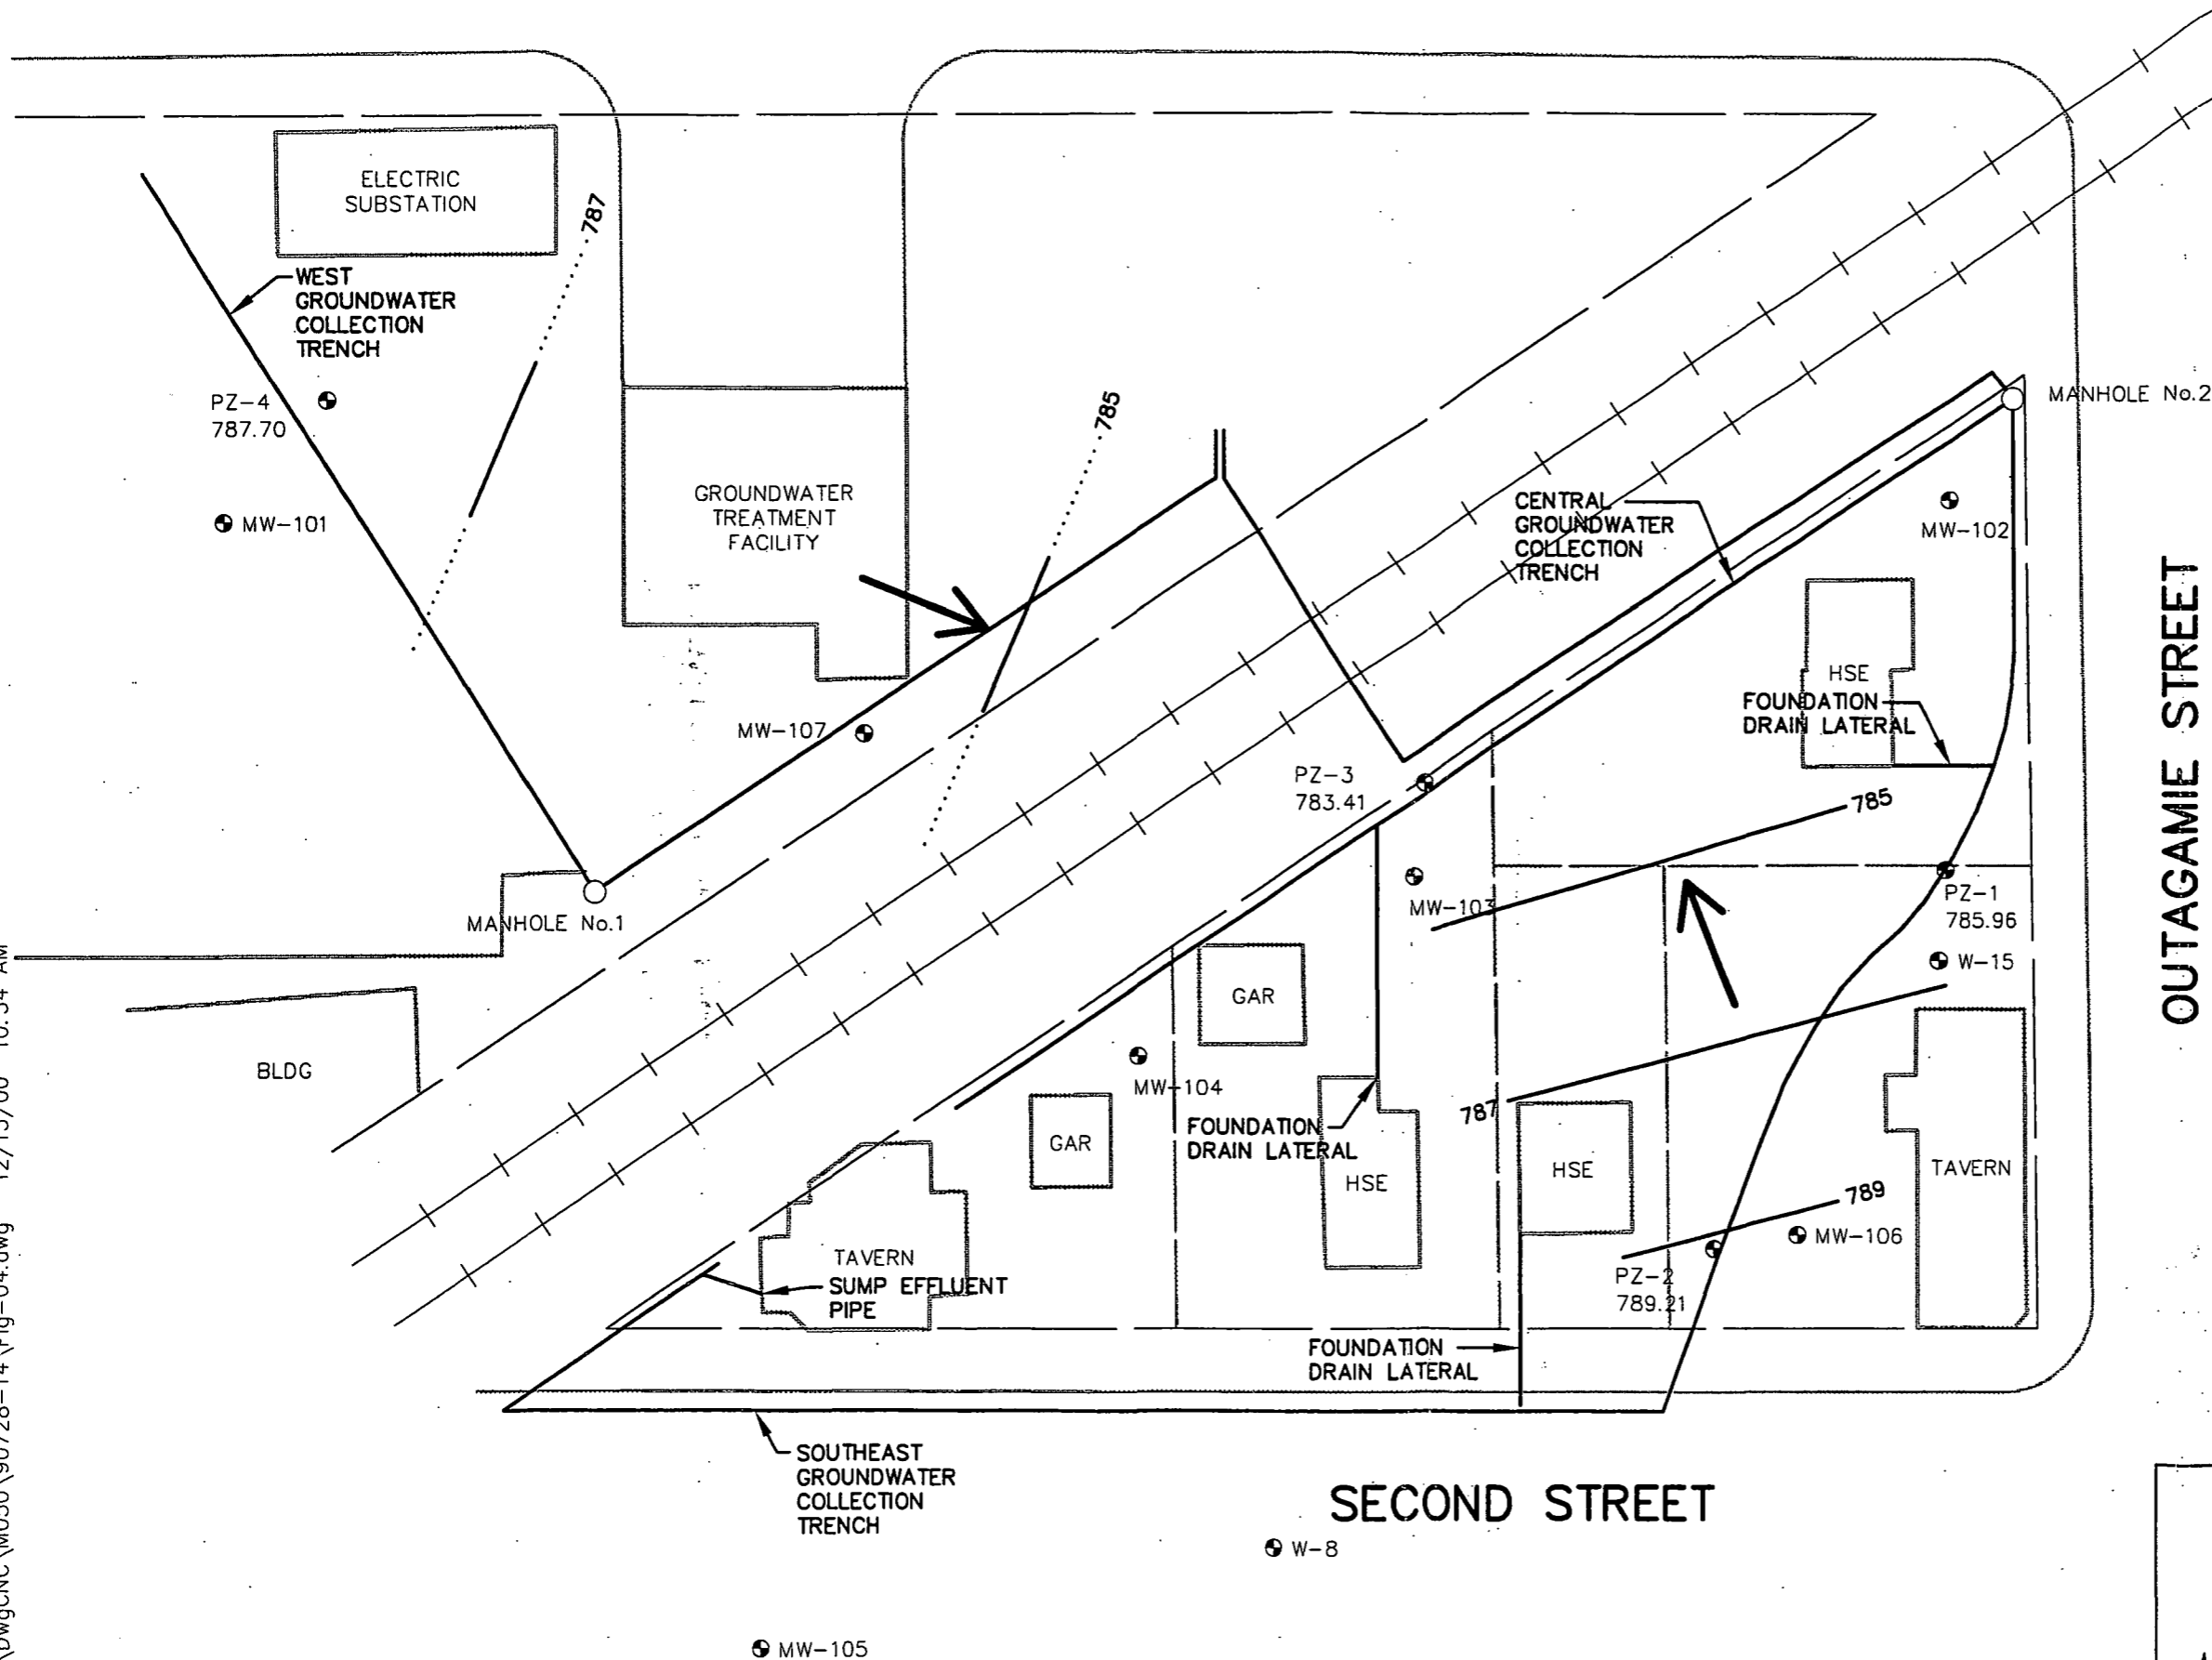



NORTH



40 20 0 40

SCALE - FEET

**LEGEND**

-  PZ-1 785.96 **PIEZOMETER & POTENTIOMETRIC SURFACE ELEVATION**
-  **POTENTIOMETRIC GRADIENT**

OUTAGAMIE STREET

SECOND STREET

**FIGURE 4  
PIEZOMETER LOCATIONS AND  
POTENTIOMETRIC CONTOURS  
N.W. MAUTHE SUPERFUND SITE**

APPLETON, WISCONSIN  
McM# M050-90728.14 SEPTEMBER 27, 2000



C:\DwgCNC\M050\90728-14\Fig-04.dwg 12/13/00 10:34 AM



MW-108  
2.9 ug/L

W-2  
1.1 ug/L\*

# MELVIN STREET

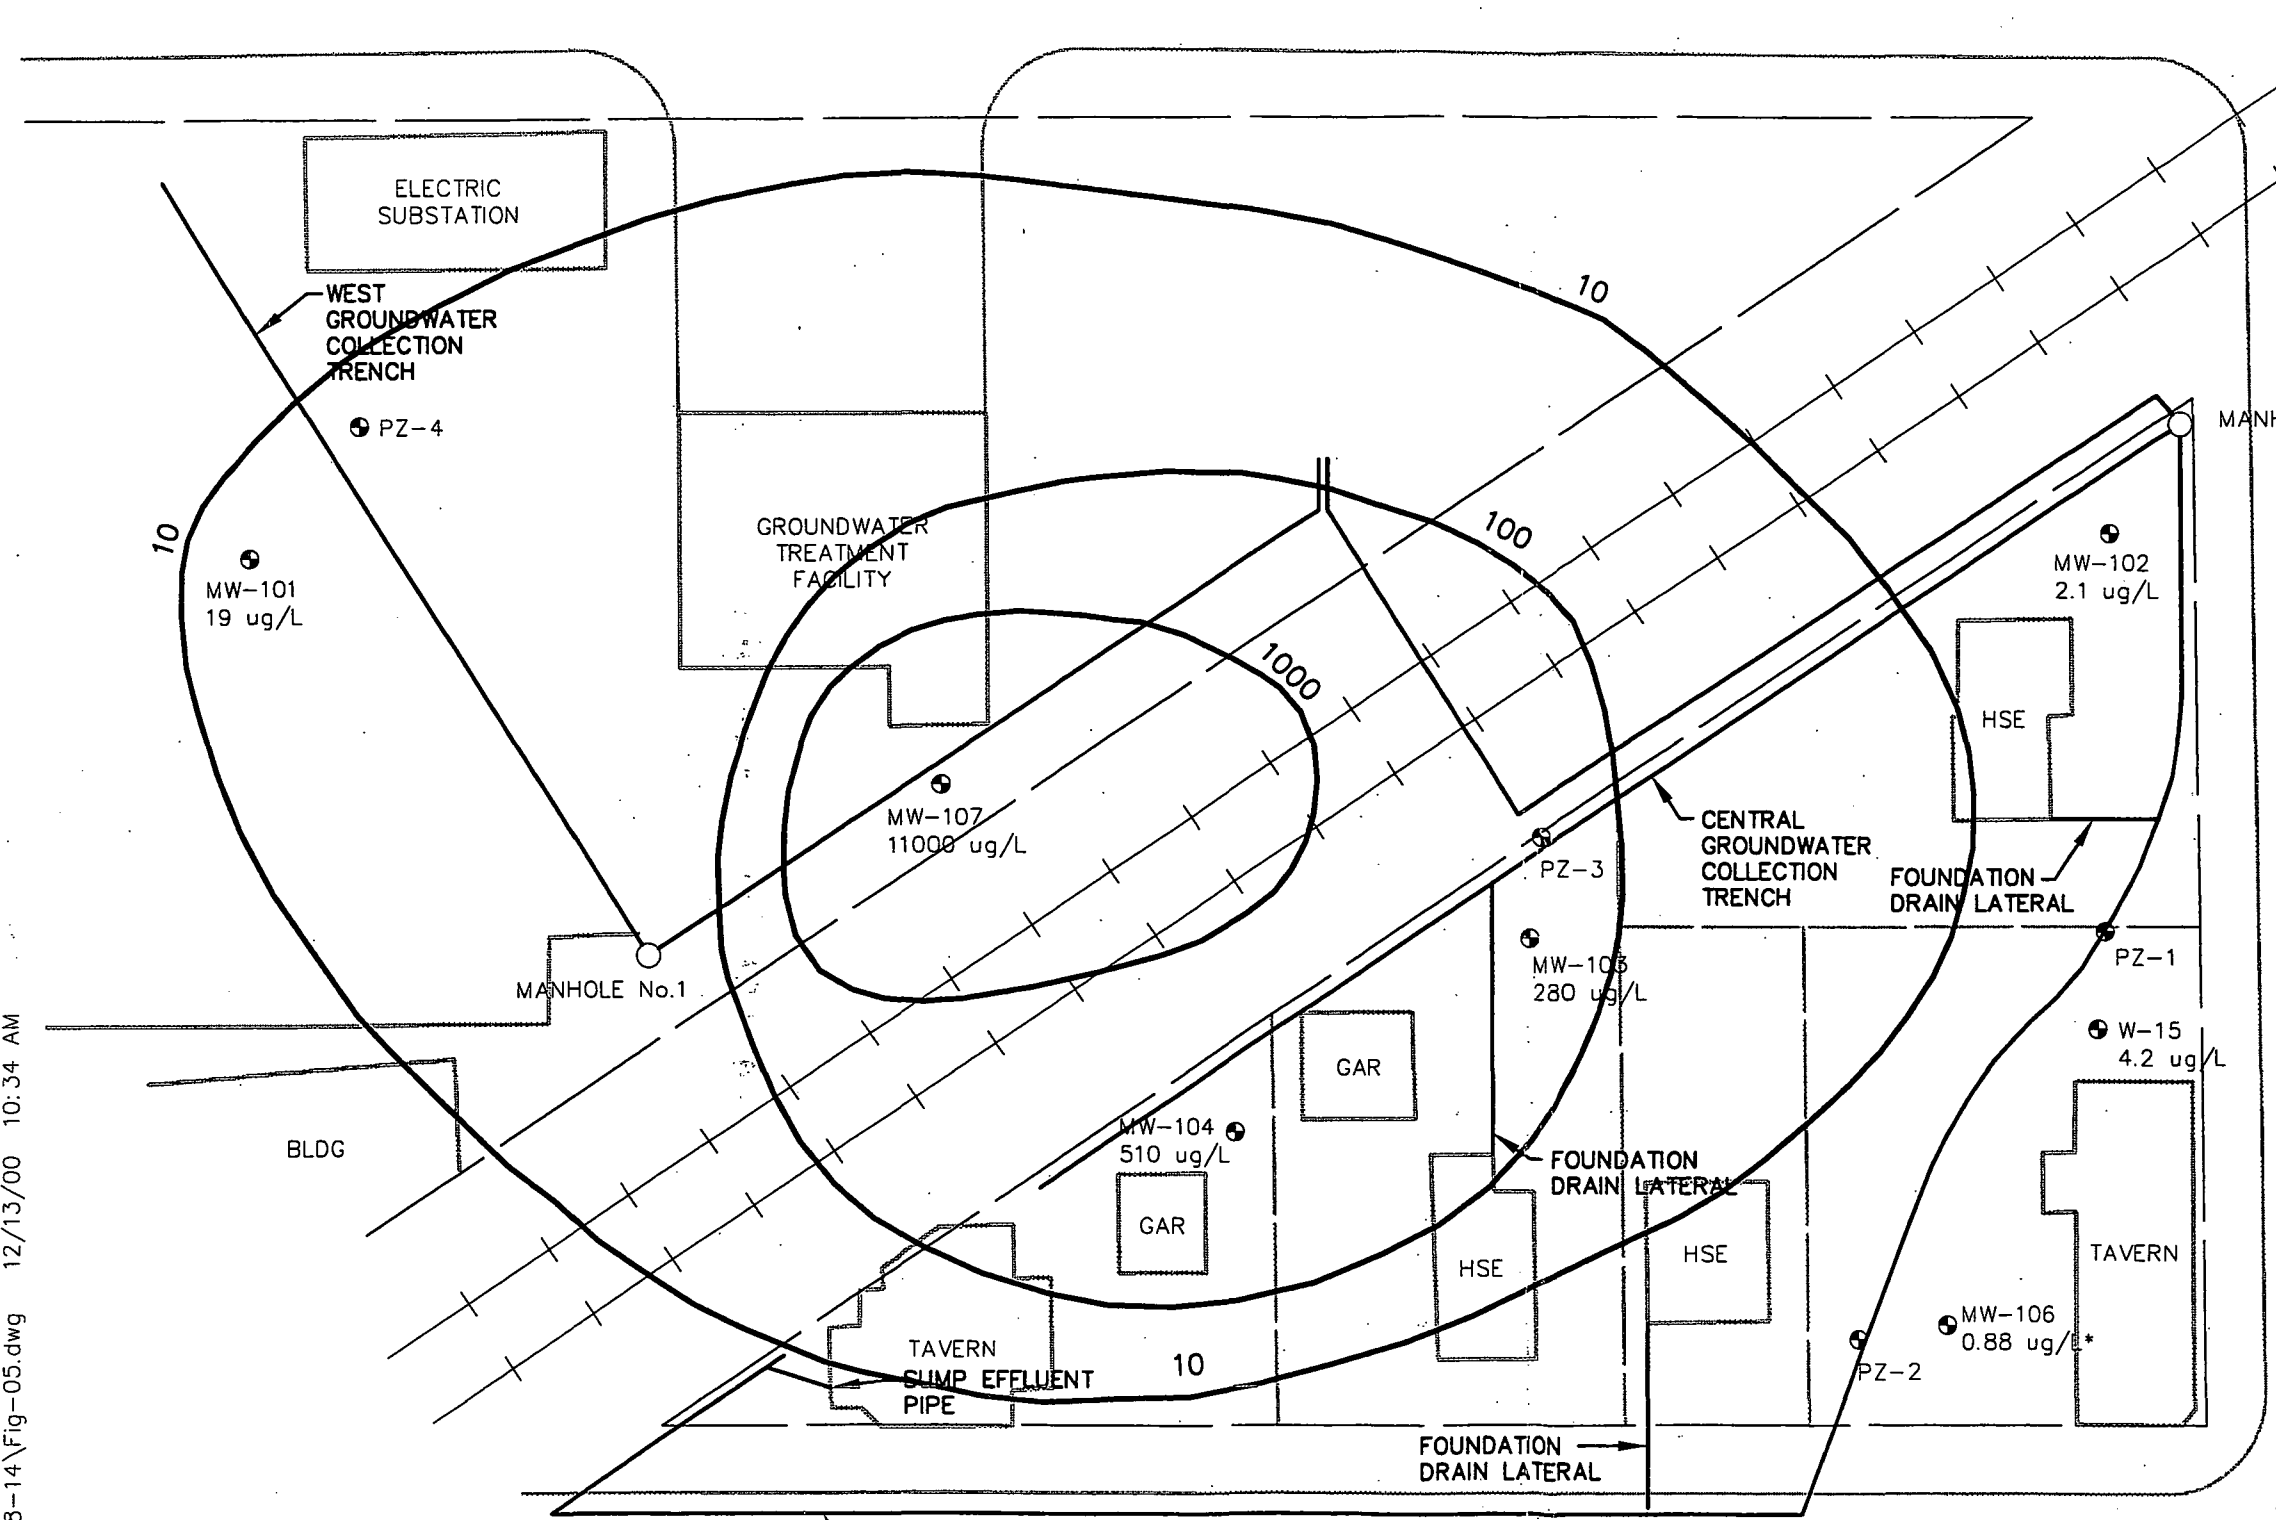

OUTAGAMIE STREET

## LEGEND

- 10 ISOCONCENTRATION OF CHROMIUM (ESTIMATED)
- < LESS THAN THE DETECTION LIMIT
- ug/L MICROGRAM.LITER
- MW-102 MONITORING WELL
- \* ANALYTE DETECTED IN THE AREA OF LESS CERTAIN QUANTITATION

# SECOND STREET

FIGURE 5  
**ISOCONCENTRATION MAP**  
**TOTAL CHROMIUM ug/L in Groundwater**  
**N.W. MAUTHE SUPERFUND SITE**  
 APPLETON, WISCONSIN  
 McM# M050-90728.14 SEPTEMBER 27, 2000

MW-105  
1.2 ug/L\*

W-8  
0.75 ug/L\*

MW-106  
0.88 ug/L\*

W-15  
4.2 ug/L

MW-105  
280 ug/L

MW-104  
510 ug/L

MW-106  
280 ug/L

MW-107  
11000 ug/L

MW-102  
2.1 ug/L

MW-101  
19 ug/L

## APPENDIX A

---

Concentration Versus Time Graphs  
Inorganic Compounds / All Wells

**Appendix A**

Concentration Versus Time Graphs  
Inorganic Compounds / All Wells

Well Name	Sample Date	Cadmium (ug/l)	Chromium (ug/l)	Manganese (ug/L)
W-2	02/20/97	NA	15.00	460
	05/27/97	0.43	8.50	170
	09/18/97	0.27	2.30	116
	12/12/97	0.06	6.20	133
	03/25/98	0.08	1.90	83.8
	06/10/98	0.15	16.40	466
	10/27/98	0.25	3.60	69
	02/09/99	0.23	0.31	240
	06/08/99	0.15	0.31	290
	09/13/99	0.15	2.00	240
	12/15/99	0.15	0.36	2.8
	03/13/00	0.15	0.39	7.8
	06/22/00	0.15	0.31	0.21
	09/27/00	2.70	0.55	17
	W-8	02/20/97	NA	17.00
05/27/97		1.60	37.00	670
09/18/97		0.45	14.40	338
12/12/97		0.25	5.70	147
03/25/98		0.43	10.10	205
06/10/98		0.54	9.90	264
10/27/98		0.80	3.90	64
02/09/99		0.15	0.31	850
06/08/99		0.15	0.31	50
09/13/99		0.15	1.90	98
12/15/99		0.15	2.80	180
03/13/00		0.15	0.70	65
06/22/00		0.15	3.10	74
09/27/00		0.14	0.37	26

**Appendix A**

Concentration Versus Time Graphs  
Inorganic Compounds / All Wells

Well Name	Sample Date	Cadmium (ug/l)	Chromium (ug/l)	Manganese (ug/L)
W-15	02/20/97	NA	32.00	430
	05/27/97	0.27	5.90	97
	09/18/97	0.31	13.90	325
	12/12/97	0.06	5.70	80.9
	03/25/98	0.02	1.90	85.7
	06/10/98	0.05	10.00	147
	10/27/98	0.02	6.80	110
	02/09/99	0.15	0.31	320
	06/08/99	0.15	2.40	130
	09/13/99	0.15	5.30	130
	12/15/99	0.15	5.00	90
	03/13/00	0.15	7.00	130
	06/22/00	0.15	1.80	11
	09/27/00	0.11	4.20	24
MW-101	02/20/97	NA	36.00	820
	05/27/97	0.10	10.00	170
	09/18/97	0.03	11.90	145
	12/12/97	0.03	12.80	176
	03/25/98	0.02	20.90	239
	06/10/98	0.13	48.20	604
	10/27/98	0.08	3.20	24
	02/09/99	0.15	0.31	1,900
	06/08/99	0.15	1.80	380
	09/13/99	0.15	2.90	31
	12/15/99	0.15	2.50	9.1
	03/13/00	0.15	2.30	100
	06/22/00	0.15	0.70	2.1
	09/27/00	0.11	19.00	3.7

**Appendix A**

Concentration Versus Time Graphs  
Inorganic Compounds / All Wells

Well Name	Sample Date	Cadmium (ug/l)	Chromium (ug/l)	Manganese (ug/L)
MW-102	02/20/97	NA	26.00	570
	05/27/97	0.21	48.00	920
	09/18/97	0.04	1.96	302
	12/12/97	0.02	1.85	387
	03/25/98	0.05	1.95	302
	06/10/98	0.02	1.95	318
	10/27/98	0.14	0.49	340
	02/09/99	0.15	0.37	670
	06/08/99	0.15	0.60	140
	09/13/99	0.15	4.00	160
	12/15/99	0.15	0.60	550
	03/13/00	0.15	1.70	580
	06/22/00	0.15	0.31	310
	09/27/00	0.11	2.10	130
	MW-103	02/20/97	NA	1300.00
05/27/97		0.10	160.00	900
09/18/97		0.03	35.20	287
12/12/97		0.02	16.30	84.3
03/25/98		0.02	15.50	83
06/10/98		0.07	57.60	417
10/27/98		0.08	6.30	27
06/08/99		0.15	87.00	810
09/13/99		0.15	720.00	83
12/15/99		0.15	260.00	160
03/13/00		0.15	600.00	79
06/22/00		0.15	130.00	180
09/27/00		0.11	280.00	230

**Appendix A**

**Concentration Versus Time Graphs  
Inorganic Compounds / All Wells**

<b>Well Name</b>	<b>Sample Date</b>	<b>Cadmium (ug/l)</b>	<b>Chromium (ug/l)</b>	<b>Manganese (ug/L)</b>
MW-104	02/20/97	NA	5.90	550
	05/27/97	0.01	6.90	470
	09/18/97	0.02	35.60	235
	12/12/97	0.02	61.80	279
	03/25/98	0.02	66.80	73.6
	06/10/98	0.02	219.00	107
	10/27/98	0.14	150.00	25
	02/09/99	0.15	94.00	1,000
	06/08/99	0.50	62.00	620
	09/13/99	0.15	80.00	9.2
	12/15/99	0.15	170.00	1.6
	03/13/00	0.15	300.00	13
	06/22/00	0.15	210.00	41
	09/27/00	0.11	510.00	3.9
MW-105	02/20/97	NA	21.00	1,100
	05/27/97	0.10	5.00	120
	09/18/97	0.07	29.50	532
	12/12/97	0.08	15.80	297
	03/25/98	0.02	30.80	518
	06/10/98	0.02	13.70	217
	10/27/98	0.14	8.80	150
	02/09/99	0.15	0.60	2,000
	06/08/99	0.15	0.50	1,300
	09/13/99	0.15	0.32	1,700
	12/15/99	0.15	0.31	860
	03/13/00	0.15	4.80	660
	06/22/00	0.15	0.50	600
	09/27/00	0.11	0.60	700

**Appendix A**

**Concentration Versus Time Graphs  
Inorganic Compounds / All Wells**

<b>Well Name</b>	<b>Sample Date</b>	<b>Cadmium (ug/l)</b>	<b>Chromium (ug/l)</b>	<b>Manganese (ug/L)</b>
MW-106	02/20/97	NA	21.00	320
	05/27/97	0.10	40.00	590
	09/18/97	0.02	5.50	56.9
	12/12/97	0.02	9.20	155
	03/25/98	NA	13.40	150
	06/10/98	0.02	1.90	10
	10/27/98	0.13	3.20	38
	02/09/99	0.15	0.31	760
	06/08/99	0.15	0.39	900
	09/13/99	0.15	1.80	1,100
	12/15/99	0.15	0.60	130
	03/13/00	0.15	2.30	270
	06/22/00	0.15	0.36	2.10
	09/27/00	0.11	0.44	50
MW-107	02/20/97	NA	2000.00	190
	05/27/97	0.10	3600.00	91
	09/18/97	0.02	2670.00	59.3
	12/12/97	0.02	2310.00	48.4
	03/25/98	0.02	11200.00	68.2
	06/10/98	0.05	6240.00	161
	10/27/98	0.08	7100.00	28
	02/09/99	0.15	3200.00	49
	06/08/99	0.15	5800.00	25
	09/13/99	0.15	4000.00	18
	12/15/99	0.15	14000.00	0.41
	03/13/00	0.15	8000.00	22
	06/30/00	0.15	14000.00	21
	09/27/00	0.11	11000.00	4.9


## Appendix A

### Concentration Versus Time Graphs Inorganic Compounds / All Wells


Well Name	Sample Date	Cadmium (ug/l)	Chromium (ug/l)	Manganese (ug/L)
MW-108	02/20/97	NA	25.00	490
	05/27/97	0.10	11.00	210
	09/18/97	0.07	27.40	462
	12/12/97	0.02	5.60	74.8
	03/25/98	0.02	9.40	142
	06/10/98	0.07	28.40	478
	10/27/98	0.13	8.90	88
	02/09/99	0.15	1.70	560
	06/08/99	0.15	3.10	450
	09/13/99	0.15	4.50	100
	12/15/99	0.15	6.1	79
	3/13/00	0.15	36	41
	6/22/00	0.15	6.5	2.1
	9/27/00	0.11	2.9	29
Maximum Contaminant Level (MCL)		5	100	50
Enforcement Standard Chapter NR 140.10		5	100	50
Preventive Action Limit Chapter NR 140.10		0.5	10	25




# Well W-2 / Concentration Vs. Time

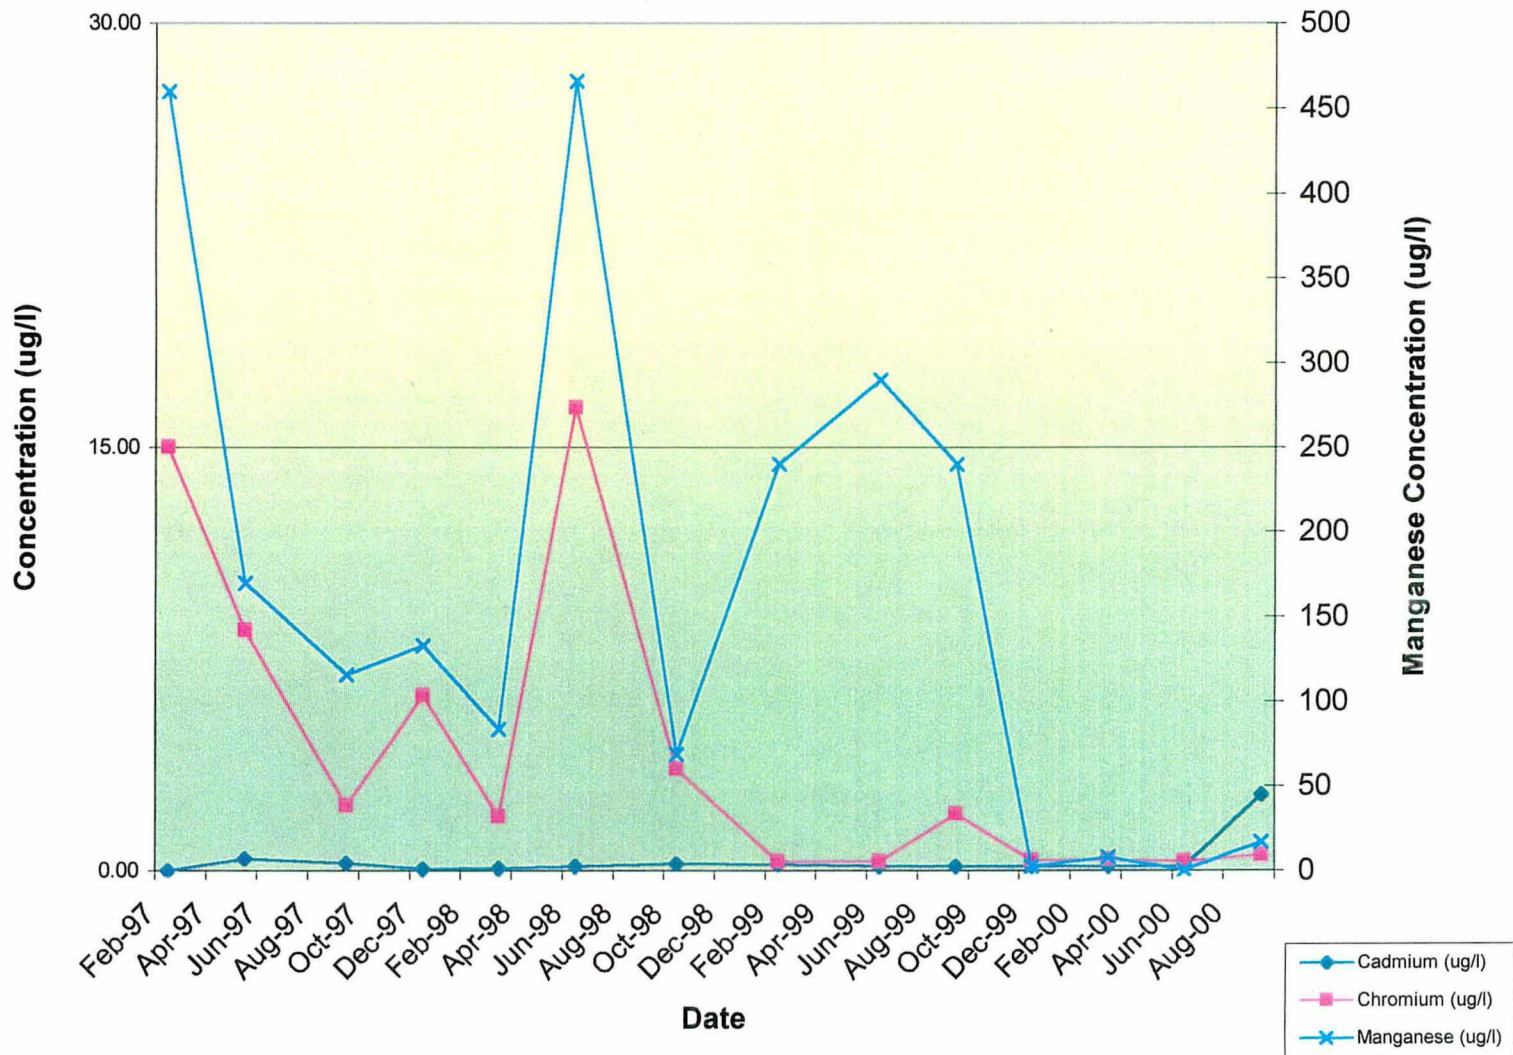


# Well W-8 / Concentration Vs. Time

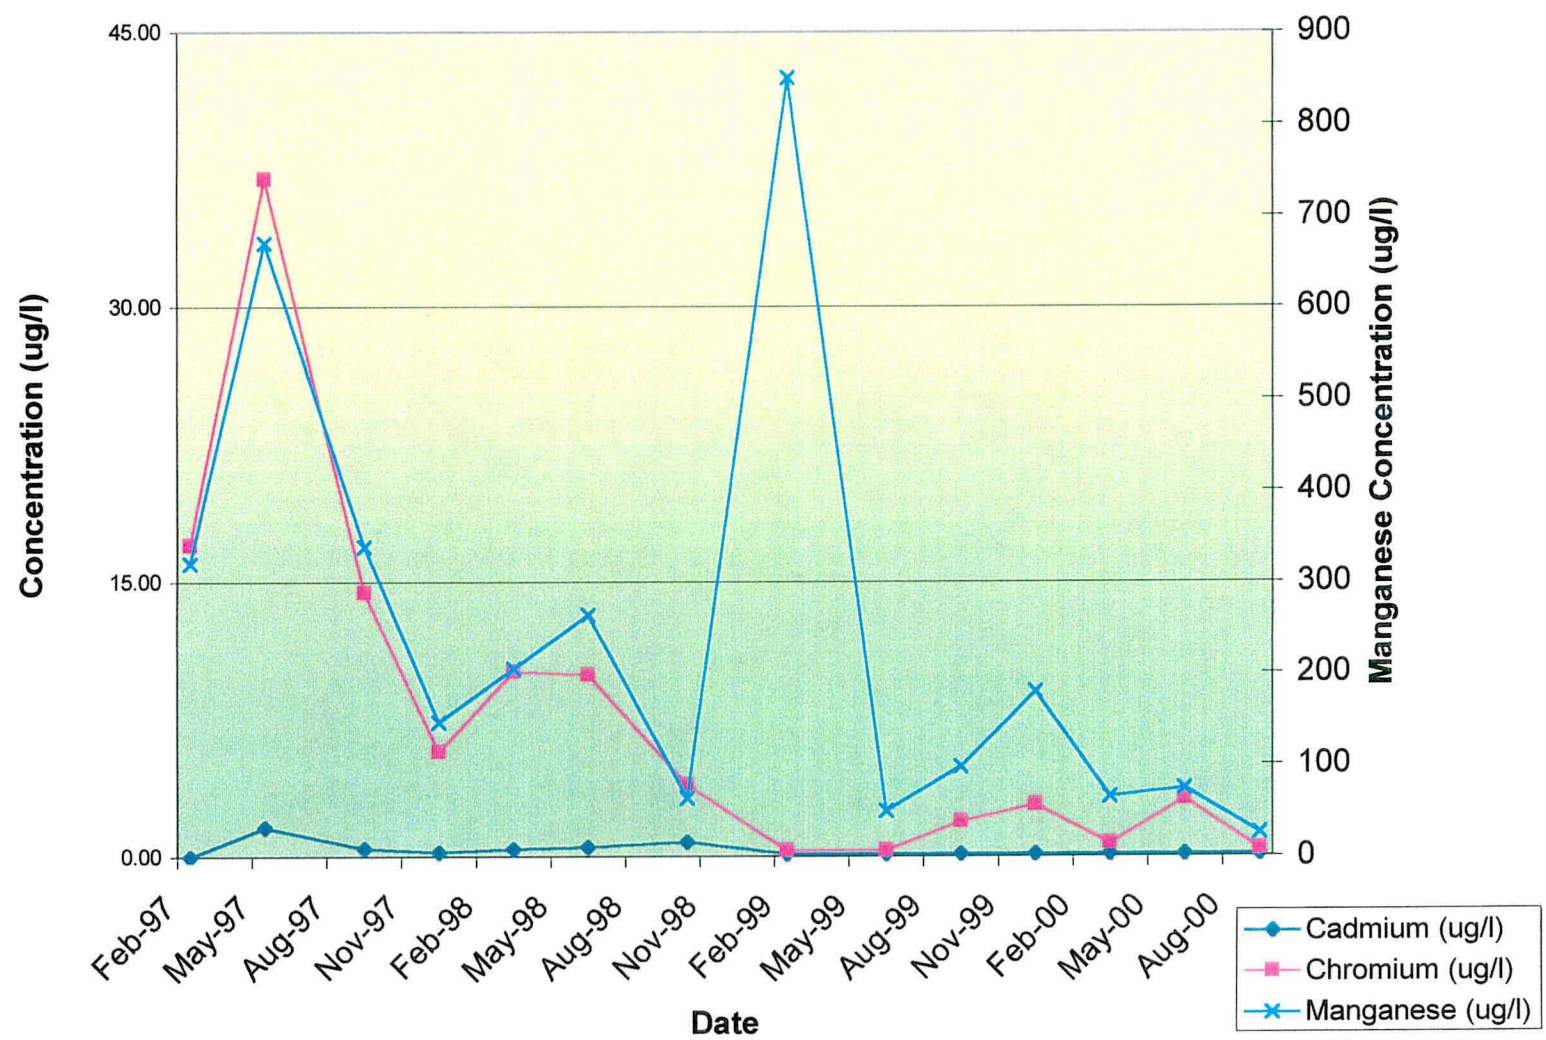


# Well W-15 / Concentration Vs. Time

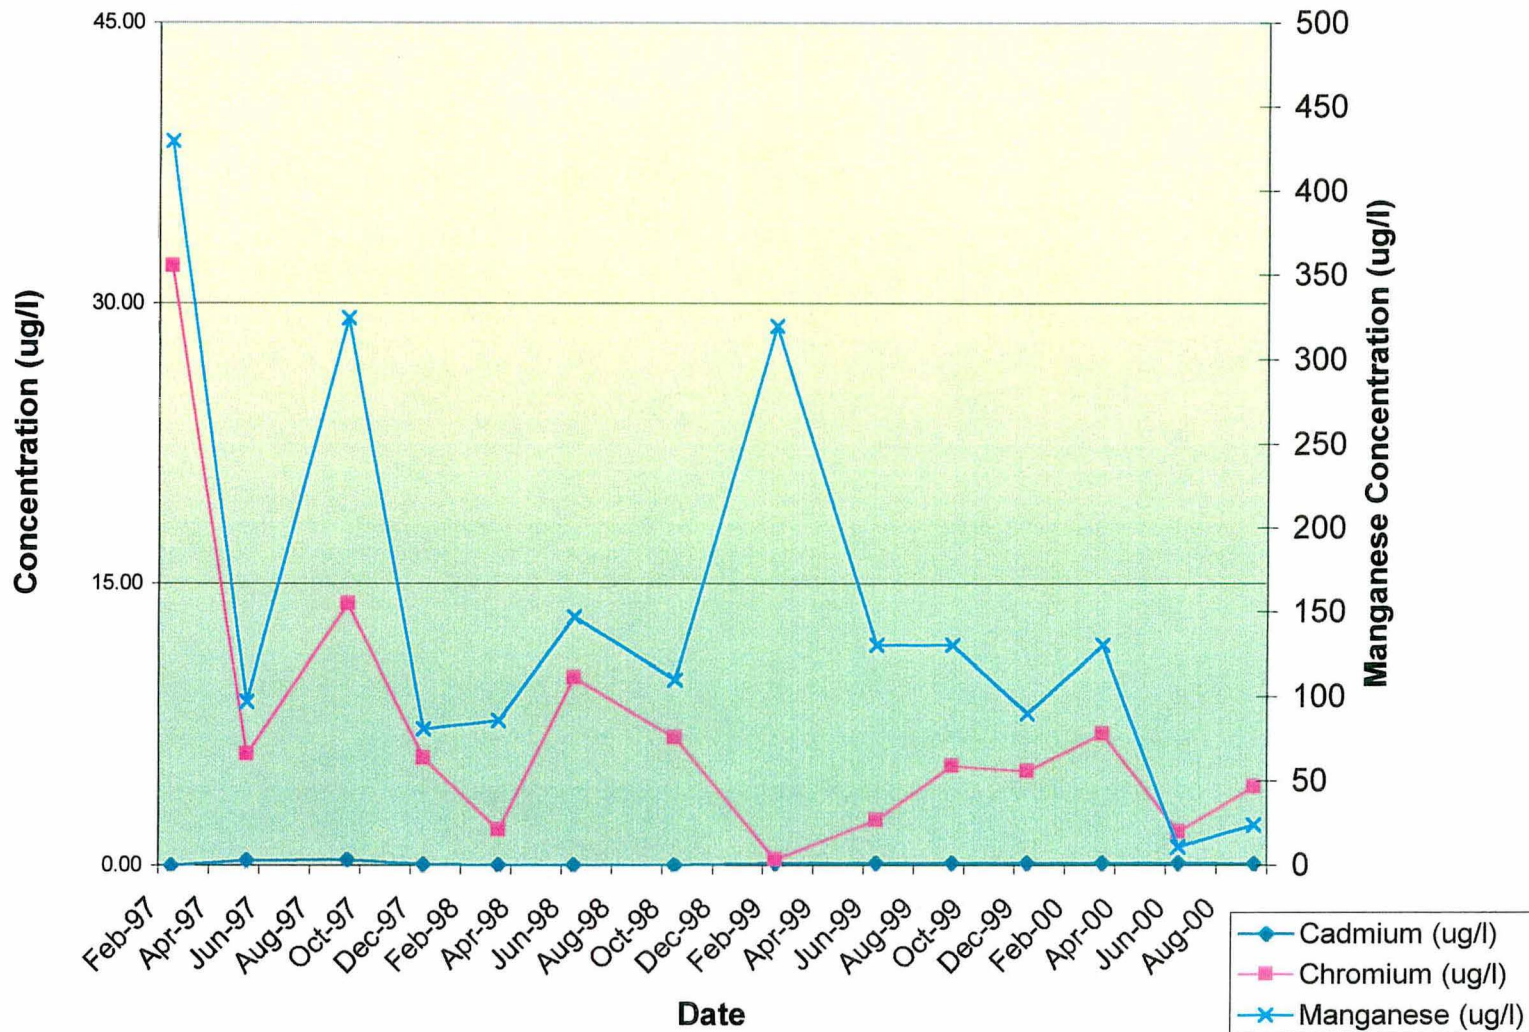


# Well W-101 / Concentration Vs. Time

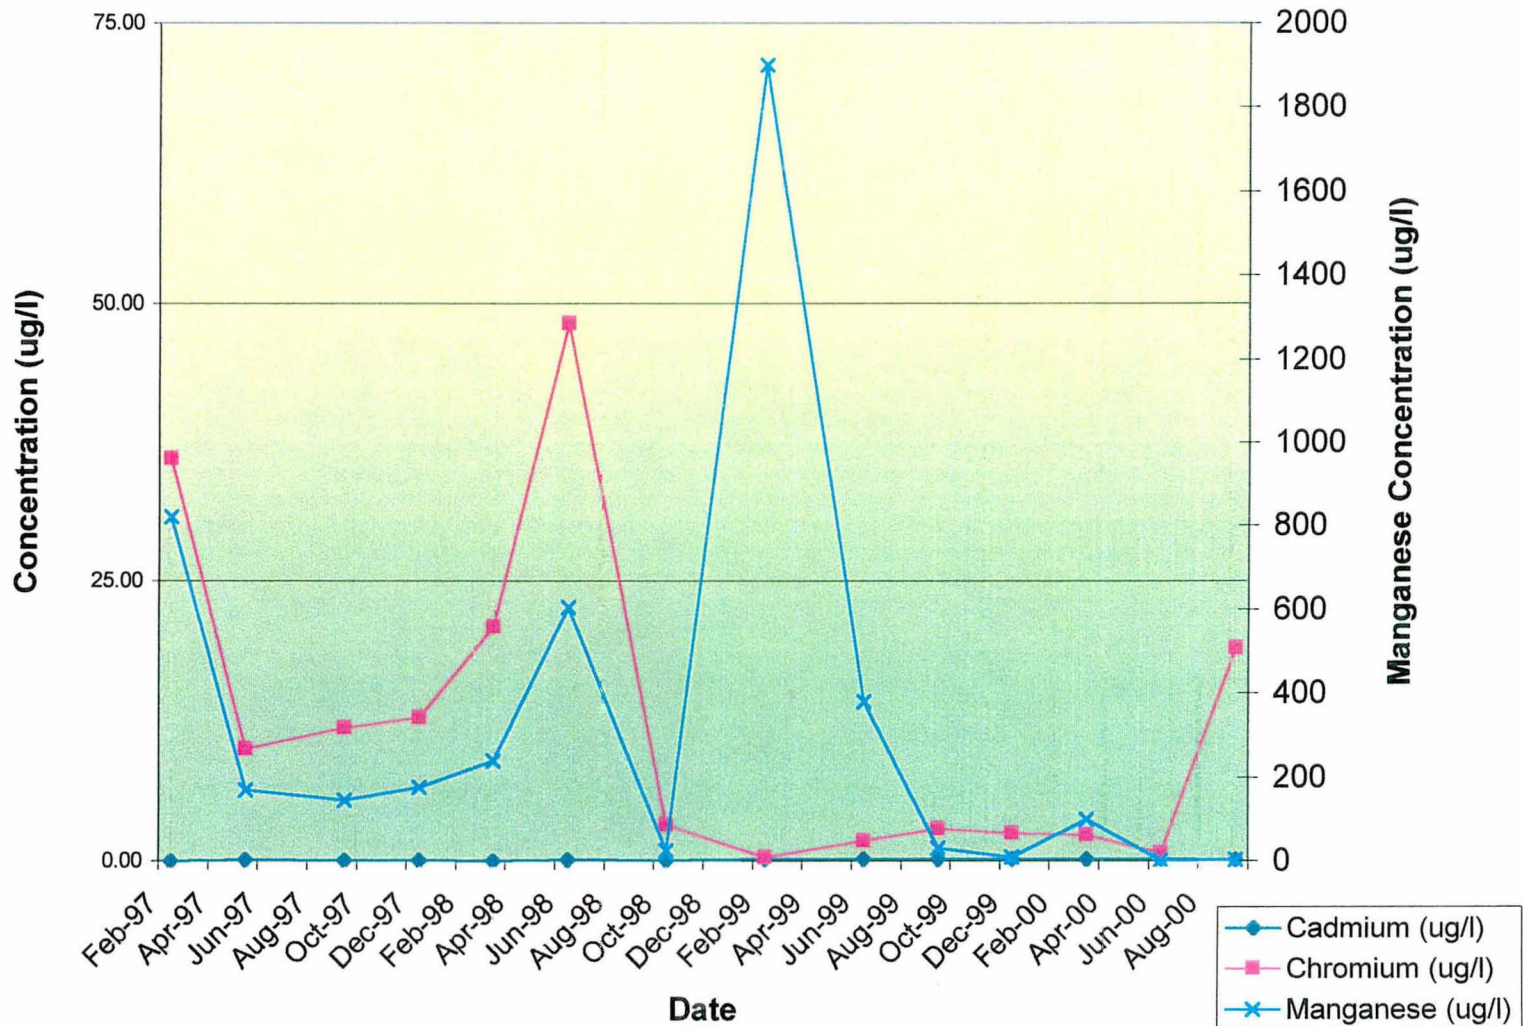


# Well W-102 / Concentration Vs. Time

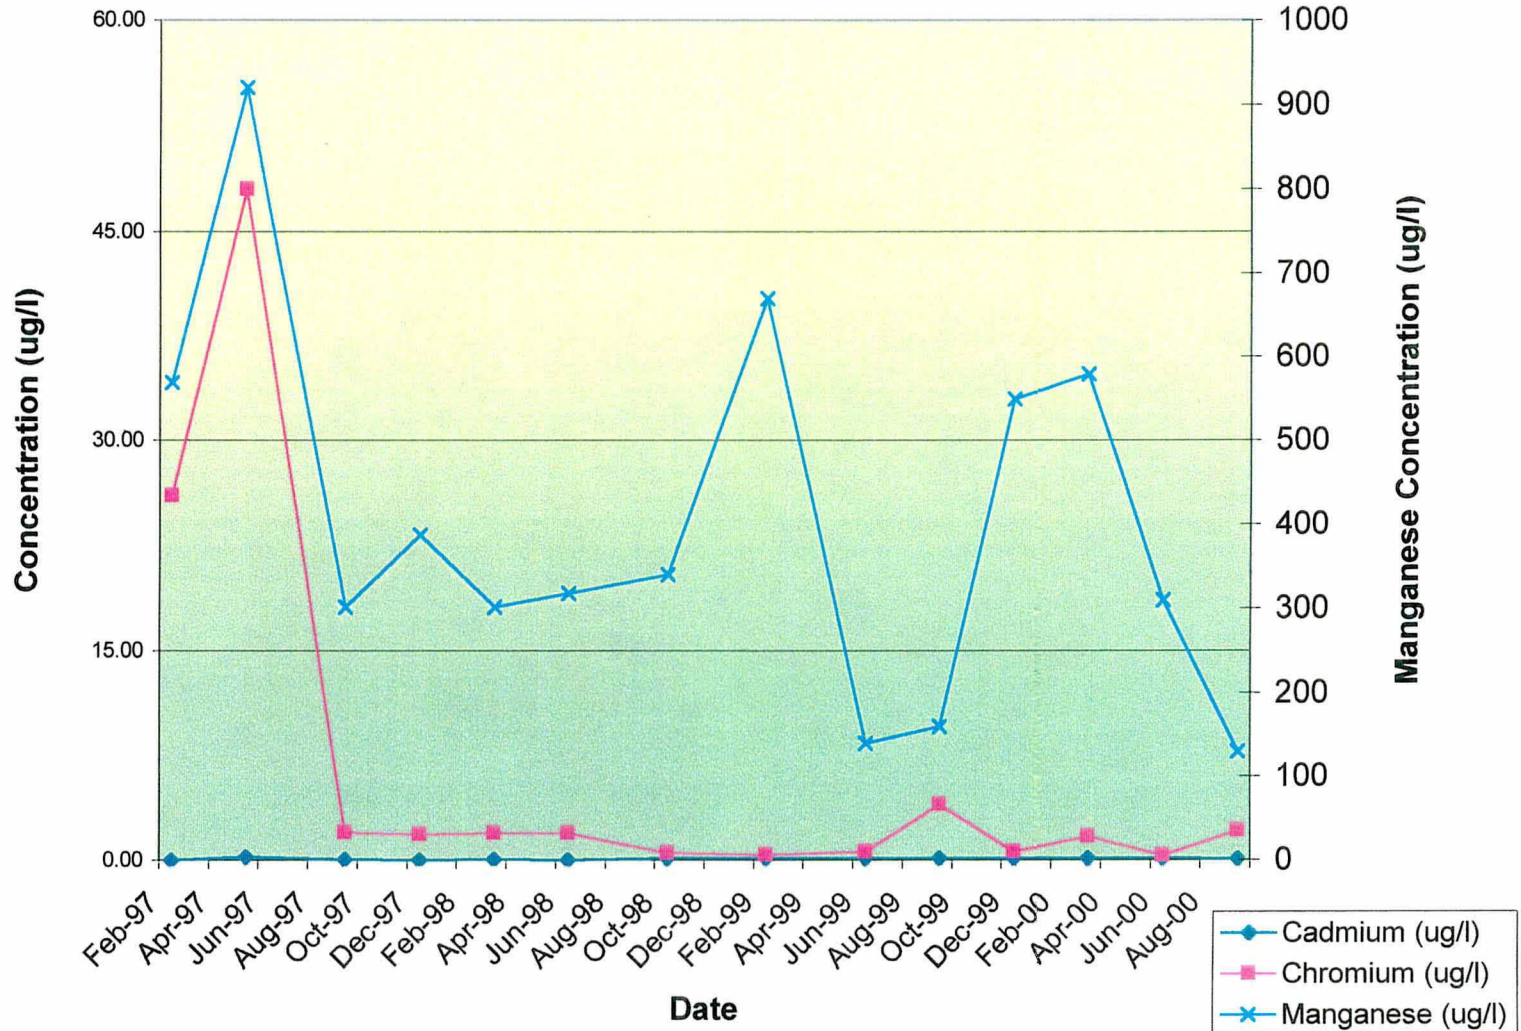


# Well W-103 / Concentration Vs. Time

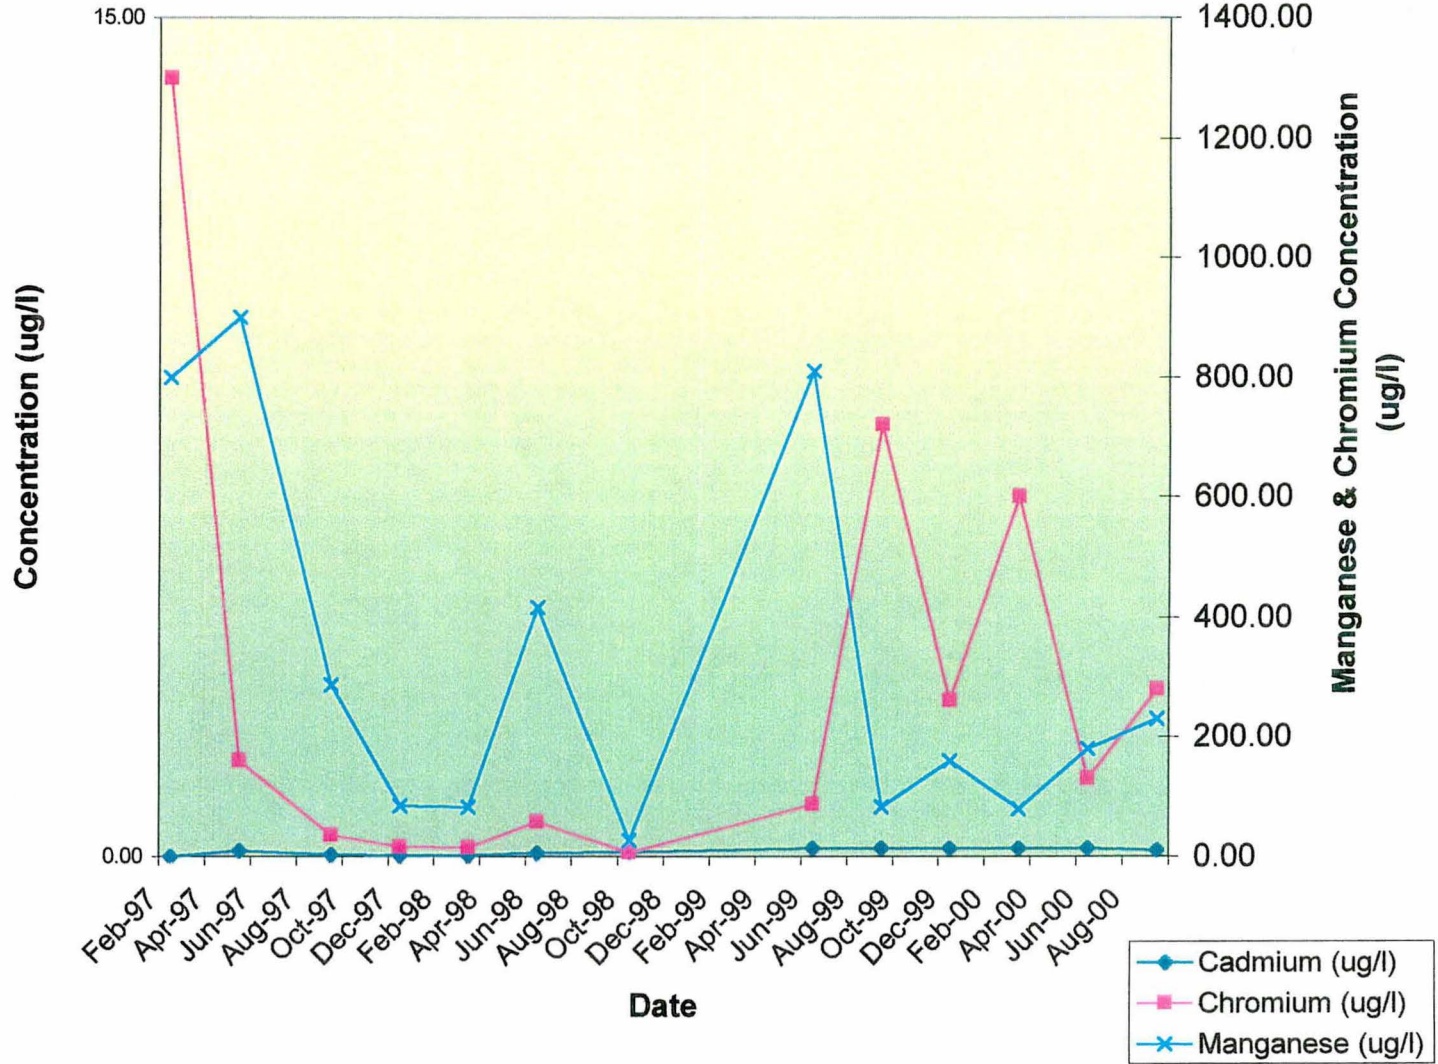

# Well W-104 / Concentration Vs. Time

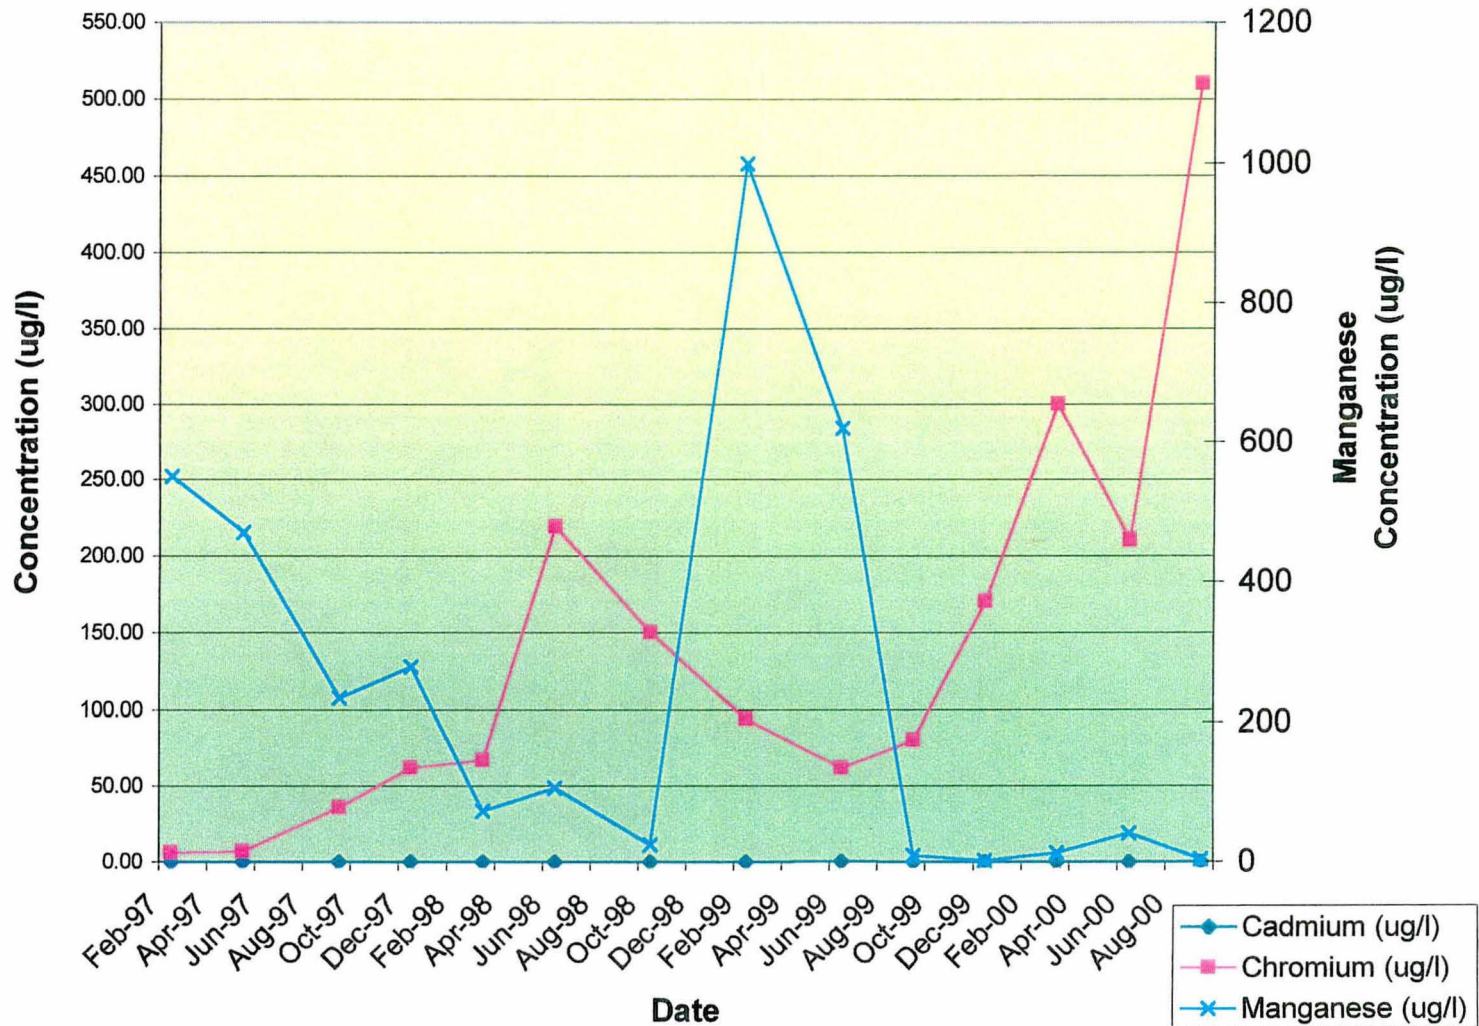


# Well W-105 / Concentration Vs. Time

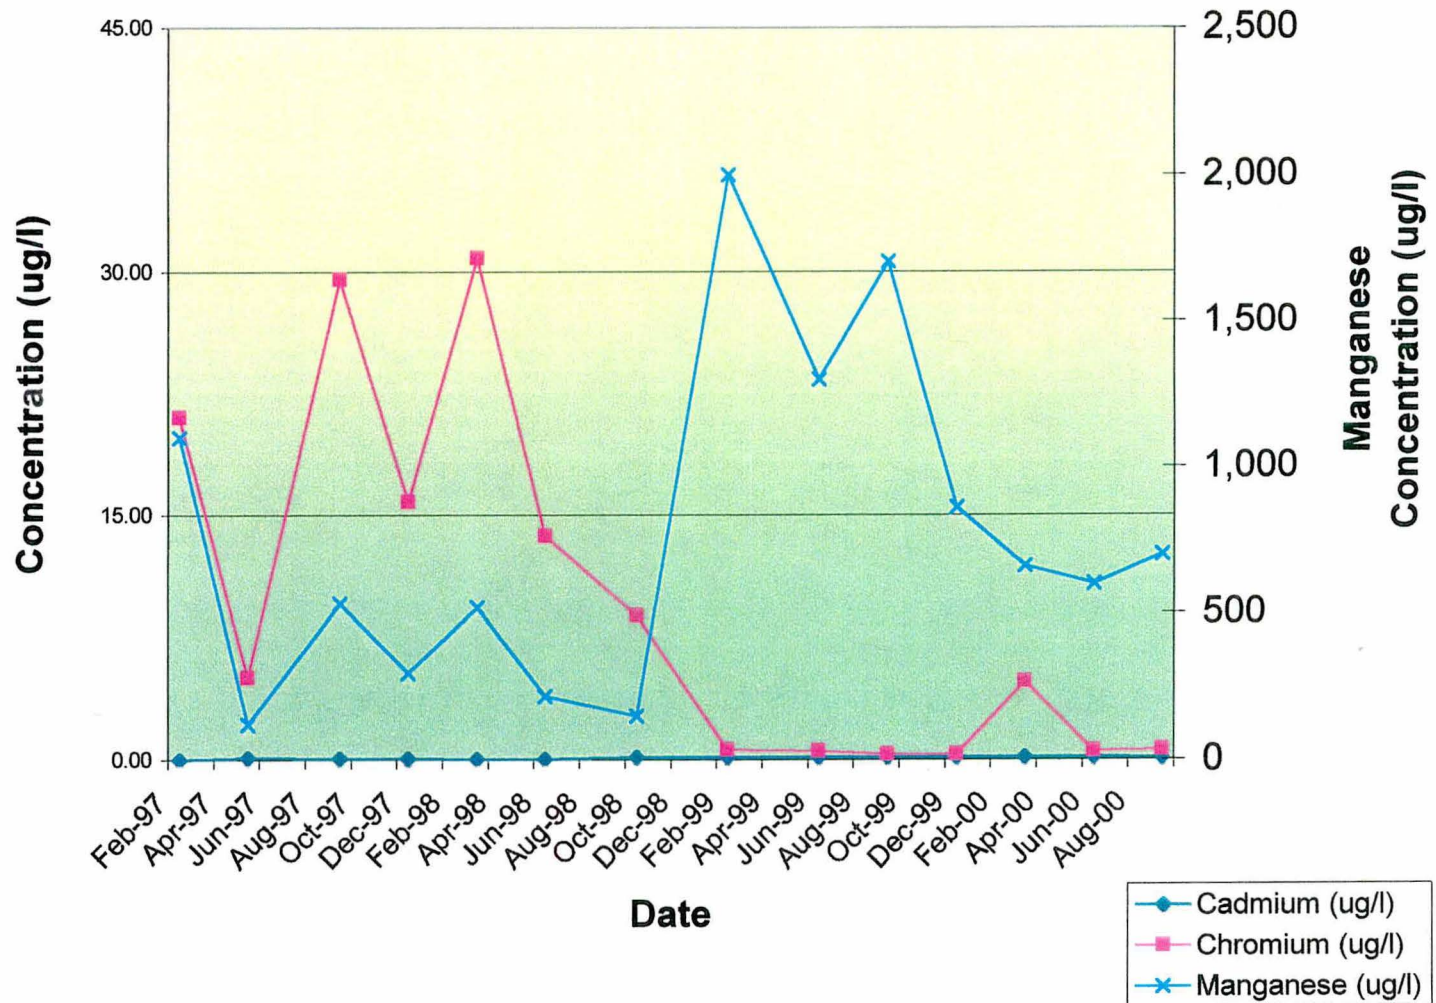





# Well W-106 / Concentration Vs. Time

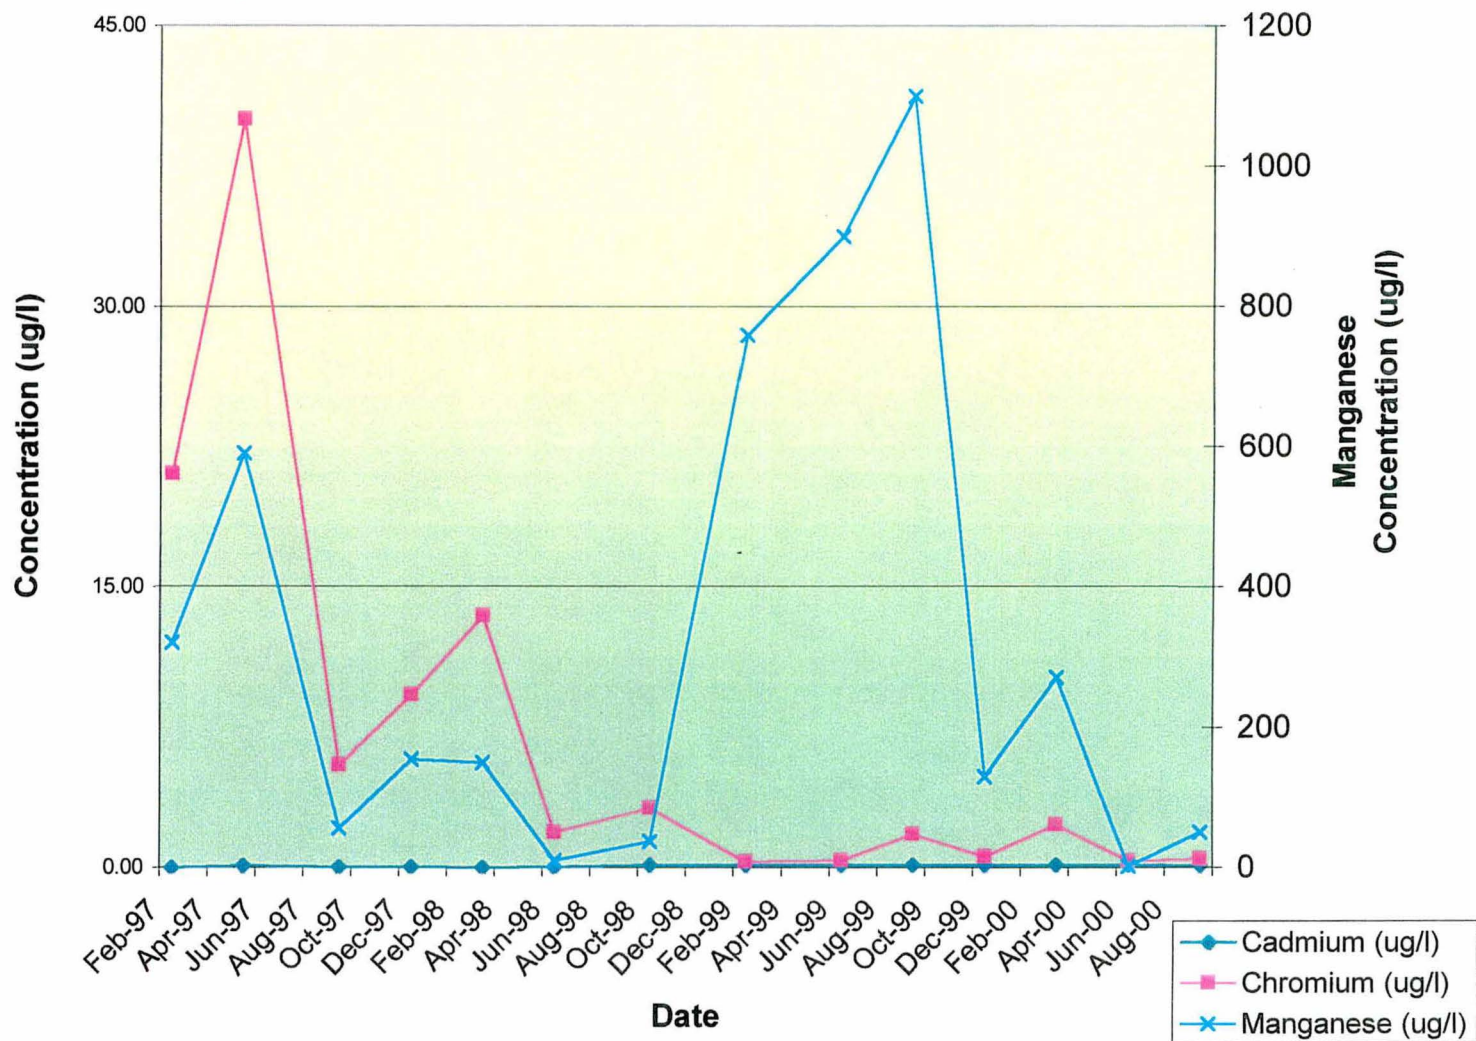

## Well W-107 / Concentration Vs. Time

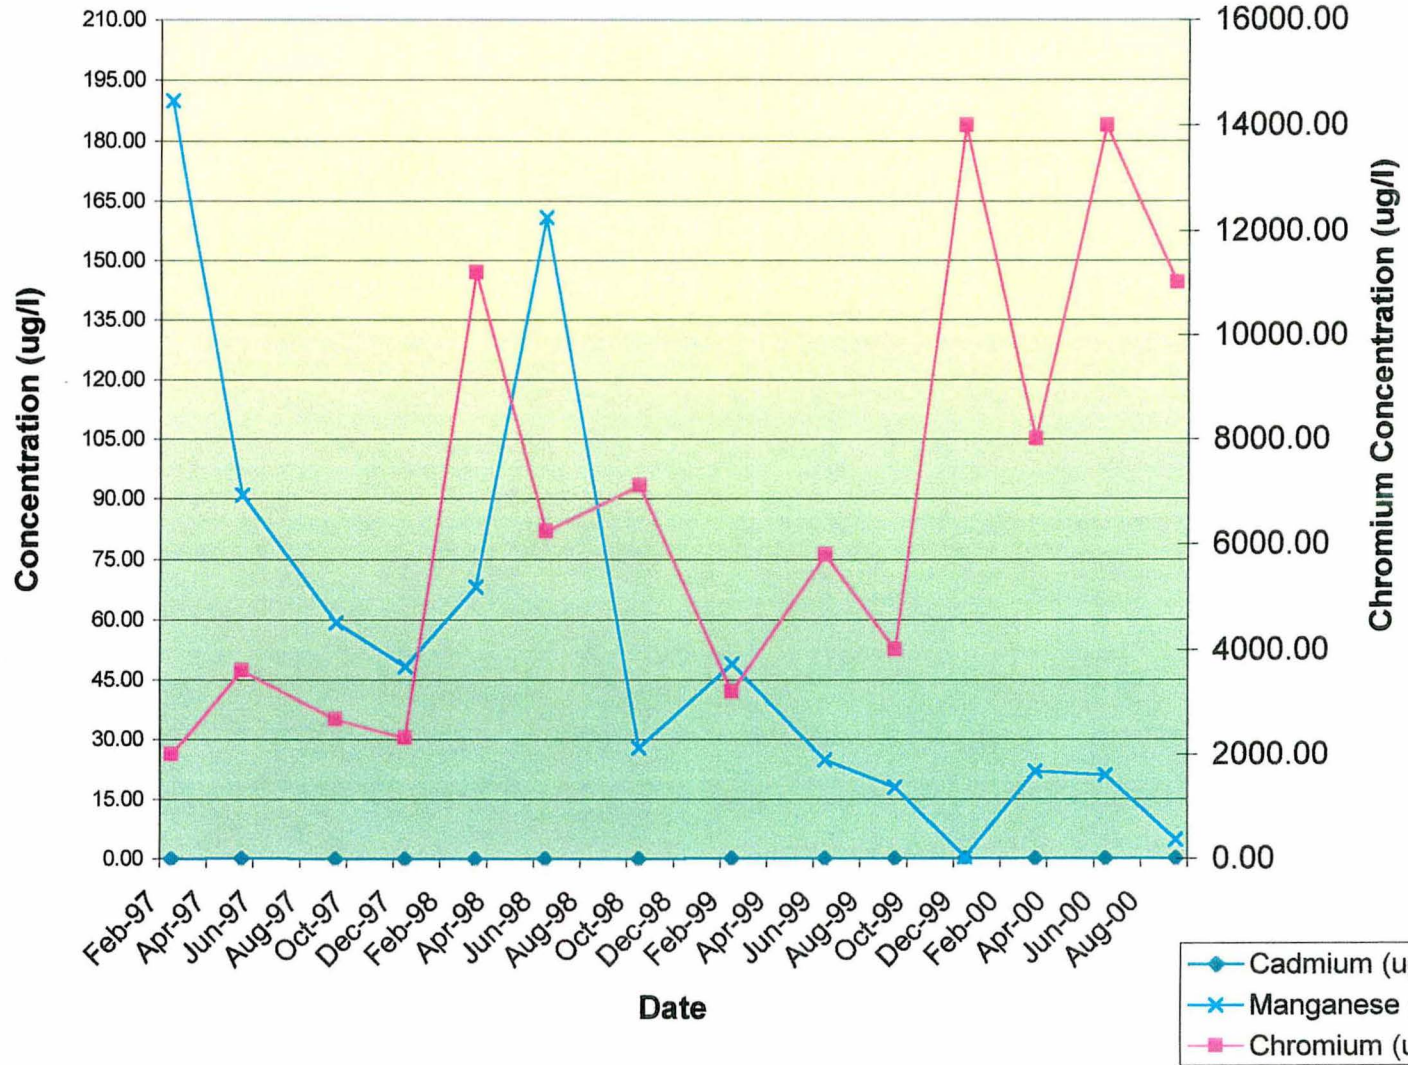

# Well W-108 / Concentration Vs. Time

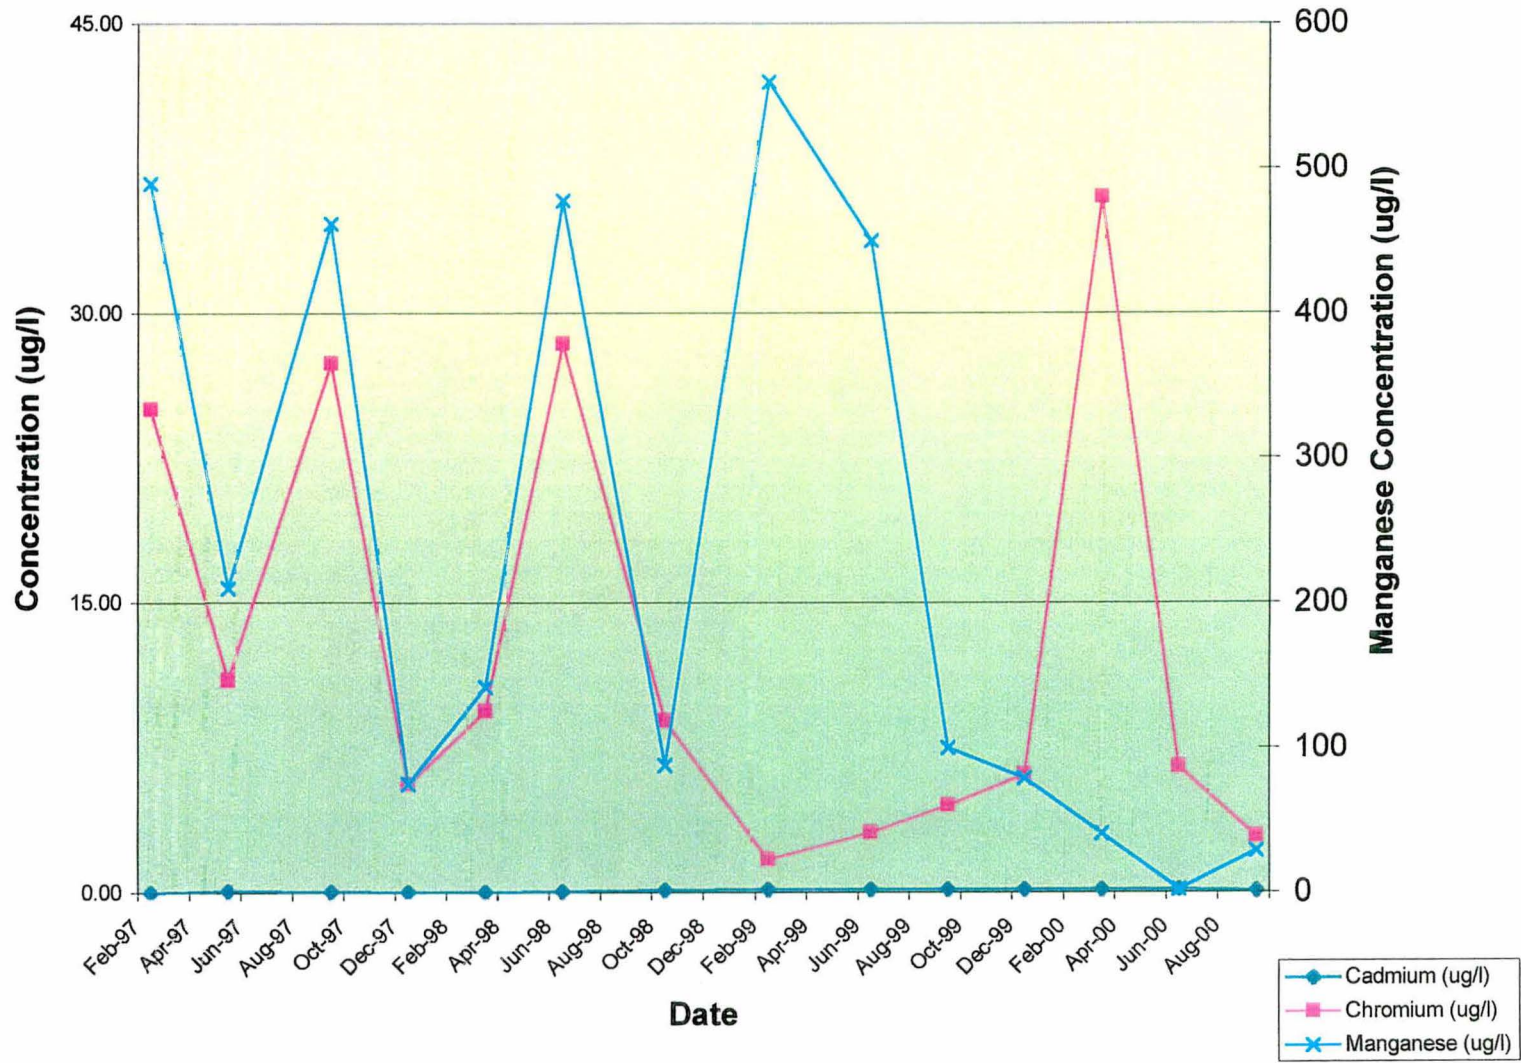

## APPENDIX B

---


Contaminant Versus Time Graph  
Detected VOC Compounds At MW-107 Graphs

## Appendix B

### Contaminant Versus Time Graph Detected VOC Compounds At MW-107 Graphs

Sample Date	1,1-Dichloroethane (ug/l)	1,1-Dichloroethene (ug/l)	cis-1,2-Dichloroethene (ug/l)	1,1,1-Trichloroethane (ug/l)	1,1,2-Trichloroethane (ug/l)	Trichloroethene (ug/l)
02/20/97	11	8.4	0.7	81	0.6	50
05/27/97	36	40	3.1	390	3.5	420
09/18/97	23.80	22.1	1.30	132	2.83	295
12/12/97	28.00	23	1.50	280	3	290
03/25/98	30.50	69	2.50	720	5	620
06/10/98	29.50	58	1.50	120	4	390
10/27/98	62	23.00	3.6	550	4.9	640
02/09/99	48	24	2.00	220	0.19	250
06/08/99	42	20	1.60	200	1.5	310
09/13/99	34	19	0.16	180	1.5	320
12/15/99	37	56	2.3	570	2.7	880
03/13/00	25	16	6	340	0.45	630
06/22/00	14	25	6	540	4.5	850
09/27/00	17	27	6	560	4.5	870

### Contamination Vs. Time / MW-107

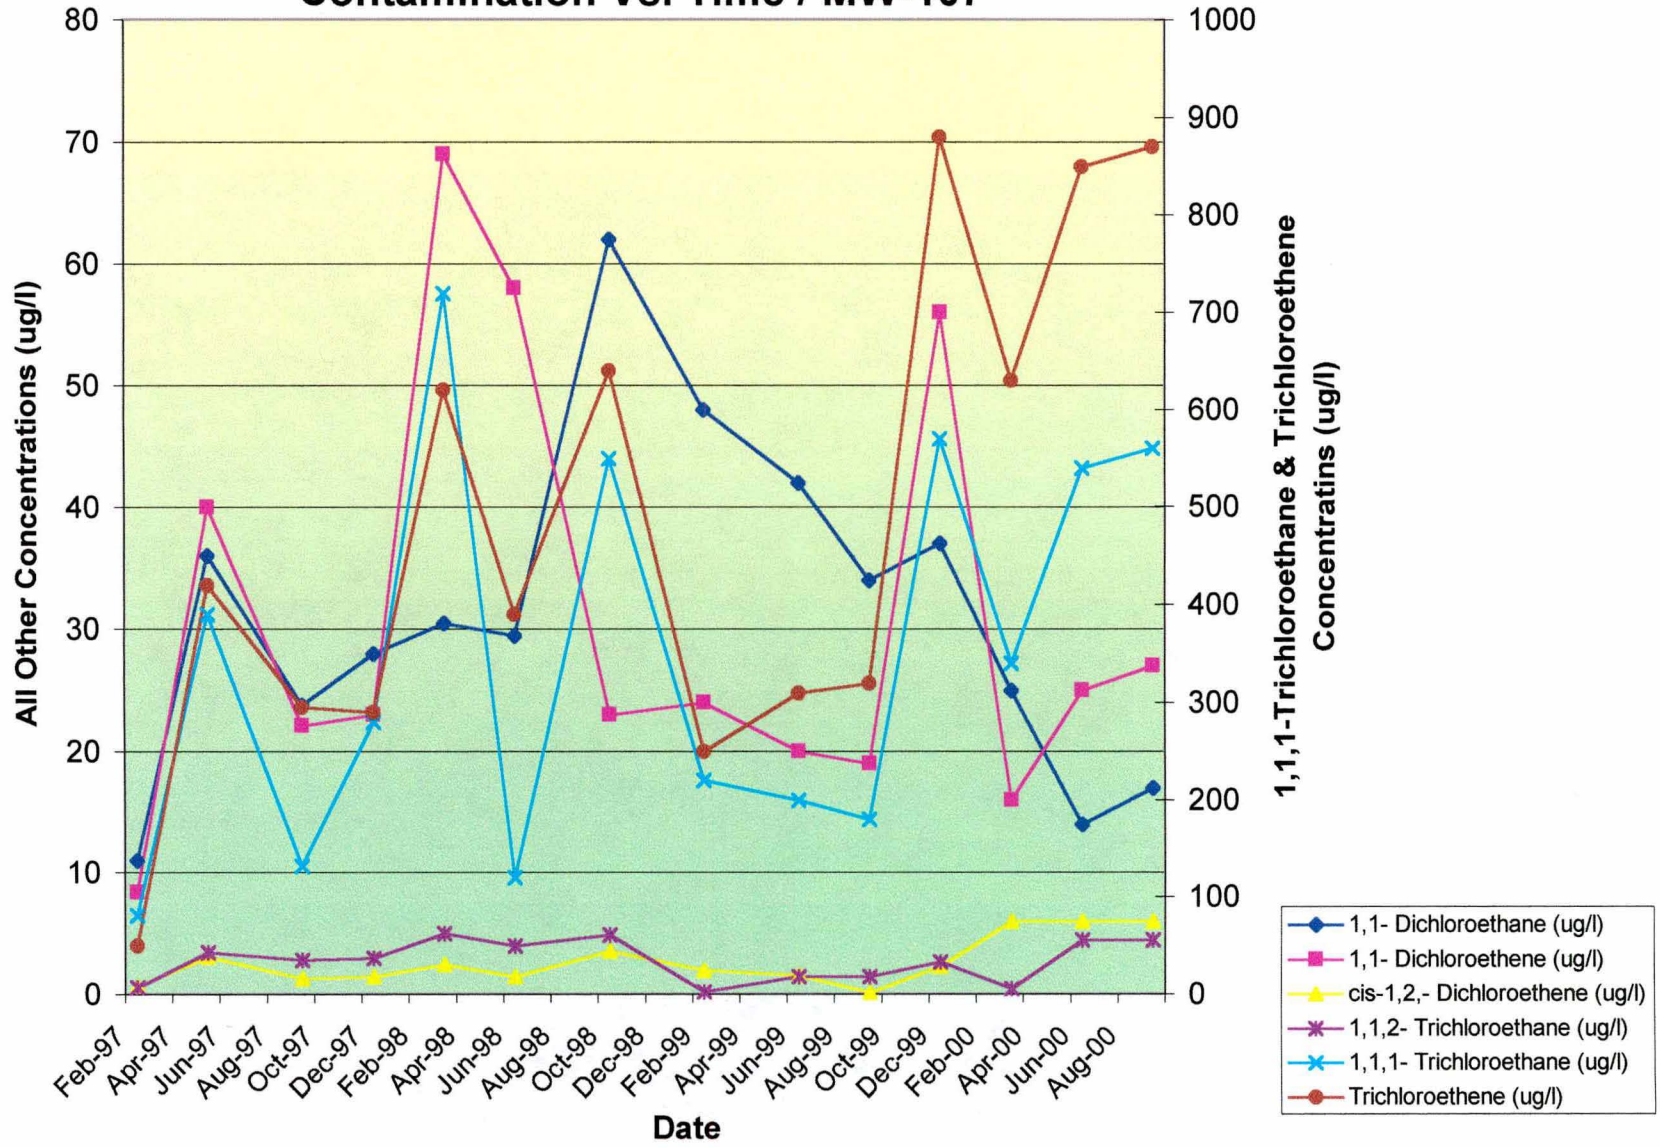

**APPENDIX C**

---

**Groundwater Elevations Versus Time  
All Wells**

Appendix C

**GROUNDWATER ELEVATIONS**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
MCO No. M050-90728.16

Well Name	Date Measured	Depth To Water (feet)	Reference Elevation (To Top PVC) (feet)	Groundwater Elevation (feet)
W-2	02/01/97	-		798.66
	05/01/97	-		801.01
	09/01/97	-		800.28
	12/01/97	-	804.66	797.69
	03/01/98	-		802.08
	06/01/98	-		799.38
	10/27/98	5.85		798.81
	02/08/99	4.50		800.16
	06/08/99	3.31		801.35
	09/13/99	5.78		798.88
	12/15/99	6.63		798.03
	03/13/00	1.60		803.06
	06/22/00	2.63		802.03
	09/27/00	3.28		801.38
W-8	02/01/97	-		797.22
	05/01/97	-		797.66
	09/01/97	-		798.01
	12/01/97	-	803.36	796.52
	03/01/98	-		798.16
	06/01/98	-		797.31
	10/27/98	6.41		796.95
	02/08/99	5.49		797.87
	06/08/99	4.38		798.98
	09/13/99	6.71		796.65
	12/15/99	6.91		796.45
	03/13/00	6.25		797.11
	06/22/00	6.42		797.34
	09/27/00	5.66		797.70
W-15	02/01/97	-		793.97
	05/01/97	-		796.92
	09/01/97	-		797.23
	12/01/97	-	803.76	795.52
	03/01/98	-		796.78
	06/01/98	-		796.32
	10/27/98	7.95		795.81
	02/08/99	9.19		794.57
	06/08/99	6.89		796.87
	09/13/99	7.85		795.91
	12/15/99	8.97		794.79
	03/13/00	7.80		795.96
	06/22/00	6.42		797.34
	09/27/00	6.30		797.46



**Appendix C**

**GROUNDWATER ELEVATIONS  
N.W. Mauthe Superfund Site - Appleton, Wisconsin  
MCO No. M050-90728.16**

Well Name	Date Measured	Depth To Water (feet)	Reference Elevation (To Top PVC) (feet)	Groundwater Elevation (feet)
MW-101	02/01/97	-		797.16
	05/01/97	-		799.99
	09/01/97	-		798.67
	12/01/97	-	807.59	798.21
	03/01/98	-		803.43
	06/01/98	-		800.48
	10/27/98	10.26		797.33
	02/08/99	11.91		795.68
	06/08/99	9.79		797.80
	09/13/99	10.35		797.24
	12/15/99	9.01		798.58
	03/13/00	12.67		794.92
	06/22/00	6.28		801.31
09/27/00	10.41		797.18	
MW-102	02/01/97	-		780.72
	05/01/97	-		780.89
	09/01/97	-		780.79
	12/01/97	-	804.45	780.95
	03/01/98	-		780.47
	06/01/98	-		780.72
	10/27/98	24.11		780.34
	02/08/99	23.84		780.61
	06/08/99	23.59		780.86
	09/13/99	23.70		780.75
	12/15/99	24.27		780.18
	03/13/00	24.00		780.45
	06/22/00	23.69		780.76
09/27/00	23.65		780.80	
MW-103	02/01/97	-		795.29
	05/01/97	-		791.83
	09/01/97	-		789.60
	12/01/97	-	803.74	787.78
	03/01/98	-		791.03
	06/01/98	-		789.13
	10/27/98	11.96		791.78
	02/08/99	10.24		793.50
	06/08/99	8.69		795.05
	09/13/99	9.79		793.95
	12/15/99	12.68		791.06
	03/13/00	9.63		794.07
	06/22/00	8.22		795.52
09/27/00	7.76		795.98	

Appendix C

**GROUNDWATER ELEVATIONS**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
**MCO No. M050-90728.16**

Well Name	Date Measured	Depth To Water (feet)	Reference Elevation (To Top PVC) (feet)	Groundwater Elevation (feet)
MW-104	02/01/97	-		792.94
	05/01/97	-		789.91
	09/01/97	-		798.59
	12/01/97	-	807.28	795.70
	03/01/98	-		799.46
	06/01/98	-		796.60
	10/27/98	10.51		796.77
	02/08/99	9.04		798.24
	06/08/99	7.49		799.79
	09/13/99	10.28		797.00
	12/15/99	10.78		796.50
	03/13/00	9.51		797.77
	06/22/00	8.41		798.88
	09/27/00	8.61		798.67
MW-105	02/01/97	-		793.74
	05/01/97	-		800.60
	09/01/97	-		800.37
	12/01/97	-	803.96	799.03
	03/01/98	-		800.08
	06/01/98	-		800.50
	10/27/98	5.41		798.55
	02/08/99	6.46		797.50
	06/08/99	3.04		800.92
	09/13/99	4.60		799.36
	12/15/99	5.28		798.68
	03/13/00	4.97		798.99
	06/22/00	3.06		800.90
	09/27/00	3.38		800.58
MW-106	02/01/97	-		794.75
	05/01/97	-		797.23
	09/01/97	-		796.91
	12/01/97	-	804.08	795.48
	03/01/98	-		797.37
	06/01/98	-		796.76
	10/27/98	8.12		795.96
	02/08/99	9.75		794.33
	06/08/99	6.72		797.36
	09/13/99	7.88		796.20
	12/15/99	8.71		795.37
	03/13/00	8.72		795.36
	06/22/00	6.87		797.21
	09/27/00	7.41		796.67

**Appendix C**

**GROUNDWATER ELEVATIONS  
N.W. Mauthe Superfund Site - Appleton, Wisconsin  
MCO No. M050-90728.16**


Well Name	Date Measured	Depth To Water (feet)	Reference Elevation (To Top PVC) (feet)	Groundwater Elevation (feet)
MW-107	02/01/97	-		788.23
	05/01/97	-		796.60
	09/01/97	-		797.64
	12/01/97	-	809.01	796.49
	03/01/98	-		796.68
	06/01/98	-		796.31
	10/27/98	10.71		798.30
	02/08/99	11.11		797.90
	06/08/99	11.04		797.97
	09/13/99	11.55		797.46
	12/15/99	11.66		797.35
	03/13/00	11.13		797.88
	06/22/00	10.69		798.32
09/27/00	12.36		796.65	
MW-108	02/01/97	-		798.36
	05/01/97	-		793.32
	09/01/97	-		790.53
	12/01/97	-	806.61	788.65
	03/01/98	-		795.59
	06/01/98	-		789.30
	10/27/98	6.98		799.63
	02/08/99	6.72		799.89
	06/08/99	5.80		800.81
	09/13/99	6.68		799.93
	12/15/99	6.87		799.74
	03/13/00	6.84		799.77
	06/22/00	6.28		800.33
09/27/00	6.31		800.30	
PZ-01	10/27/98	17.43	804.17	786.74
	02/08/99	18.24		785.93
	06/08/99	18.22		785.95
	09/13/99	18.25		785.92
	12/15/99	18.25		785.92
	03/13/00	18.25		785.92
	06/22/00	18.21		785.96
09/27/00	18.21		785.96	
PZ-02	10/27/98	14.66	803.64	788.98
	02/08/99	14.70		788.94
	06/08/99	14.70		788.94
	09/13/99	14.74		788.90
	12/15/99	14.72		788.92
	03/13/00	14.76		788.88
	06/22/00	14.41		789.23
09/27/00	14.43		789.21	

Appendix C

**GROUNDWATER ELEVATIONS**  
**N.W. Mauthe Superfund Site - Appleton, Wisconsin**  
MCO No. M050-90728.16

Well Name	Date Measured	Depth To Water (feet)	Reference Elevation (To Top PVC) (feet)	Groundwater Elevation (feet)
PZ-03	10/27/98	22.71	803.62	780.91
	02/08/99	23.74		779.88
	06/08/99	23.74		779.88
	09/13/99	23.55		780.07
	12/15/99	23.52		780.10
	03/13/00	23.30		780.24
	06/22/00	23.40		780.22
	09/27/00	20.21		783.41
	PZ-04	10/27/98	15.18	807.30
02/08/99		23.61		783.69
06/08/99		21.69		785.61
9/13/99		23.87		783.43
12/15/99		23.80		783.50
03/13/00		25.77		781.53
06/22/00		22.51		784.79
09/27/00		19.60		787.70

# Groundwater Elevations Vs. Time

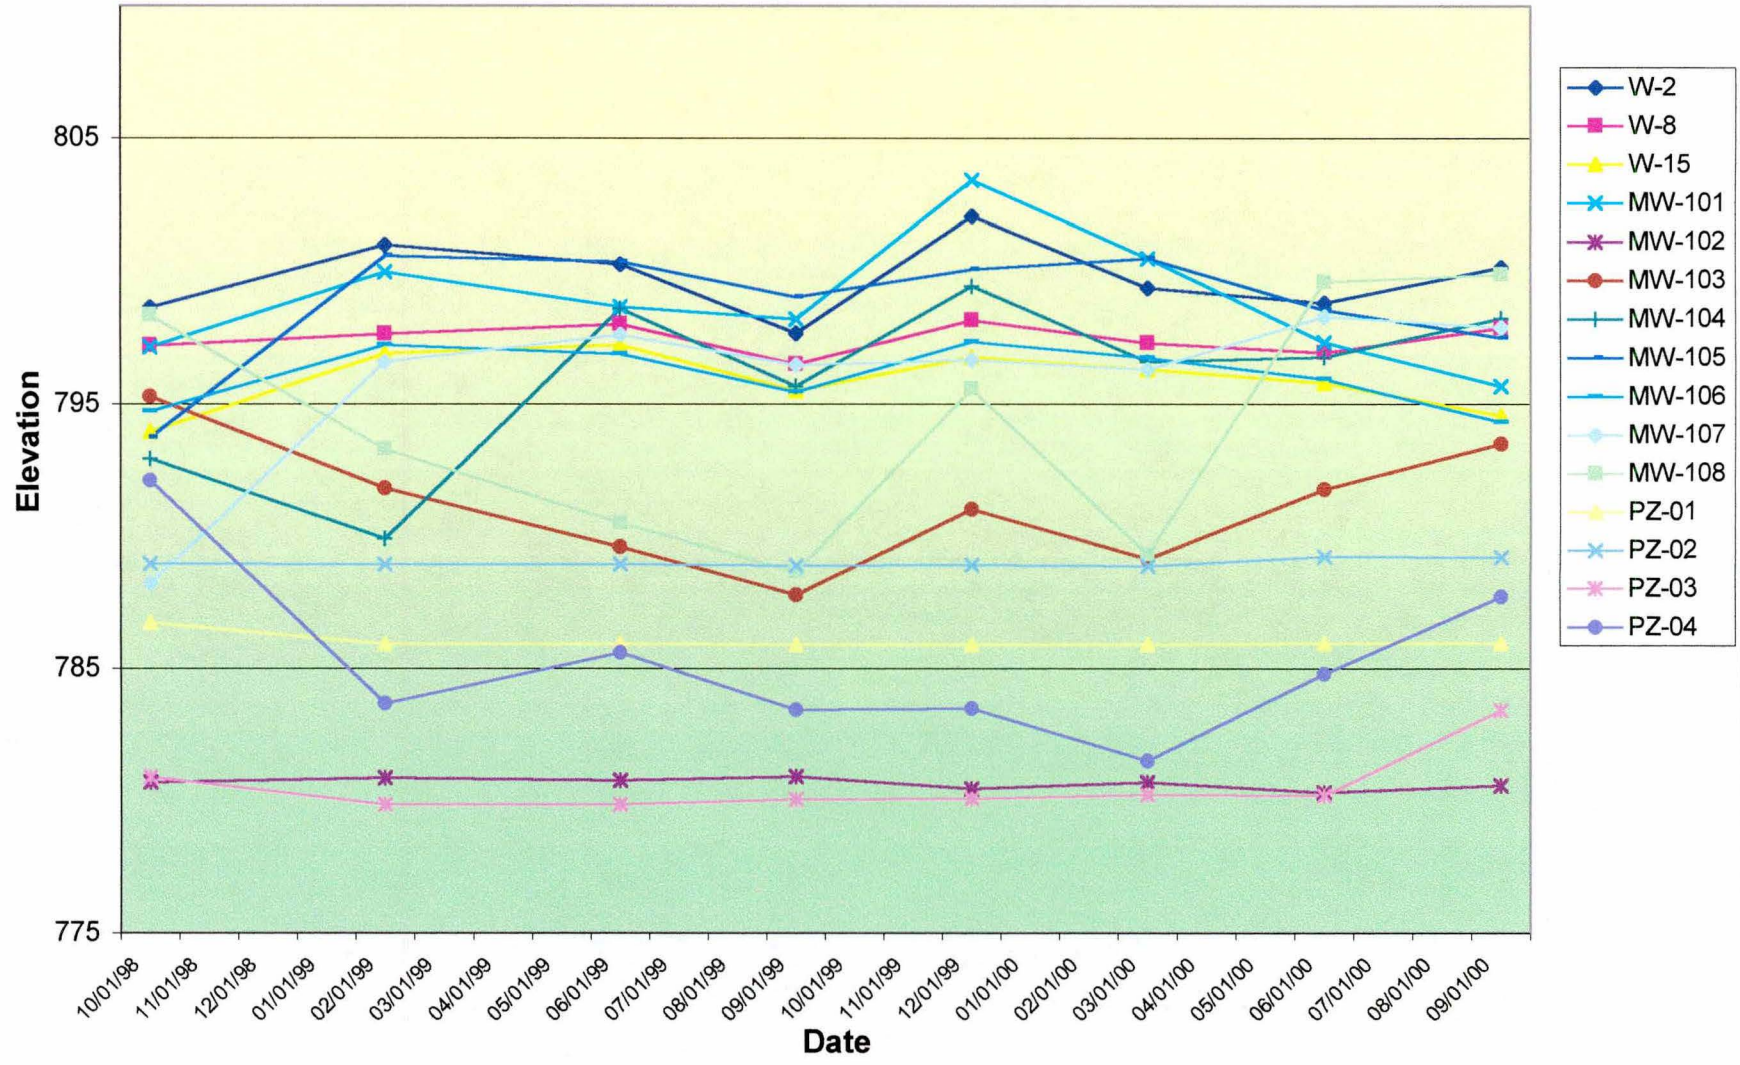

## APPENDIX D

---

### Operation & Maintenance Cost Summary

**Appendix D**

**Summary Of Operation & Maintenance Costs  
N.W. Mauthe Superfund Site - Appleton, Wisconsin  
MCO. No. M050-90728.16**

O&M Cost Category	Oct. 99	Nov. 99	Dec. 99	Jan. 00	Feb. 00	Mar. 00	Apr. 00	May.00	June. 00	July. 00	Aug. 00	Sept. 00	Totals
<b>LABOR COSTS</b>													
Routine Labor (Including Alarms, Groundwater Sampling)	2,888.61	3,107.41	2,192.82	2,061.37	3,365.42	2,678.49	3,137.35	2,677.33	1,945.80	2,213.99	2,762.14	2,763.19	31,793.92
Building & Equipment Maintenance	0.00	0.00	64.35	658.13	832.41	382.80	620.82	571.14	262.13	666.48	910.50	925.49	5,894.25
Labor - Subtotal	2,888.61	3,107.41	2,257.17	2,719.50	4,197.83	3,061.29	3,758.17	3,248.47	2,207.93	2,880.47	3,672.64	3,688.68	37,688.17
<b>ANALYTICAL SERVICES</b>													
City Monitoring (Semi-Annual) - System Outfall						323.40					323.40		646.80
Quarterly Monitoring - System Outfall & Groundwater Wells	2,371.20			628.50			1,897.40			618.00			5,515.10
Analytical - Subtotal	2,371.20	0.00	0.00	628.50	0.00	323.40	1,897.40	0.00	0.00	618.00	323.40	0.00	6,161.90
<b>CHEMICALS</b>													
Nitrogen Cylinder Rental & Gas	7.16	50.25											57.41
Sodium Hydroxide (55-Gal. Drums)									207.81			199.02	406.83
Ferrous Sulfate (55-Gal. Drums)						300.04			291.26			316.55	907.85
Chemicals - Subtotal	7.16	50.25	0.00	0.00	0.00	300.04	0.00	0.00	499.07	0.00	0.00	515.57	1,372.09
<b>UTILITY SERVICES</b>													
Electrical & Natural Gas	261.67	332.20	332.20	332.20	332.20	332.20	332.20	188.10	188.10	188.10	188.10	188.10	3,195.37
Telephone	25.04	20.93	23.10	23.33	23.22	23.73	24.24	22.82	25.28	25.42	25.81	25.35	288.27
Utilities - Subtotal	286.71	353.13	355.36	355.53	355.42	355.93	356.44	210.92	213.38	213.52	213.91	213.45	3,483.64
<b>CITY WATER &amp; SEWER FEES</b>													
Water Charge, Sewer Charge, Storm Water Charge		73.02				129.24			79.06			80.53	361.85
Sewer Volume Charge		372.14				257.06			577.79			976.02	2,183.01
Subtotal - City Fees	0.00	445.16	0.00	0.00	0.00	386.30	0.00	0.00	656.85	0.00	0.00	1,056.55	2,544.86
<b>MISCELLANEOUS</b>													
			50.04	19.79				75.33			61.91	88.43	295.50
<b>TOTAL O&amp;M COSTS</b>	<b>5,553.68</b>	<b>3,955.95</b>	<b>2,662.57</b>	<b>3,723.32</b>	<b>4,553.25</b>	<b>4,426.96</b>	<b>6,012.01</b>	<b>3,534.72</b>	<b>3,577.23</b>	<b>3,711.99</b>	<b>4,271.86</b>	<b>5,562.68</b>	<b>51,546.16</b>
<b>ADMINISTRATIVE COSTS ALLOWANCE</b>													
(Monthly & Semi-Annual Reporting, Data Management & Recordkeeping)	750.00	750.00	750.00	750.00	750.00	750.00	750.00	750.00	750.00	750.00	750.00	750.00	9,000.00
<b>TOTAL O&amp;M INCLUDING ADMINISTRATION</b>	<b>6,303.68</b>	<b>4,705.95</b>	<b>3,412.57</b>	<b>4,473.32</b>	<b>5,303.25</b>	<b>5,176.96</b>	<b>6,762.01</b>	<b>4,284.72</b>	<b>4,327.23</b>	<b>4,461.99</b>	<b>5,021.86</b>	<b>6,312.68</b>	<b>60,546.16</b>

NOTES: 1) Nitrogen costs include cylinder rented and estimated gas costs. November 2000 costs represent year lease of cylinder.  
2) Administrative costs are based upon the total budgeted costs divided by 12-months.

## APPENDIX E

---

Operation & Maintenance Report / Form 4400-194



OPERATION, MAINTENANCE, MONITORING  
AND OPTIMIZATION REPORTING OF  
SOIL AND GROUNDWATER REMEDIATION SYSTEMS

**PURPOSE AND APPLICABILITY OF THIS FORM:** Completion of this form is required under s. NR 724.13(e), Wis. Adm. Code. Use of this form is mandatory. Failure to submit this form as required is a violation of s. NR 724.13, Wis. Adm. Code, and is subject to the penalties in s. 144.99, Wis. Stats. This form must be submitted every six months for active soil and groundwater remediation projects and every twelve months for passive (natural attenuation) remediation projects that are regulated under the NR 700 series of Wis. Adm. Code. Specifically, for sites meeting any of the following criteria:

- Soil or groundwater remediation projects that report progress in accordance with s. NR 700.11(1), Wis. Adm. Code.
- Soil or groundwater remediation projects that report progress in accordance with s. NR 724.13(3), Wis. Adm. Code. (Note: s. NR 724.13(3) requires progress reports for operation and maintenance of active systems to be submitted every three months however the Department considers submittal of this form every six months to satisfy the requirements of the rules, unless otherwise directed by the Department on a site specific basis.)
- Soil or groundwater remediation projects that report progress in accordance with s. NR 724.17(3), Wis. Adm. Code. (Note: s. NR 724.17(3) requires progress reports every time that samples are collected however the Department considers submittal of this form every twelve months to satisfy the requirements of the rules for monitoring natural attenuation, unless otherwise directed by the Department on a site specific basis.)

Submittal of this form is not a substitute for reporting required by Department programs such as Wastewater or Air Management. Personally identifiable information on this form is not intended to be used for any other purpose than tracking progress of the remediation by the Bureau for Remediation and Redevelopment.

Please refer to the instructions that are attached to the back of these forms starting on page INS-1. In all cases, when asked to "explain," those explanations are to be included on separate sheets of paper. Explanations must include a title that refers to the page and item number, for example: Page GI-2, C.1.a.

**A. GENERAL INFORMATION:**

1. Site name: N.W. Mantle Superfund Site
2. Reporting period from: October 1, 1995 To: September 30, 2000 Days in period: 365
3. Regulatory agency (enter DNR, DCOM, DATCP and/or other): WONR / U.S. EPA
4. DNR issued site number: BRRTS ID # 02-45-000127
5. State reimbursement fund claim number and fund name (if not applicable, enter NA): NA
6. Site location:
  - a. DNR region and county: Northeast Region Outagamie County
  - b. Street address and municipality: 725 South Outagamie Street, Appleton, WI
  - c. Township, range, section and quarter quarter section: NE 1/4 of NW 1/4 of Section 34  
Township 21 North, Range 17 East
7. Responsible party:
  - a. Name: Carol Maunthe (WONR contact Jennifer HuHua)
  - b. Mailing address: WONR 3369 West Brewster Street  
Appleton, WI 54914-1602
  - c. Phone number: (920) 832-1803
8. Consultant:
  - a. Company name: McMahan Associates, Inc
  - b. Mailing address: P.O. Box 1025, 1445 McMahan Drive  
Neenah, WI 54957-1025
  - c. Phone number: (920) 751-4200
9. Contaminants: Chromium, VOC's
10. Soil types (USCS or USDA): Clay / Silty Clay
11. Hydraulic conductivity (cm/sec):  $1 \times 10^{-7}$
12. Average linear velocity of groundwater (ft/yr): 10.34

GENERAL SITE INFORMATION, CONTINUED

SITE NAME AND REPORTING PERIOD:

Site name: N.W. Maunke Superfund Site

Reporting period from: October 1, 1999 To: September 30, 2000 Days in period: 365

A. GENERAL INFORMATION (CONTINUED):

13. If soil is treated ex situ, is the treatment location off site? (Y/N) If yes, give location:
- a. DNR region and county: \_\_\_\_\_
  - b. Township, range, section and quarter quarter section: \_\_\_\_\_

B. REMEDIATION METHOD: Only submit pages that apply to an individual site. Check all that apply:

- Groundwater extraction (submit a completed page GW-1).
- Free product recovery (submit a completed page GW-1).
- In situ air sparging (submit a completed page GW-2).
- Groundwater natural attenuation (submit a completed page GW-3).
- Other groundwater remediation method (submit a completed page GW-4).
- Soil venting (including soil vapor extraction and bioventing, submit a completed page IS-1).
- Soil natural attenuation (submit a completed page IS-2).
- Other in situ soil remediation method (submit a completed page IS-3).
- Biopiles (submit a completed page ES-1).
- Landspreading/thinspreading of petroleum contaminated soil (submit a completed page ES-2).
- Other ex situ soil remediation method (submit a completed page ES-3).

C. GENERAL EFFECTIVENESS EVALUATION FOR ALL ACTIVE SYSTEMS: If the remediation is active (not natural attenuation), complete this subsection.

- 1. Is the system operating at design rates and specifications? (Y/N): \_\_\_\_\_  
If the answer is no, explain whether or not modifications are necessary to achieve the goal that was previously established in design.
- 2. Are modifications to the system warranted to improve effectiveness? (Y/N) If yes, explain: \_\_\_\_\_
- 3. Is natural attenuation an effective low cost option at this time? (Y/N) \_\_\_\_\_
- 4. Is closure sampling warranted at this time? (Y/N) \_\_\_\_\_
- 5. Are there any modifications that can be made to the remediation to improve cost effectiveness? (Y/N) If yes, explain: \_\_\_\_\_

D. ECONOMIC AND COST DATA TO DATE:

- 1. Total investigation costs (\$): NA
- 2. Implementation costs (design, capital and installation costs, excluding investigation costs) (\$): NA
- 3. Total costs during the previous reporting period (\$): 80,189
- 4. Total costs during this reporting period (\$): 74,507
- 5. Total anticipated costs for the next reporting period (\$): 76,048
- 6. Are any unusual or one-time costs listed in the reporting periods covered by D.3., D.4. or D.5. above? (Y/N) If yes explain: \_\_\_\_\_
- 7. If close out is anticipated within 12 months, estimated costs for project closeout (\$): NO

OPERATION, MAINTENANCE, MONITORING  
AND OPTIMIZATION REPORTING OF  
SOIL AND GROUNDWATER REMEDIATION SYSTEMS

GENERAL SITE INFORMATION, CONTINUED

SITE NAME AND REPORTING PERIOD:

Site name: N.W. Maunle Superfund Site  
Reporting period from: October 1, 1999 To: September 30, 2001 Days in period: 365

E. NAME(S), SIGNATURE(S) AND DATE OF PERSON(S) SUBMITTING FORM: Legibly print name, date and sign. Only persons qualified to submit reports under ch. NR 712 Wis. Adm. Code are to sign this form.

Registered Professional Engineers:

I (print name) THOMAS J. KISPERT, hereby certify that I am a registered professional engineer in the State of Wisconsin, registered in accordance with the requirements of ch. A-E 4, Wis. Adm. Code; that this document has been prepared in accordance with the rules of Professional Conduct in ch. A-E 8, Wis. Adm. Code; and that, to the best of my knowledge, all information contained in this document is correct and the document was prepared in compliance with all applicable requirements in chs. NR 700 to 726, Wis. Adm. Code.

Signature, title, P.E. number and date: *Thomas J. Kispert* Associate P.E. 26225 3-2-01

Hydrogeologists:

I (print name) Stuart A. Boerst, hereby certify that I am a hydrogeologist as that term is defined in s. NR 712.03(1), Wis. Adm. Code, and that, to the best of my knowledge, all information contained in this document is correct and the document was prepared in compliance with all applicable requirements in chs. NR 700 to 726, Wis. Adm. Code.



Signature, title and date: *Stuart A. Boerst*, Hydrogeologist, March 2, 2001

Scientists:

I (print name) \_\_\_\_\_, hereby certify that I am a scientist as that term is defined in s. NR 712.03(3), Wis. Adm. Code, and that, to the best of my knowledge, all information contained in this document is correct and the document was prepared in compliance with all applicable requirements in chs. NR 700 to 726, Wis. Adm. Code.

Signature, title and date: \_\_\_\_\_

Professional Seal(s), if applicable:

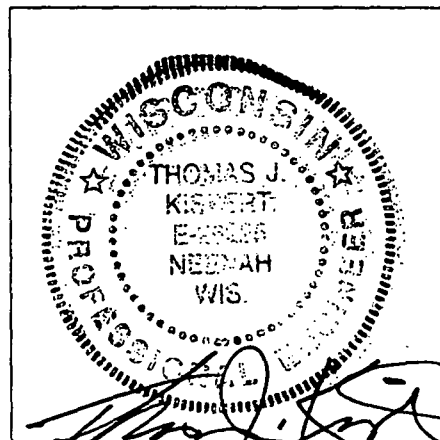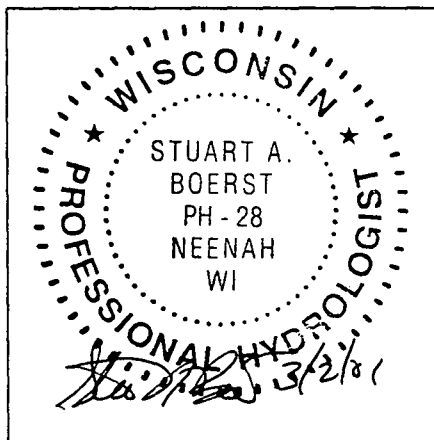

OPERATION, MAINTENANCE, MONITORING  
AND OPTIMIZATION REPORTING OF  
SOIL AND GROUNDWATER REMEDIATION SYSTEMS

GROUNDWATER PUMP AND TREAT SYSTEMS AND FREE PRODUCT RECOVERY SYSTEMS

SITE NAME AND REPORTING PERIOD:

Site name: N.W. Maunthe Superfund Site  
Reporting period from: October 1, 1999 To: September 30, 2000 Days in period: 365  
Date that the system was first started up: January 14, 1997

A. GROUNDWATER EXTRACTION SYSTEM OPERATION:

1. Total number of groundwater extraction wells or trenches available and the number in use during period: 2/2
2. Number of days of operation (only list the number of days the system actually operated, if unknown explain): 365
3. System utilization in percent (days of operation divided by reporting time period multiplied by 100). If < 80%, explain: 100
4. Quantity of groundwater extracted during this time period (gallons): 748,306
5. Average groundwater extraction rate (gpm): 1.4
6. Quantity of dissolved phase contaminants removed during this time period in pounds: 7.8 pounds

B. FREE PRODUCT RECOVERY SYSTEM OPERATION:

1. Is free product (nonaqueous phase liquid) being recovered at this site? (Y/N) If yes, list method: (N)
2. Quantity of free product extracted during this time period (gallons, enter none if none): None
3. Average free product extraction rate (gpd): NA

C. SYSTEM EFFECTIVENESS EVALUATION:

1. Is a contaminated groundwater plume fully contained in the capture zone? (Y/N) If no, explain: (N)
2. If free product is present, is the free product fully contained in capture zone? (Y/N) If no, explain: NA
3. If free product is present in any wells at the site, but free product was not recovered during reporting period, explain.
4. If free product is not present, determine the single contaminant that requires the greatest percent reduction to achieve ch. NR 140 ES and PAL. Perform this calculation for all contaminants that were present at the site that have ch. NR 140 standards. Use the highest contaminant concentration measured in any sampling points during reporting period. If free product is present, write "FREE PRODUCT" in C.4.a.
  - a. Contaminant: Chromium 14,000 ug/L
  - b. Percent reduction necessary to reach ch. NR 140 ES and PAL: ES 99.3% PAL 100%
  - c. Maximum contaminant concentration level in any monitoring well of that contaminant (ug/L): 14,000 ug/L MW-107
  - d. Maximum contaminant concentration level in any extraction well of that contaminant (ug/L): NA
  - e. If the maximum concentration in a monitoring well is more that one order of magnitude above the concentration measured in an extraction well, explain why the extracted groundwater contamination levels are significantly less than the levels at other locations within the aquifer.

D. ADDITIONAL ATTACHMENTS: Attach the following to this form:

- Most recent report to the DNR Wastewater Program, if applicable.
- Groundwater contour map with capture zone indicated.
- Groundwater contaminant distribution map (may be combined with contour map).
- Graph of cumulative contaminant removal, if both free product recovery and ground water extraction are used, provide separate graphs.
- Time versus groundwater contaminant concentration graphs for the contaminant listed in C.4.a. (above), as follows:
  - Graph of contaminant concentrations versus time for each extraction well in use during the period.
  - Graph of contaminant concentrations versus time for the monitoring well with the greatest level of contamination.
- Groundwater contaminant chemistry table.
- Groundwater elevations table.
- System operational data table.

OPERATION, MAINTENANCE, MONITORING  
AND OPTIMIZATION REPORTING OF  
SOIL AND GROUNDWATER REMEDIATION SYSTEMS

OTHER GROUNDWATER REMEDIATION METHODS

SITE NAME AND REPORTING PERIOD:

Site name: N.W. Maunthe Superfund Site

Reporting period from: October 1, 1999 To: September 30, 2000 Days in period: 365

Date that the system was first started up: January 4, 1997

A. EFFECTIVENESS EVALUATION:

1. If free product is not present, determine the single contaminant that requires the greatest percent reduction to achieve ch. NR 140 ES and PAL. Perform this calculation for all contaminants that were present at the site that have ch. NR 140 standards. Use the highest contaminant concentration measured in any sampling points during reporting period. If free product is present, write "FREE PRODUCT" in A.1.a.

a. Contaminant: Chromium

b. Percent reduction necessary: ES 99.3% PAL 100%

c. Maximum contaminant concentration level in any monitoring well ( $\mu\text{g/L}$ ): 14,000  $\mu\text{g/L}$  / MW-107

2. Is the size of the plume increasing, stabilized, or decreasing: Stabilized

3. Describe the method used to remediate groundwater at the site.

See Section IIA of Enclosed Report

4. List any additional information required by the DNR for this method for this site:

\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

B. ADDITIONAL ATTACHMENTS: Attach the following to this form:

- Groundwater contour map.
- Groundwater contaminant distribution map (may be combined with contour map).
- When contaminants are aerobically biodegradable, attach a dissolved oxygen in groundwater map (dissolved oxygen may be combined with the contaminant data on a single map).
- Graph of contaminant concentrations versus time for the contaminant listed in A.1.a. (above) for the monitoring point with the greatest level of contamination.
- Groundwater contaminant chemistry table.
- Groundwater elevations table.
- Any other attachments required by the DNR for this remediation method.

OPERATION, MAINTENANCE, MONITORING  
AND OPTIMIZATION REPORTING OF  
SOIL AND GROUNDWATER REMEDIATION SYSTEMS

SOIL VENTING (INCLUDING BOTH SOIL VAPOR EXTRACTION AND BIOVENTING)

SITE NAME AND REPORTING PERIOD:

Site name: \_\_\_\_\_

Reporting period from: \_\_\_\_\_ To: \_\_\_\_\_ Days in period: \_\_\_\_\_

Date that the system was first started up: \_\_\_\_\_

A. SOIL VENTING SYSTEM OPERATION:

1. Number of air extraction wells available and number of wells actually in use during the period: \_\_\_\_\_

2. Number of days of operation (only list the number of days the system actually operated, if unknown explain): \_\_\_\_\_

3. System utilization in percent (days of operation divided by reporting time period multiplied by 100). If less than 80%, explain: \_\_\_\_\_

4. Average depth to groundwater: \_\_\_\_\_

B. EFFECTIVENESS EVALUATION:

1. Average contaminant removal rate for the entire system (pounds per day): \_\_\_\_\_

2. Average contaminant removal rate per well (pounds per day): \_\_\_\_\_

3. If the average contaminant removal rate is less than one pound per day for the entire system, or if the average contaminant removal rate per well is less than one tenth of a pound per day, evaluate the following:

a. If contaminants are aerobically biodegradable and confirmation borings have not been drilled in the past year:

i. Oxygen levels in extracted air (percent): \_\_\_\_\_

ii. Methane levels in extracted air (ppm,) If over 10 ppm,, explain: \_\_\_\_\_

iii. If methane is not present above 10 ppm, and if oxygen is greater than 20 percent in extracted air, you should either:

- Drill confirmation borings during the next reporting period, if the entire site should be considered for closure.
- Or, perform an in situ respirometry test in a zone of high contamination. Do not perform the test in an air extraction well, use a gas probe or water table well. If a zero order rate of decay based on oxygen depletion is less than 2 mg/kg per day, then you should drill confirmation borings, if the entire site should be considered for closure. If the rate of decay is between 2 and 10 mg/kg, operate for one more reporting period before evaluating further. If the zero order rate of decay is greater than 10 mg/kg total hydrocarbons, continue operating the system in a manner than maximizes aerobic biodegradation.

b. If contaminants are not aerobically biodegradable and confirmation borings have not been recently drilled during the past year, you should drill confirmation borings during the next reporting period if the entire site should be considered for closure.

c. If soil borings were drilled during the past year and soil contamination remains above acceptable levels, explain if the system effectiveness can be increased and/or if other options need to be considered to achieve cleanup criteria.

C. ADDITIONAL ATTACHMENTS: Attach the following to this form:

- Well and soil sample location map indicating all air extraction wells. If forced air injection wells are also in use, identify those wells.
- If water table monitoring wells are present at the site, a map of well locations.
- Time versus vapor phase contaminant concentration graph.
- Time versus cumulative contaminant removal graph.
- Groundwater elevations table, if water table wells are present at the site; also list screen lengths and elevations.
- Table of soil contaminant chemistry data.
- Soil gas data, if gas probes are used to monitor subsurface conditions in locations other than where air is extracted.
- System operational data table.

## APPENDIX F

---

Weekly Hexavalent Chromium Concentrations

Appendix F

WEEKLY INFLUENT HEXAVALENT CHROMIUM RESULTS  
 N.W. Mauthe Superfund Site - Appleton, Wisconsin  
 MCO. No. M050-90728.14

DATE	INFLUENT HEXAVALENT CHROMIUM* (ppm)
02/26/97	1.0
03/03/97	.8
03/06/97	1.0
03/10/97	1.5
03/23/97	.9
03/29/97	1.2
04/06/97	1.1
04/09/97	1.2
04/16/97	1.0
04/25/97	1.0
04/27/97	1.1
05/02/97	1.1
05/08/97	1.1
05/13/97	1.2
05/21/97	1.1
05/29/97	1.1
06/06/97	1.2
06/13/97	1.2
06/17/97	1.3
06/23/97	1.2
07/02/97	1.2
07/08/97	1.2
07/14/97	1.2
07/21/97	1.2
07/28/97	1.4
08/04/97	1.4
08/13/97	1.3
08/18/97	1.3
08/25/97	1.3
09/04/97	1.3
09/08/97	1.5
09/15/97	1.4
09/24/97	1.3
10/01/97	1.3
10/08/97	1.4
10/15/97	1.3
10/22/97	1.4
10/29/97	1.4
11/05/97	1.3
11/11/97	1.2
11/22/97	1.0
11/24/97	1.0
12/03/97	1.0
12/10/97	1.0
12/17/97	1.1
01/07/98	1.0
01/14/98	1.0
01/21/98	1.0

DATE	INFLUENT HEXAVALENT CHROMIUM* (ppm)
01/28/98	1.0
02/04/98	1.4
02/11/98	1.4
02/18/98	1.4
02/25/98	0.8
03/04/98	1.3
03/11/98	1.3
03/18/98	1.3
03/26/98	1.3
04/01/98	0.8
04/08/98	1.0
04/15/98	1.3
04/23/98	1.3
04/29/98	1.3
05/06/98	1.3
05/13/98	1.3
05/20/98	1.3
05/27/98	1.4
06/03/98	1.3
06/10/98	1.4
06/17/98	1.2
06/24/98	1.2
07/01/98	1.1
07/08/98	1.1
07/15/98	1.1
07/23/98	1.3
07/29/98	1.3
08/06/98	1.2
08/12/98	1.2
08/19/98	1.2
08/26/98	1.2
09/02/98	1.2
09/09/98	1.2
09/16/98	1.2
09/23/98	1.2
09/30/98	1.2
10/07/98	1.0
10/15/98	1.1
10/21/98	1.3
10/28/98	1.3
11/04/98	1.1
11/11/98	1.1
11/18/98	1.2
11/25/98	1.2
12/02/98	1.2
12/09/98	1.5
12/16/98	1.3
12/23/98	1.3

DATE	INFLUENT HEXAVALENT CHROMIUM* (ppm)
12/30/98	1.3
01/06/99	1.3
01/12/99	1.1
01/20/99	1.2
01/28/99	1.3
02/03/99	1.3
02/10/99	1.4
02/17/99	1.4
02/24/99	1.4
03/03/99	1.3
03/10/99	1.3
03/17/99	1.3
03/24/99	1.3
03/31/99	1.3
04/07/99	1.2
04/14/99	1.2
04/21/99	1.1
04/28/99	1.2
05/05/99	1.2
05/12/99	1.2
05/19/99	1.1
05/26/99	1.2
06/02/99	1.1
06/10/99	1.4
06/16/99	1.5
06/23/99	2.2
06/30/99	2.2
07/07/99	2.4
07/14/99	2.0
07/21/99	1.8
07/28/99	1.2
08/04/99	1.5
08/11/99	1.4
08/18/99	1.3
08/25/99	1.3
09/01/99	1.3
09/08/99	1.4
09/15/99	1.5
09/21/99	1.3
09/29/99	1.2
10/06/99	1.4
10/13/99	1.5
10/20/99	1.4
10/27/99	1.4
11/04/99	1.3
11/10/99	1.2
11/18/99	1.3
11/24/99	1.2

DATE	INFLUENT HEXAVALENT CHROMIUM* (ppm)
11/30/99	1.3
12/08/99	1.3
12/15/99	1.2
12/22/99	1.3
12/29/99	1.2
01/06/00	1.3
01/12/00	1.3
01/19/00	1.2
01/26/00	1.2
02/02/00	1.1
02/09/00	1.1
02/16/00	1.2
02/23/00	1.3
03/01/00	1.2
03/08/00	1.3
03/14/00	1.2
03/22/00	1.2
03/29/00	1.1
04/05/00	1.4
04/11/00	1.1
04/19/00	1.1
04/26/00	1.1
05/03/00	1.3
05/10/00	1.1
05/17/00	1.2
05/24/00	1.1
05/31/00	1.1
06/07/00	1.4
06/14/00	0.5
06/21/00	1.0
06/28/00	1.1
07/05/00	1.3
07/12/00	1.2
07/19/00	1.3
07/26/00	1.3
08/02/00	1.3
08/09/00	1.4
08/16/00	1.2
08/23/00	1.4
08/30/00	1.3
09/06/00	1.4
09/13/00	1.2
09/20/00	1.2
09/27/00	1.4

\*Hexavalent Chromium is Measured Utilizing a Hach Test Kit.
