


Tom Janisch-WR/2
FYI



THREE HAWTHORN PARKWAY, SUITE 400
VERNON HILLS, IL 60061-1450
708-918-4000 • FAX: 708-918-4055

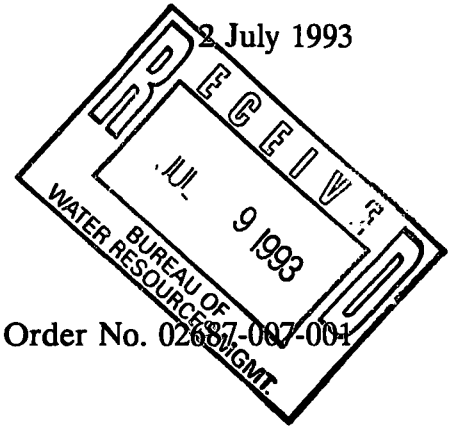

Ms. Bonnie L. Eleder
Remedial Project Manager (HSRW-6J)
U.S. Environmental Protection Agency
77 West Jackson Boulevard
Chicago, Illinois 60604

Work Order No. 02687-007-001

Re: Monthly Progress Report for June 1993
Moss-American Site, Milwaukee, Wisconsin

Dear Ms. Eleder:

Roy F. Weston, Inc. (WESTON®) has prepared this monthly progress report on behalf of the Settling Defendant for the Moss-American Superfund site, Kerr-McGee Chemical Corporation (KMCC). This monthly progress report has been prepared to document progress during June.

Progress During June 1993

The following summary of predesign task progress is presented for this reporting period:

- Predesign Task 9 - WESTON and KMCC have completed the evaluation of alternative alignments for the Little Menomonee River. WESTON is preparing the Draft Technical Memorandum to present the findings of this task. U.S. EPA approval of the Predesign Task 10 findings is required before the Technical Memorandum can be completed. On 22 June 1993, WESTON issued a letter to U.S. EPA requesting an expedited approval of the Task 10 Technical Memorandum.
- Predesign Task 16 - IT Corporation and Bergmann USA have completed the laboratory treatability subtasks of the bioslurry and soil washing technology evaluations. Laboratory data is currently being reduced and validated. Information is also being compiled in preparing the Draft Technical Memoranda to present the findings of these studies. WESTON and KMCC have requested a meeting with U.S. EPA during the week of 19 July 1993 to discuss the findings of the studies prior to completing the Draft Technical Memoranda.





Ms. Bonnie L. Eleder
U.S. EPA

-2-

7 June 1993

Problems Encountered/Issues To Be Resolved

As previously reported by KMCC and WESTON, denial of access to County of Milwaukee properties of the Moss-American site has resulted in cessation of Predesign Work (with the exception of limited tasks reported herein). During this reporting period, no further reports from U.S. EPA of the progress toward obtaining site access have been received.

Additional project task-related issues to be resolved, include:

- Predesign Task 16 - WESTON has identified certain Test Plan issues with the IT Corp. treatability study. WESTON and KMCC will present additional information on this issue during our meeting requested for the week of 19 July 1993.
- Predesign Task 10 - WESTON is awaiting final U.S. EPA approval/concurrence with the findings of Predesign Task 10 in order that the Predesign Task 9 Technical Memorandum can be completed.
- Predesign Phase Quality Assurance Project Plan (QAPP) - On 9 February 1993, WESTON transmitted responses to U.S.EPA review comments and document revisions to the Draft Predesign Phase QAPP. WESTON and KMCC are currently awaiting U.S. EPA review comments on this transmittal.
- Predesign Task 2 - On 15 March 1993, WESTON and KMCC transmitted the Technical Memorandum to U.S. EPA. WESTON and KMCC received WDNR review comments on 16 May 1993, however, we are currently awaiting U.S. EPA review comments on the Technical Memorandum.

Activities Anticipated During July 1993

KMCC and WESTON anticipate conducting the following predesign phase activities during July 1993:

- We anticipate conducting a task review meeting with U.S. EPA to discuss the initial findings of the Predesign Task 16 studies during the week of 19 July 1993.



Ms. Bonnie L. Eleder
U.S. EPA

-3-

7 June 1993

Should further clarification of this progress report be required, please contact the undersigned at (708) 918-4000.

Very truly yours,

ROY F. WESTON, INC.

A handwritten signature in black ink that reads "Gary J. Deigan".

Gary J. Deigan
Senior Project Manager

A handwritten signature in black ink that reads "Kurt S. Stimpson" with a circled "PK" to the right.

Kurt S. Stimpson
Project Director

GJD:KSS:llk
Attachment

cc: Mr. Mark Krippel, Project Manager
Kerr-McGee Chemical Corporation
798 Factory St.
P.O. Box 548
West Chicago, IL 60186

Mr. George B. Rice
Kerr-McGee Chemical Corporation
P.O. Box 25861
Oklahoma City, Oklahoma 73125

Mr. Richard Meserve
Covington & Burling
1201 Pennsylvania Avenue N.W.
P.O. Box 7566
Washington, D.C. 20044



Ms. Bonnie L. Eleder
U.S. EPA

-4-

7 June 1993

Regional Counsel (1 copy)
Attn: Moss-American Site Coordinator (5CS)
U.S. Environmental Protection Agency
77 West Jackson Boulevard
Chicago, IL 60604

Assistant Attorney General (1 copy)
Environment and Natural Resources Division
U.S. Department of Justice
P.O. Box 7611
Ben Franklin Station
Washington, D.C. 20044
Ref. D.J. #90-11-2-590

Section Chief (3 copies)
Environmental Response and Repair Section
Bureau of Solid and Hazardous Waste Management
Department of Natural Resources
101 S. Webster Street
P.O. Box 7921
Madison, WI 53707-7921

Mr. Jim Schmidt (2 copies)
Department of Natural Resources
Southeast District Office
P.O. Box 12436
Milwaukee, WI 53212
